

Works Access Permit

Registration Number: R1066208
Utility Reference: 2025 Generic Car Minor Excavation



1. Details of Proposed Work

Activity: Open Trenching, Pot Holing, Vehicle Crossing, Other (Specify Detail), Footpath / Kerb & Channel, Hand Digging
Address: 30 Laings Road, Lower Hutt Central, Lower Hutt, 5045
Location in road: Carriageway, Footpath, Berm, Nature Strip
WAP valid period: 01 January 2025 to 31 December 2025

2. The Parties

Hutt City Council being a body corporate in accordance with the Local Government Act 2002 ('the Corridor Manager;')
Wellington Water Alliance being an approved Utility Operator in accordance with Local Government Act 2002 submitting a request for access in accordance with that act;
Wellington Water Alliance being the agent of the Utility Operator submitting this request on behalf of the Utility Operator and in accordance with the Utility Operator's statutory rights ('the Applicant').

3. Attachments

Attachment 1 being the Schedule of Reasonable Conditions.
Attachment 2 being plan TMP showing the agreed service location.

4. Background

- (a) The Utility Operator wishes to carry out the works stated on CAR Number R1066208 and thereafter maintain the utility services established in the corridor;
- (b) The Corridor Manager is required to provide a written consent in accordance with its governing legislation and to provide a schedule of reasonable conditions, if required, by the utility legislation under which the request for access has been made; and
- (c) In accordance with the Code: Utilities' Access to the Transport Corridors and on behalf of the Corridor Manager, I give my written consent for access to the corridor at the agreed location and attach my schedule of reasonable conditions:
- (d) In the case of State highways this Works Access Permit serves as the approvals required under sections 51 and 78 of the Government Roothing Powers Act.

Signed



Date 15/11/2024

Josef Stains acting pursuant to delegated authority.

FOR Corridor Manager APPROVAL USE ONLY

Time Spent Processing:

<input type="checkbox"/>	Approved Contractor	<input type="checkbox"/>	Route Plan Submitted	<input checked="" type="checkbox"/>	TMP Submitted	<input type="checkbox"/>	Stockpiling Arrangements
--------------------------	---------------------	--------------------------	----------------------	-------------------------------------	---------------	--------------------------	--------------------------



CONDITIONS

Special Conditions

1. Conditions/TMP/Permit must be adhered too at all times, TMP,WAP and conditions are to be keep on site at all times via paper copies or downloaded to a site tablet. Failure to do so may result in a NCN or a stop work notice being issued.
2. Excavations in carriageways - Footpath and Berm.
 1. All excavations are to be backfilled and AC sealed at the end of each shift
 - 2.Compaction test results are to be uploaded into CAR Manager for all excavation work in carriageways, footpath and berms.
 3. Photos prior to backfill of excavation in carriageways to be uploaded into the CAR showing the 150mm trimming allowance on either side of the excavation.
 4. Hot poured rubber bitumen bandage must be applied where excavations are carried out within the carriageway.
The width of the sealing shoe is to be at least 60mm wide. Once the hot poured rubber bitumen bandage has been applied to the joint/s, an emulsion and grit (or sand seal) is to be placed over the bandage.
The surface joints must be clean and dry before applying the hot poured rubber bitumen.
 5. All time extensions must be approved by the Corridor Manager.
 - 6. Site Photos: ensure that photos are uploaded the CAR, showing the physical works, site setup, and when works are completed (give a reference in the photo i.e. Address - letter box) also required for completion sign off**
 7. Any Small excavations, must reinstated to the 1m rule, this applies for AC and Concrete, any cracks or divots to be captured in the reinstatement.
 8. Only the work stated in the approved TMP, can be completed with the TMP
 9. Steel Plates are not approved to be used on this site(unless prior approval is given by the Operation corridor manager)
 10. Micro Slot trenching is not approved to be used on the HCC network (Carriage way and footpath. micro slot trench is a trench that is 100mm or less in width.)
 11. Ensure there is an adequate surface for pedestrians being diverted onto grass berms
 12. if temp seal has been approved for this work, it is to include a top layer of coldmix AC and be monitored daily.
 13. all reinstatement is to be done to HCC standards, all remedials are to be completed as soon as possible, if not the same day
 14. Any pedestrians being diverted on to the berm, the berm must have a non slip surface or the berm must be suitable and not boggy/muddy
 15. Yellow plastic plates are to used in con-junction with fencing to cover any small excavations on the berm or footpaths
 16. if trenching is required through a driveway, please contact HCC to discuss (kara.collins@huttcity.govt.nz)
3. This Corridor Access Request (CAR) is approved in order for the Utility to have a set of Generic Traffic Management Plan's available for use with an excavation CAR. In all cases a separate CAR is required for excavation work.
4. Clash of works check, please ensure to check for clashes on the planning map and contact the other party to ensure you can have access to the site, if not, please plan the works to suit the allowed date/s.
5. **The cover sheet uploaded to the CAR forms part of the approved CAR application and associated TMP, and the comments from the TMC/Delegated authority must be reviewed and incorporated into the approved TMP.**

General Conditions


6. The Utility Operator must:

CAR Number: R1066208



- (a) carry out all Work in Transport Corridors in accordance with the Code and KiwiRail's Specifications for Working in Railway Corridors;
- (b) undertake all Works in compliance with the Acts of Parliament and mandated codes of practice that relate to their industry and the type of Work described within the plans and methodology submitted;
- (c) install assets more or less in the location shown on the attached plans, and agree the exact location and position with the Road Corridor Manager before Work commences;
- (d) locate any Utility Structures in the Road Corridor in the agreed position shown on the drawings and clear of the Carriageway, Road Corridor furniture and kerbs, drains, manholes, etc. Utility Structures agreed to be within the trafficable part of the Road are to be flush with the surface and designed to withstand full heavy Traffic loading (NZTA's HN-HO-72 Traffic Loading);
- (e) provide a full description of the construction methodology, reinstatement, resurfacing and compaction and agree this with the Road Corridor Manager prior to Work commencing;
- (f) make the Works available at all times for inspection by any person representing the Road Corridor Manager;
- (g) if requested, pay the reasonable costs of the Road Corridor Manager in connection with the processing of this notice and for the monitoring and auditing of the Works; (See NZ Transport Agency Cost Structure under Clause 23)
- (h) keep a full copy of the Works Access Permit/ Permit to Enter and Reasonable Conditions on the Work Site at all times during the Works;
- (i) undertake remedial action on non-conforming Work within the timeframe set by the Road Corridor Manager, where reasonable and practicable;
- (j) gain all the necessary consents, approvals and permits from the relevant statutory and regulatory authorities at its own cost;
- (k) keep plans of the installed Work and make them available to the Railway Corridor Manager (in all cases) and Road Corridor Manager (on request);
- (l) compensate the Road Corridor Manager for any damage or costs incurred to the Road Corridor due to the Work or for costs resulting from the removal of abandoned installations, Utility Structures, components and equipment that belong to the Utility Operator;
- (m) repair all Road Corridor assets damaged as a result of the Works, should the Road Corridor Manager determine these are necessary prior to the end of the Warranty period;
- (n) restore to their original condition any surface or Utility Structure that was damaged or removed as a result of the Works;
- (o) control the surface water channels so as to cause minimal interference to existing flows;
- (p) fully restore the surface water channels at the completion of the Works;
- (q) notify the Road Corridor Manager of any maintenance Work it proposes to undertake within the two-year Warranty period;
- (r) have in place an approved TMP for Roads and Motorways at least two days prior to Work commencing on the Work Site;
- (s) provide the Road Corridor Manager with two Working Days' notice before commencement of Work on the Work Site;

CAR Number: R1066208



(t) ensure that the Work is carried out under the control of a warranted supervisor as required by the Code of Practice for Temporary Traffic Management and ensure that there are sufficient people on site specifically to control the flow of Traffic through the site in accordance with the TMP;

(u) comply with instructions from an officer of the NZ Police Traffic Safety Branch or a duly authorised agent of the Road Corridor Manager in respect of Traffic management and safety;

(v) complete Works in the Road Corridor in one continuous operation (suspension of Works over five continuous days requires the prior written permission of the Road Corridor Manager);

(w) protect and maintain all Road Corridor signs, markers, signals, barriers and associated marking and replace them to the appropriate industry standard where they have been damaged by the Works;

(x) complete and submit a Works Completion Notice form when the Works are complete; and

(y) stop Work as necessary to meet the requirements of section 42 of the Heritage New Zealand Pouhere Taonga Act 2014.

7. Work must not take place on or near a State highway during and one day either side of a public holiday or public holiday weekend.
8. Where otherwise required due to Traffic volumes or specific residential or Central Business District requirements, the hours of Work must be as specified in the Local Conditions and Special Conditions.
9. The Warranty period starts from the date the Road Corridor Manager has given signed acceptance that the Work is complete or otherwise as provided in Section 4.7.1.7 of the Code.
10. Unless the Works stated in the WAP have started on the Work Site, the agreement relating to the Works will only remain valid for six months from the date of approval on the Works Access Permit.
11. The Road Corridor Manager must manage all applications relating to Road Corridor access in accordance with the timeframes and processes in the Code.
12. The Corridor Manager may:
 - (a) assess the suitability of any action proposed by the Utility Operator during the Warranty period and impose Reasonable Conditions that will maintain the integrity of the Road assets;
 - (b) arrange for remedial Work to be done and recover the costs incurred from the Utility Operator, if the Utility Operator fails to take action within the agreed timeframe; and
 - (c) instruct the Utility Operator to stop Work and leave the Work Site (having made the site safe) if the Works are not complying with the relevant Reasonable Conditions including any plans, relevant conditions or specifications contained in the Code, or permission requirements.
13. In granting this WAP, no vested right is created.
14. This WAP is not transferable without the written permission of the Road Corridor Manager.

Local Conditions

CAR Number: R1066208



CAR HCC Full Scope of Works Utility
Utility

Company	Wellington Water
Contract Manager	Bob Wilson
Phone	027 3355 334
Email	Bob.Wilson@wellingtonwater.co.nz

Contractor

Company	Wellington Water alliance
Contract Manager	Bob Wilson
Phone	027 3355 334
Email	Bob.Wilson@wellingtonwater.co.nz

Type of Work (Tick)					Minor	x
Location Road (Tick)	Carriageway	x	Footpath	x	Berm	x

Work Location

Physical Address	Various Locations / Streets within Hutt City Region
------------------	---

Work Programme

Start Date	01/01/2025	Completion Date	31/12/2025
Duration of Work	24/7	Day / Night	365

Hours of work

Start Time		Finish Time	
------------	--	-------------	--

Description of Activity

P3/P4 Minor excavation works including reinstatement not needing site specific:

- All work carried out may involve having 1 to 2man onsite including sub-contractors.
- All digging works can involve but not limited to hand digging or using a digger / hydro vac when required.
- Any works that are not reinstated will follow the reinstatement requirements.

ALL ROAD CLOSURES MUST HAVE RCA / TMC APPROVAL

All night works must have Noise Control Approval before the work can start.

6:00pm – 7:30am Mon-Sat, All time Sunday & Public Holidays

Note: All project works, or other work not covered under the Generic Tmp / Tmd will need site specific.

Confirmation is required from RCA to see if Generic covers main arterial roads or suburban shopping areas, Site Specific TMP maybe required.

Only approved contractors listed on Tmp are covered under Generic Car.

ALL CONTRACTORS ARE TO NOTIFY THE RCA PRIOR TO CARRY OUT THEIR WORK ACTIVITY.

Weekend or afterhour works:

All weekend (Sat-Sun) or afterhours (6pm – 7am) work requires a child CAR to be raised in advance.

Repairs:

- Leaks – 3 Water network leaks which covers repairs / replacement of council assets.
- Repair / replacement of Tobies / meters / hydrants / valves /potable services / mains that can be repaired on the same day.
- Locating or exposing buried tobies / lids / manholes.

- Repair / Replace Manhole frame and centres.
- Repair / Replace Stormwater and Wastewater laterals.
- Pothole to avoid damage to buried utility lines.

Crews and Sub contractors must adhere to the following:

- Ensure proper traffic and pedestrian management is in place.
- Set up correct Tmd to suit the work site.
- Complete a separate RCP form for every excavation.
- Safety induction is carried out as per RCP process.
- Ensure safety is always adhered to.
- Ensure all efforts are made to minimise disruption to residents, business, and pedestrians.
- Make sure relevant documents are onsite (utility plans).
- Mark out utility / council assets to carry out work above.
- Provide before photos showing a wide street view of location.
- Photo of repairs.
- Photo after the repair and how the site was left.
- Clear notes of what was repaired.
- Where possible reinstatement will be completed after excavation.
- Site is packed up and left clean and tidy.

Work Vehicles onsite at various stages of work but not limited to:

Standard work crew:

1 to 2 service vehicles equipped with beacons onsite along with any small plant and equipment to carry out maintenance work. Crews to set up own Tmd.

Service crews are equipped to set up the following Tmd's only.

Traffic management will be required if you do not carry correct signage.

CC1	F2.1
CC2	F2.2
CC3	F2.5
CC4	F2.6
CC5	F2.7
CC7	J2.16A
CC8	
CC9	
CC12	

Sub-contractors are to follow the Tmd criteria above, or if you do not have correct signage to set up own Tmd. Any Tmd not listed above will require external traffic management.

Extended crew when needed:

- Hydro Vac Truck / Digger / Jet Flusher / Mini combo maybe utilised to assist with repairing leaks.
- Traffic management vehicles if unable to set up own traffic.
- Reinstatement vehicles / plant where possible.

Reinstatement:

Note: all work not covered under the Generic Tmp / Tmd will need site specific.

Confirmation is required from RCA to see if Generic covers main arterial roads or suburban shopping areas, Site TMP maybe required.

- Reinstatement must be completed as per National code requirements.
- Photo of site upon arrival showing wide-street view.
- Photo of preparation/boxing, emulsion & final reinstatement.
- Compaction test must be supplied as per National code requirements.
- Photo of wide view shot of person holding clegg machine.
- Photo of each compaction test taken must be supplied showing close-up digital results.
- If work is postponed or cancelled; works will go ahead the next safe and practical date possible weather permitting.
- Uneven surface and speed restriction signage will need to be installed and the site will need to be monitored once within each 24-hour period and recorded on the site record and monitoring form.
- Sites left unattended must be fenced off as per National code requirements.
- Photo of site left unattended upon first establishing protective fencing.
- If for any reason a site has not been temp sealed, we must advise the Corridor Manager ASAP.
- **Temporary surface must be installed within one working day and full reinstatement to be completed as soon as possible weather permitting.**

Work Vehicles onsite at various stages of work but not limited to:

- 1 to 2 service vehicles equipped with beacons onsite along with any small plant and equipment to complete the work.
- Concrete truck / Hot Box Truck along with any small plant and equipment to complete the work.
- Digger / Roller.
- Tipper Truck.
- Traffic management vehicles if unable to set up own traffic.

WHEN ARE SITE SPECIFIC TMP'S NEEDED:

Site Specific TMP required depending on the work activities and impact. Works include:

- **Entry to access Three Water Assets located at a major intersection, or within a live lane that will impact traffic flow.**
- **Burst water main / water leaks in the carriageway / intersections that will impact traffic.**
- **Hydrant / valve replacements in the carriageway that will impact traffic.**
- **Water / wastewater lateral replacements that involve trenching across the carriageway.**
- **All works within KiwiRail property, prior approval is required.**
- **Road closures.**

Health and Safety Policy



Our Purpose |

Creating excellence in regional water services for healthy communities

Our Vision

Our people, suppliers and affected parties go home healthy and safe

Our Beliefs

- Health and safety is our top priority
- We look after ourselves; everyone takes personal responsibility for their own health and safety
- We look out for each other, suppliers and the public; we make sure everyone is safe
- Wellington Water takes a methodical approach to health and safety; we continuously review our systems to ensure they are up-to-date and ensure that health and safety is foremost in infrastructure planning and design
- We're committed to health and safety at all times; nobody walks past an unsafe activity or work site - we make it safe

Our Commitments

Leadership

- We make sure our people work in a safe environment
- We make sure our work sites are safe for suppliers, neighbours and the general public
- We empower our people to manage health and safety in all situations and to stop unsafe acts as they happen; we make sure there's a safe working environment before work continues
- We proactively identify and manage hazards and ensure safe behaviour
- We support the safe and early return to work of any of our people who are injured or sick, and support and follow up on anyone who is injured on a Wellington Water site
- We recognise staff and suppliers who practice excellence in health and safety

Systems

- We make sure our people have the training, skills and resources to work safely
- We ensure infrastructure managed by Wellington Water is designed, constructed, operated and maintained safely, and will remain safe for our people, suppliers and the community
- We accurately record, investigate and report incidents and learn from them
- We monitor our health and safety performance and that of our suppliers as a basis for continuous improvement and identifying new and safer ways of working

Working with others

- Our suppliers are required to commit to our vision of our people and suppliers going home healthy and safe
- We make sure all suppliers working on behalf of Wellington Water have high quality health and safety systems in place
- We comply with and exceed all relevant legislation, regulations, codes of practice and industry standards
- We interpret health and safety broadly and work with all stakeholders to achieve our health and safety vision

A handwritten signature in black ink, appearing to read 'Colin Crampton'.

COLIN CRAMPTON
CHIEF EXECUTIVE



Living Safely Policy

People at the heart of everything we do

Living safely is how we go about every aspect of our lives; all day, every day. It is more than work, it is about integrating our work, home and interests, our desire to get the best out of life, and to be the best we can. It is recognising our strengths and weaknesses, and making positive choices that benefit our wellbeing and way of life, including those of others in the communities in which we live and work.

We will:

- Demonstrate our commitment through active and visible leadership
- Abide by a simple safety management system that encourages health and safety ownership by each and every individual
- Incorporate health and safety into the way we design, plan and do our work
- Work collaboratively with our subcontractors to meet the required health and safety standards
- Enhance our health and safety skills and behaviours through training and development
- Foster a culture of reporting, learning and sharing
- Be empowered to maintain a safe and healthy workplace
- Promote a positive health and wellbeing mindset
- Meet or exceed relevant standards and legal requirements
- Set measurable objectives and targets to ensure continual improvement

C W Bruyn
Managing Director

ROAD SPACE BOOKING

Address:				
Contractor:				
Dates & Times (attended):	From:		To:	
Dates & Times (unattended):	From:		To:	
Generic TMP used:				
Diagram (s) used:				
CAR #				
Work Activity and Reasons TTM to remain in place:				
Contractor Name:				
Contractors Signature:				
TMC Approval:				

Please attach photos of site active site set up (these photos are to include both ends of the site (inclusive of any side roads), pedestrian/cycle management and the working area.

Notes to the applicant / contractor (of working space) / contractor or delegated authority (of TTM)

CAR reference number: R1066208

Approved TMP reference number: ATMS 2024-372

This TMP is approved with the following conditions / comments:

1. In addition to Environmental Health approval - environmental.health@huttcity.govt.nz - Friday and Saturday night works requires prior approval from the Corridor Manager
2. In addition to the above prior approval is required from the Corridor Manager for:
 - Saturday and Sunday day works
 - Working on public holidays
 - Working during the Christmas moratorium period
 - No works between Central Business District (CBD) and retail zones between 6 December 2024 to 6 January 2025
 - No works outside the CBD and retail zones between 20 December 2024 to 6 January 2025
3. Additional for stop/stop and stop/go closures – to prevent any road user conflict all approaches should be on stop to allow for safe driveway access control
4. Escorting pedestrians through the site – this may require work activities to be halted
5. Diagrams:
 - Use of F2.4 if approved by the TMC will require the installation of a temporary speed limit for both attended and unattended
 - CC4 – refer to F2.3 for minimum pedestrian diversion requirements i.e. 1.2m path + 1m lateral safety zone
 - Any cone mounted RD6L or R signs are to be twin disc as opposed to single disc
 - F2.24, F2.25 and ATMS08 are NOT approved as part of this application
 - ATMS02 – if required when unattended prior approval from the TMC is required
6. Proposed TSLs would include the following as additional diagram references:
 - F2.4 for attended and unattended
 - F2.21 for unattended
7. A notification letter template is to be uploaded to the parent CAR prior to the start date of this GTMP
8. TTM contractor interim contacts
 - Men At Work – Todd Lynch is no longer with Men At Work
 - Traffic Management NZ – Steven Loftus was recently with another contractor, alternative TMNZ contacts are either Stephen Morgan 021 400 023 or Barney Miller 021 986 014



Jason Wildman

Traffic Management Coordinator

14 November 2024



TRAFFIC MANAGEMENT PLAN (TMP) – FULL FORM

Use this form for complex activities. Refer to the NZ Transport **Agency's** Traffic control devices manual, part 8 Code of practice for temporary traffic management (CoPTTM), section E, appendix A for a guide on how to complete each field.

Organisations /TMP reference	TMP reference: ATMS 2024-372	Contractor (Working space): As per attached list	Principal (Client): Wellington Water		
		Contractor (TTM): As per attached list	RCA: Hutt City Council		
Location details and road characteristics	Road names and Suburb		House no./RPs From and to	Road level	Speed Limit
	Various within the Hutt City Region		Various	01	30/40/50/60 /70/80km/h
Traffic details (main route)	AADT	Peak flows			
	Various	AM	Start 5:30am	End 9:00am	
		PM	4:00pm	7:00pm	

Description of work activity

P3/P4 Minor excavation works including reinstatement not needing site specific:

- All work carried out may involve having 1 to 2man onsite including sub-contractors.
- All digging works can involve but not limited to hand digging or using a digger / hydro vac when required.
- Any works that are not reinstated will follow the reinstatement requirements.

ALL ROAD CLOSURES MUST HAVE RCA / TMC APPROVAL

All night works must have Noise Control Approval before the work can start.
6:00pm – 7:30am Mon-Sat, All time Sunday & Public Holidays

Note: All project works, or other work not covered under the Generic Tmp / Tmd will need site specific.

Confirmation is required from RCA to see if Generic covers main arterial roads or suburban shopping areas. Site Specific TMP maybe required.

Only approved contractors listed on Tmp are covered under Generic Car.

ALL CONTRACTORS ARE TO NOTIFY THE RCA PRIOR TO CARRY OUT THEIR WORK ACTIVITY.

Weekend or afterhour works:

All weekend (Sat-Sun) or afterhours (6pm – 7am) work requires a child CAR to be raised in advance.

Repairs:

- Leaks – 3 Water network leaks which covers repairs / replacement of council assets.
- Repair / replacement of Tobies / meters / hydrants / valves /potable services / mains that can be repaired on the same day.
- Locating or exposing buried tobies / lids / manholes
- Repair / Replace Manhole frame and centres
- Repair / Replace Stormwater and Wastewater laterals

APPROVED
CAR R1066208
Celine Wildman
STMS Hutt City 307 43
14 November 2024

- Pothole to avoid damage to buried utility lines.

Crews and Sub contractors must adhere to the following:

- Ensure proper traffic and pedestrian management is in place.
- Set up correct Tmd to suit the work site.
- Complete a separate RCP form for every excavation.
- Safety induction is carried out as per RCP process.
- Ensure safety is always adhered to.
- Ensure all efforts are made to minimise disruption to residents, business, and pedestrians.
- Make sure relevant documents are onsite (utility plans).
- Mark out utility / council assets to carry out work above.
- Provide before photos showing a wide street view of location.
- Photo of repairs.
- Photo after the repair and how the site was left.
- Clear notes of what was repaired.
- Where possible reinstatement will be completed after excavation.
- Site is packed up and left clean and tidy.

Work Vehicles onsite at various stages of work but not limited to:

Standard work crew:

1 to 2 service vehicles equipped with beacons onsite along with any small plant and equipment to carry out maintenance work. Crews to set up own Tmd.

Service crews are equipped to set up the following **Tmd's** only.

Traffic management will be required if you do not carry correct signage.

CC1	F2.1
CC2	F2.2
CC3	F2.5
CC4	F2.6
CC5	F2.7
CC7	J2.16A
CC8	
CC9	
CC12	

Sub-contractors are to follow the Tmd criteria above, or if you do not have correct signage to set up own Tmd. Any Tmd not listed above will require external traffic management.

Extended crew when needed:

- Hydro Vac Truck / Digger / Jet Flusher / Mini combo maybe utilised to assist with repairing leaks.
- Traffic management vehicles if unable to set up own traffic.
- Reinstatement vehicles / plant where possible.

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307.43

Hutt City Council

Page 2

14 November 2024



APPROVED

CAR R1066208
Jason Wildman
STMS Number 307.43

Hutt City Council

14 November 2024

Reinstatement:

Note: all work not covered under the Generic Tmp / Tmd will need site specific.

Confirmation is required from RCA to see if Generic covers main arterial roads or suburban shopping areas. Site TMP maybe required.

- Reinstatement must be completed as per National code requirements.
- Photo of site upon arrival showing wide-street view.
- Photo of preparation/boxing, emulsion & final reinstatement.
- Compaction test must be supplied as per National code requirements.
- Photo of wide view shot of person holding clegg machine.
- Photo of each compaction test taken must be supplied showing close-up digital results.
- If work is postponed or cancelled; works will go ahead the next safe and practical date possible weather permitting.
- Uneven surface and speed restriction signage will need to be installed and the site will need to be monitored once within each 24-hour period and recorded on the site record and monitoring form.
- Sites left unattended must be fenced off as per National code requirements.
- Photo of site left unattended upon first establishing protective fencing.
- If for any reason a site has not been temp sealed, we must advise the Corridor Manager ASAP.
- Temporary surface must be installed within one working day and full reinstatement to be completed as soon as possible weather permitting.

Work Vehicles onsite at various stages of work but not limited to:

- 1 to 2 service vehicles equipped with beacons onsite along with any small plant and equipment to complete the work.
- Concrete truck / Hot Box Truck along with any small plant and equipment to complete the work.
- Digger / Roller.
- Tipper Truck.
- Traffic management vehicles if unable to set up own traffic.

WHEN ARE SITE SPECIFIC TMP'S NEEDED:

Site Specific TMP required depending on the work activities and impact. Works include:

- Entry to access Three Water Assets located at a major intersection, or within a live lane that will impact traffic flow.
- Burst water main / water leaks in the carriageway / intersections that will impact traffic.
- Hydrant / valve replacements in the carriageway that will impact traffic.
- Water / wastewater lateral replacements that involve trenching across the carriageway.
- All works within State Highways.
- All works within KiwiRail property, prior approval is required.
- All works that impact bus stops, including relocation, will need a site TMP.
- All works that impact a school during school hours.
- Road closures.
- This also includes works that may have an impact on traffic and project work taking more than 1 day.

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307.43

Hutt City Council

14 November 2024

Planned work programme

Start date	01/01/2025	Time	See Below	End date	31/12/2025	Time	See Below
Consider significant stages, for example:	<p>Residential Roads</p> <p>Installation: 7:00am – 7:30am or whenever site is installed.</p> <p>Site Active: 7:30am – 17:30pm</p> <p>Site Removal: 17:30pm – 18:00pm</p> <p>NIGHTWORKS ARE NOT PERMITTED IN RESIDENTIAL AREAS</p> <p>Main Road</p> <p>Installation: 9:00am -9:30am or whenever site is installed</p> <p>Site Active: 9:30am – 15:30pm</p> <p>Site Removal: 15:30pm – 16:00pm</p> <p>Installation: 19:00pm – 19:30pm or whenever site is installed</p> <p>Site Active: 19:30pm – 5:00am</p> <p>Site Removal: 5:00am – 5:30am</p> <p>Works near schools</p> <p>No work to be completed between school drop off & pick up times: Between 8.30am – 9.30am & 2.30pm – 3.30pm</p> <p>Only approved contractors listed on Tmp are covered under Generic Car.</p> <p>This TMP is to cover 1 day attended minor excavation works – a Road Space Booking (attached), CAR and email notification to the TMC & Corridor access manager will be required for any works required to be left unattended.</p> <p>Road Space Booking MUST include:</p> <ul style="list-style-type: none"> • Location/Address • Dates/Times of works – attended & unattended • TMP & Diagram(s) used • Reasons for works/TTM remaining in place, longer than 1 day • Photos of the active site set up (these photos are to include both ends of the site (inclusive of any side roads), pedestrian/cycle management and the working area. <p>A site specific TMP is required for/when:</p> <ul style="list-style-type: none"> • The generic TMD does not suit/fit the site • A road closure or one way system (partial road closure) • Removal of mobility parking • Bus lane only closed (Petone Esplanade) • Roads of Significance (refer attached list, map) <p>Use of Traffic Signals (F2.17) & F2.4 must be approved by TMC prior to leaving on an unattended site. F2.16 requires TMC approval prior to installing on both attended and unattended sites.</p> <p>e-STOPS – ATMS 02, ATMS 03 & ATMS 05 are not permitted for use whilst site is unattended – e-STOPS must be manned at all times. e-Stops are a remote control MANUAL operated system so cannot physically operate when unattended.</p> <p>Any changes to the approved TMP must be documented on the Onsite Record.</p>						

CAR R1066208
Jason Wildman
STMS Number 307.43

Hutt City Council

14 November 2024

Parking Restrictions:

Parking restrictions will be installed where required 12-24hrs prior to works commencing. Parking restriction signage is to show actual work times and dates.

INFORMATION ONLY: vehicles may require towing.

Police and Council (570 6666) are to be provided the license plate number of any towed vehicle to be contacted prior to contacting tow company: 04 570 6666 | 0800 HUTT CITY. Supreme Towing: 0800 129 029.

All related towing fees will be directed to the contractor. Towing authority is not approved as part of the TMP process. HCC including parking enforcement do not approve or take responsibility for any organising and towing of vehicles.

Kerb Side Collection:

Kerb side collection occurs Monday to Friday. Refer to the attached kerb side collection schedule. Works to halt when kerb side collection vehicle is working in the area or onsite personnel to assist with the collection.

See <https://www.toogoodtowaste.co.nz/> if unsure of collection day (QR code below)




- A risk assessment is to be applied prior to selecting/installing TMDs.
- Checking-process-for-GTMPs checklist form (attached) is to be completed prior to using the GTMP.

Reinstatement:

- Wellington Water is responsible for managing the aftercare for all temporary surface – contact 04 912 470 or email: landaccess@wellingtonwater.co.nz.
- Reinstatement must be completed as per National code requirements.
- Compaction test must be supplied as per National code requirements.
- If work is postponed or cancelled; works will go ahead the next safe and practical date possible weather permitting.
- Sites left unattended need to be monitored once within each 24-hour period and recorded on the site record and monitoring form.
- Sites left unattended must be fenced off as per National code requirements.
- Reinstatement is to be planned same day or as soon as practicably possible. Pedestrian management (remaining on the path/berm) and shoulder closures can remain in place with fencing. Any works requiring pedestrian diversion onto the road or larger than a Shoulder Closure must be backfilled to road level with aftercare left in place or temporary sealed.

Work Vehicles onsite at various stages of work but not limited to:

- 1 to 2 service vehicles equipped with beacons onsite along with any small plant and equipment to complete the work.
- Concrete truck / Hot Box Truck along with any small plant and equipment to complete the work.
- Digger / Roller.
- Traffic management if unable to set up own traffic.



- Reinstatement vehicles / plant.

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307.43

Hutt City Council



14 November 2024

Inspection activities must be completed as detailed in the approved TMP.			
Type of road	On shoulder or roadside – no time limit	On live lane – up to 5 minutes	Over 5 minutes
Low volume (less than 500vpd) category A or B road environment	Spotter optional – can be one person activity Onsite control must be by either a practising STMS of any category, a practising TMO or an Inspector <i>and in the interim until the warrants are phased out, an STMS of any level or a TC-Inspector.</i>		Inspection not permitted. Must use a mobile, semi-static, or static closure.
Category A	Spotter optional – can be one person activity	Spotter required – minimum two person activity	
	Onsite control must be by either practising STMS of any category, practising TMO or Inspector <i>(and in the interim until the warrants are phased out):</i>		
	Road level	Onsite control	
	Level 1 road	TC, TC-Inspector or STMS	
	Level 2 road	L2/3 STMS, STMS-NP, or TC-Inspector	
Category B	Spotter optional – can be one person activity	Spotter required – minimum two person activity	
	Onsite control must be by either a practising STMS of any category, a practising TMO or an Inspector <i>and in the interim until the warrants are phased out:</i>		
	Road level	Onsite control	
	Level 1 road	TC, TC-Inspector or STMS	
	Level 2 road (shoulder, roadside or on the lane with speed 60km/h or less)	L2/3 STMS, STMS-NP or TC-Inspector	
	Level 2 road (on the lane with speed 70km/h or more)	L2/3 STMS or STMS-NP	
Category C	Spotter optional – can be one person activity: Onsite control must be by either a practising STMS (C) or an Inspector <i>(and in the interim until the warrants are phased out, a L2/3 STMS, STMS-NP, or TC-Inspector).</i>	Inspection not permitted. Must use a mobile, semi-static, or static closure.	

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307.43

Hutt City Council

Page 8

14 November 2024

	<p>General rules (apply to all the above)</p> <p>Inspectors must move to avoid traffic. They must not expect traffic to move or slow down to avoid them.</p> <p>There must be CSD to the Inspector when on the live lane.</p> <p>On busy roads where traffic volumes and speed affect access to the live lane, peak periods should be avoided or a higher level of TTM considered.</p> <p>Crossing a level LV, 1 or 2 road does not constitute being on a live lane but crossing a level 3 road does, unless a pedestrian crossing facility is being used.</p> <p>Vehicle</p> <p>Advance warning in the form of an inspection vehicle fitted with one and preferably two amber flashing beacons and a rear-mounted sign indicating the type of activity taking place must be positioned in advance of the inspection site.</p> <p>A vehicle is not required on a level LV or level 1 road with a permanent speed of less than 65km/h if the Inspector remains on a footpath.</p> <p>On roads with a permanent speed of less than 65km/h an amber flashing beacon is not required on the vehicle if the Inspector or non-invasive works is on an unsealed shoulder (or further away from the carriageway - including a footpath).</p> <p>Spotter</p> <p>A spotter is not required for inspections and non-invasive works on level LV roads.</p> <p>Unless otherwise approved by the RCA, all inspections on the live lane of level 1 and level 2 roads require a spotter. The RCA may provide a list of level 1 roads, times and/or activities suitable for inspection by a single inspector (eg where no level LV roads have been declared by the RCA)</p> <p>Where an unaccompanied Inspector is not able to maintain adequate attention (eg due to work tasks or poor visibility), a spotter will be required or another type of traffic management operation used.</p>
Alternative dates if activity delayed	N/A – works will be carried out within the times/dates as listed.

Road aspects affected (*delete either Yes or No to show which aspects are affected*)

Pedestrians affected?	Potentially	Property access affected?	Potentially	Traffic lanes affected?	Potentially
Cyclists affected?	Potentially	Restricted parking affected?	Potentially	Delays or queuing likely?	Potentially

Proposed traffic management methods

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307.43

Hutt City Council

Jason Wildman
14 November 2024

Installation
(includes parking of
plant and materials
storage)

- STMS to contact Metlink (0800 801 700) for any works including installing a TSL on a bus route or impacting bus stops 30mins prior to installation.
- STMS to contact WTOC (0800 869 286) for any works affecting or close to traffic signals 30 mins prior to installation.

Once on site, the TMP will be implemented as follows:

- Identify public safety and site safety hazards and how they will be addressed and place on the hazard document for **'toolbox'** briefing
- STMS to check the TMP is appropriate to the worksite.
- All vehicles are to have correct signage and flashing beacons. They also need to have continuous and appropriate communication with the STMS and each other on an agreed channel at all times
- Work vehicles required on site will be parked within the site or parked legally nearby.
- Mobile Operations or inspection activities may be required to turn on/off water valves.

Layout Procedure

Installation of the site will be done under a level 1 mobile closure with appropriate work vehicles and crew.

- A site drive through will be conducted first to confirm layout, conditions and environment are all appropriate for works to proceed.
- Vehicle positioning will be as far to the left as practical and the installation vehicle will be stationary at the installation of each sign, with activity occurring only on the non-traffic side of the vehicle.
- Advanced warning signage will be installed first on the left, followed by progressive signage installation in a **'loop'** fashion around the site area.
- Once ALL signage for the site has been installed delineation and direction signage will be installed in the following order;

- Longitudinal Delineation (Along the lane)
- Tapers (Shifting) & RD6 signage
- Tapers (Merging) & RD6 signage

Once all delineation is installed and prior to personnel, vehicle, plant and machinery populating the worksite, a drive through check must be performed by the STMS to ensure the site has been set up as per the selected TMDs, this should include the checking of worksite layout distances.

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307.43

Hutt City Council

Jason Wildman

14 November 2024

<p>Attended (day)</p>	<ul style="list-style-type: none"> • An STMS or delegated TMO must be onsite at all times. • TM-W/ TMO /STMS to assist pedestrians/cyclists/driveways and any resident/business driveways. • For Stop/Stop and Stop/Go setups, cyclists will be sent prior to any vehicles. • STMS/TMO will complete 2 hourly site checks and document on the onsite record. • Where Mobility Parking is affected alternative to be provided (same side of road, as close as possible), TM personnel to assist and guide users as required <p>Works near Signals:</p> <ul style="list-style-type: none"> • Any affected signal loops must be notified to WTOC during the pre-installation call to allow them to adjust signal management. <p>Works near Pedestrian Crossings:</p> <ul style="list-style-type: none"> • MTC's to guide pedestrians through/around the closure. <p>Works near a Bus Stop:</p> <p>Bus stop integrated into MTC Stop Point</p> <ul style="list-style-type: none"> • MTC's on stop/go are to stop each bus and assist with loading & unloading of passengers as required. • Bus stop signage is to direct pedestrians towards the stop point <p>Bus stop relocated away from site</p> <ul style="list-style-type: none"> • Bus stop signage is be placed to show patrons where the relocation is. • TM personnel to assist and guide bus patrons as required • Temporary bus stop signage is to be used • Parking restrictions are to be in place at the relocated bus stop <p>Works near a School:</p> <p>No work to be completed between school drop off & pick up times:</p> <p>Between 8.30am – 9.30am & 2.30pm – 3.30pm</p>
<p>Attended (night)</p>	<ul style="list-style-type: none"> • An STMS or delegated TMO must be onsite at all times. • TC/STMS to assist pedestrians/cyclists/driveways and any resident/business driveways. • For Stop/Stop and Stop/Go setups, cyclists will be sent prior to any vehicles. • STMS/TC will complete 2 hourly site checks and document on the onsite record. • Additional lighting may be required/supplied. • Noise will be kept to a minimum where possible. • Where Mobility Parking is affected alternative to be provided (same side of road, as close as possible), TM personnel to assist and guide users as required <p>Works near Signals:</p> <ul style="list-style-type: none"> • Any affected signal loops must be notified to WTOC during the pre-installation call to allow them to adjust signal management. <p>Works near Pedestrian Crossings:</p> <ul style="list-style-type: none"> • MTC's to guide pedestrians through/around the closure. <p>Works near a Bus Stop:</p> <p>Bus stop integrated into MTC Stop Point</p> <ul style="list-style-type: none"> • MTC's on stop/go are to stop each bus and assist with loading & unloading of passengers as required. • Bus stop signage is to direct pedestrians towards the stop point <p>Bus stop relocated away from site</p> <ul style="list-style-type: none"> • Bus stop signage is be placed to show patrons where the relocation is. • TM personnel to assist and guide bus patrons as required • Temporary bus stop signage is to be used • Parking restrictions are to be in place at the relocated bus stop

Unattended (day)	<ul style="list-style-type: none"> Where hazards are present an appropriate aftercare closure would be installed as required. Contractor to perform risk assessment on site and determine if additional lighting sources are required. A site check must be completed a minimum of once every 24hrs or as required due to adverse weather or complaints. <u>Road Space Booking</u> (attached), CAR and email notification to the TMC & Corridor access manager will be required for any works required to be left unattended. Use of Traffic Signals (F2.17) & F2.4 must be approved by TMC prior to leaving on an unattended site. F2.16 requires TMC approval prior to installing on both attended and unattended sites e-STOPS – ATMS 02, ATMS 03 & ATMS 05 are not permitted for use whilst site is unattended – e-STOPS must be manned at all times. e-Stops are a remote control MANUAL operated system so cannot physically operate when unattended. Unattended site for concrete setting maybe left as required in footpath, berm or shoulder using F2.1, F2.2, F2.3, F2.7. must be approved prior by TMC.
Unattended (night)	As per Unattended (day)
Detour route	<p>A detour route is not required or approved in the TMP</p> <p>Does detour route go into another RCA's road network? No</p> <p>If Yes, has confirmation of acceptance been requested from that RCA? No</p> <p>Note: Confirmation of acceptance from affected RCA must be submitted prior to occupying the site.</p>
Removal	<p>STMS to contact Metlink (0800 801 700) upon site removal</p> <p>STMS to contact WTOC (0800 869 286) upon site removal.</p> <p>Work plant / vehicles to be removed from site before closure is removed</p> <p>Removal of the site will be done under a level 1 mobile closure with appropriate work vehicles and crew.</p> <ol style="list-style-type: none"> Workspace delineation to be removed first (by either removing to the kerb for later collection or directly onto a stationary working vehicle) Centreline delineation may now be removed using the same method as installation Once all delineation is removed – sign removal may commence in a clockwise 'loop' fashion (leaving advanced warning signage in place till last) A full site check being conducted prior to site departure. <p>The STMS will carry out the final check before leaving the site.</p>

Proposed TSLs (see TSL decision matrix for guidance)				
	TSL details as required Approval Temporary Speed Limits (TSL) of Section 7 of Land Transport Rule: Setting of Speed Limits 2022. (additional rows may be added if required)	Times (From and to)	Dates (Start and finish)	Diagram ref. no.s (Layout drawings or traffic management diagrams)
Attended day/night	<p>A temporary maximum speed limit is hereby fixed for motor vehicles travelling over the length of _____ situated between _____ (house no./RP) and _____ (house no./RP) on _____ (street or road name)</p> <p>STMS to document on the Onsite Record daily.</p>	24hrs	01/01/2025 To 31/12/2025	F2.11, F2.12, F2.13, ATMS02, F2.14, ATMS04, F2.22, F2.15, F2.16, F2.17, F2.18, F2.19, F2.20, F2.21, F2.30, F2.31, F2.8, F2.9, ATMS03, J2.19a, J2.20a, J2.20b, J2.20c, J2.20d, J2.20e,


APPROVED

CAR R1066208

Jason Wildman

STMS Number 307.43

Hutt City Council



14 November 2024

Unattended day/night	A temporary maximum speed limit is hereby fixed for motor vehicles travelling over the length of _____ situated between _____ (house no./RP) and _____ (house no./RP) on _____ (street or road name) STMS to document on the Onsite Record daily.	24hrs	01/01/2025 To 31/12/2025	F2.1, F2.2, F2.3, F2.7, F2.8, F2.9, F2.11, F2.12, F2.13, F2.16, F2.17, F2.18, F2.19, F2.20, F2.26, F2.27, F2.28, F2.29, F2.30, F2.31, J2.20a, J2.20b, J2.20c, J2.20d, J2.20e, ATMS02, ATMS03
TSL duration	Will the TSL be required for longer than 12 months? <i>If yes, attach the completed checklist from section I-18: Guidance on TMP Monitoring Processes for TSLs to this TMP.</i>			No

Positive traffic management measures



APPROVED

CAR R1066208
Jason Wildman
STMS Number 307.43


Hutt City Council

Signature
Page 13

14 November 2024

- Side friction delineation installed from TSL to the start of the taper.
- Additional cones may be placed on centerlines, edgelines or shoulders to increase site safety and reduce vehicle speed.
- Use of paddles and TSL
- Cone offset delineation – where cones are placed either side of the lane(s), the cones on one side are placed longitudinally offset from the other by half a cone spacing.

Reduced cone spacing (2.5m)
can be utilised to increase impact

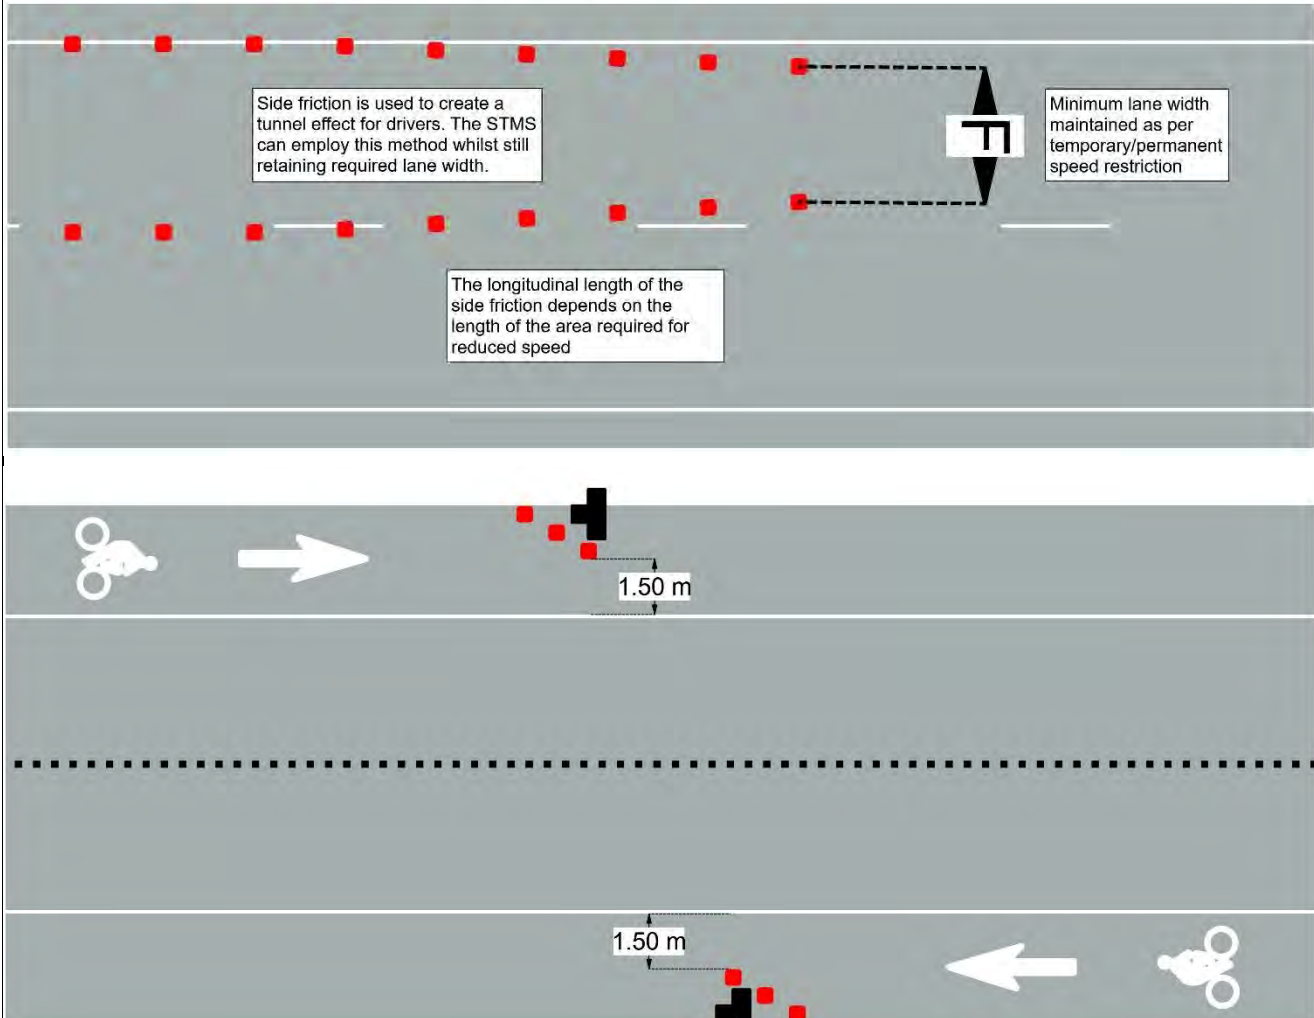

Contingency plans

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307.43

Hutt City Council

14 November 2024

<p>Generic contingencies for:</p> <ul style="list-style-type: none"> major incidents incidents pre planned detours. <p><i>Remove any options which do not apply to your job</i></p>	<p>Major Incident A major incident is described as:</p> <ul style="list-style-type: none"> Fatality or notifiable injury - real or potential Significant property damage, or Emergency services (police, fire, etc) require access or control of the site. 	<p>Actions The STMS must immediately conduct the following:</p> <ul style="list-style-type: none"> stop all activity and traffic movement secure the site to prevent (further) injury or damage contact the appropriate emergency authorities render first aid if competent and able to do so notify the RCA representative and / or the engineer under the guidance of the officer in charge of the site, reduce effects of TTM on the road or remove the activity if safe to do so re-establish TTM and traffic movements when advised by emergency authorities that it is safe to do so Comply with any obligation to notify WorkSafe.
	<p>Incident An incident is described as:</p> <ul style="list-style-type: none"> excessive delays - real or potential minor or non-inquiry accident that has the potential to affect traffic flow structural failure of the road. 	<p>Actions The STMS must immediately conduct the following:</p> <ul style="list-style-type: none"> stop all activity and traffic movement if required secure the site to prevent the prospect of injury or further damage notify the RCA representative and / or the engineer STMS to implement a plan to safely remove TTM and to establish normal traffic flow if safe to do so re-establish TTM and traffic movements when it is safe to do so and when traffic volumes have reduced.
	<p>Detour If because of the on-site activity it will not be possible to remove or reduce the effects of TTM once it is established a detour route must be designed. This is likely for:</p> <ul style="list-style-type: none"> excessive delays when using an alternating flow design for TTM redirecting one direction of flow and / or total road closure and redirection of traffic until such time that traffic volumes reduce and tailbacks have been cleared. <p>The risks in the type of work being undertaken, the risks inherent in the detour, the probable duration of closure and availability and suitability of detour routes need to be considered.</p> <p>The detour and route must be designed including:</p> <ul style="list-style-type: none"> pre-approval from the RCA's whose roads will be used or affected by the detour route ensure that TTM equipment for the detour signs etc are on site and pre-installed. 	<p>Actions When it is necessary to implement the pre-planned detour the STMS must immediately undertake the following:</p> <ul style="list-style-type: none"> Notify the RCA and / or the engineer when the detour is to be established Drive through the detour in both directions to check that it is stable and safe Remove the detour as soon as it is practicable and safe to do so and the traffic volumes have reduced and tailbacks have cleared Notify the RCA and / or the engineer when the detour has been disestablished and normal traffic flows have resumed.

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307.43

Hutt City Council

14 November 2024

	<p>Note also the requirements for no interference at an accident scene:</p> <p>In the event of an accident involving serious harm the STMS must ensure that nothing, including TTM equipment, is removed or disturbed and any wreckage article or thing must not be disturbed or interfered with, except to:</p> <ul style="list-style-type: none"> • save a life of, prevent harm to or relieve the suffering of any person, or • make the site safe or to minimise the risk of a further accident; or • maintain the access of the general public to an essential service or utility, or • prevent serious damage to or serious loss of property, or • follow the direction of a constable acting in his or her duties or act with the permission of an inspector.
Other contingencies to be identified by the applicant (i.e. steel plates to quickly cover excavations)	<p>This will be determined on a case-by-case basis. Where achievable works will stop until emergency or delays have been cleared.</p> <p>Should signals or e-STOPS fail – Manual Traffic Control is to be installed immediately (refer to F2.14 & F2.22).</p>

Authorisations				
Parking restriction(s) alteration authority	Will controlled street parking be affected?	Yes (potentially)	Has approval been granted?	N/A
	Where Mobility Parking is affected alternative to be provided (same side of road, as close as possible), TM personnel to assist and guide users as required			
Authorisation to work at permanent traffic signal sites	Will portable traffic signals be used or permanent traffic signals be changed?	Yes (potentially)	Has approval been granted?	No
	WTOC to be notified 30 mins prior to site installation and upon removal.			
Road closure authorisation(s)	Will full carriageway closure continue for more than 5 minutes (or other RCA stipulated time)?	No	Has approval been granted?	No
	N/A			
Bus stop relocation(s) – closure(s)	Will bus stop(s) be obstructed by the activity?	Yes (potentially)	Has approval been granted?	No
	Pre-approval required from Metlink for any works obstructing bus stops. Metlink will be notified 30 mins prior to installation and upon removal.			
Authorisation to use portable traffic signals	Make, model and description/number	eSTOP Portable Traffic Signals: model# <ul style="list-style-type: none"> • 627 - 1, 627 - 2 • 628 - 1, 628 - 2 • 629 - 1, 629 - 2 • 630 - 1, 630 - 2 • 631 - 1, 631 - 2 		
	NZTA compliant?	Yes		

EED			
Is an EED applicable?	EED is not required	EED attached?	EED is not required

Delay calculations/trial plan to determine potential extent of delays

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307.43

e-STOP & Stop Go Closures:

Delays of up to 5 minutes can be expected due to the nature of the TTM implemented. The STMS is to take measures to ensure delays remain under 5 minutes at all times, and queues do not extend past the advance warning signage.

If delays are occurring or excessive queueing is apparent, the STMS is to implement one of the following contingency plans;

- 1) Traffic Metering
Send only a specific amount of vehicles per side instead of clearing the entire queue
- 2) Pause works and open site
Make the site safe, remove plant and vehicles from the carriageway and open the tapers
- 3) Prioritise high flow route
Send vehicles from the approach with the highest flow first. Hold side street traffic for slightly longer if required.
- 4) Install additional signage
Install T2A/T234 "Warning – Hidden Queue" signage up to 2xB from the initial advance warning signage for additional advance warning

STMS will continuously monitor for delays – TMC will be notified of any excessive delays.

Public notification plan

A letter drop to residents and businesses is to be completed 5 working days prior to works commencing.

WTOC notification for any works which are in close proximity to traffic signals and/or for a communications plan on permanent VMS within Hutt City region.

Public notification plan attached? No

On-site monitoring plan

Attended (day and/or night)	An STMS or delegated TMO will be on site at all times. 2 Hourly Site Checks to be documented on the on-site record. STMS/TM-W to monitor and assist pedestrians, cyclists and driveways when needed.
Unattended (day and/or night)	Unattended site to be checked at least once every 24 hours with site check frequency increasing in the case of inclement weather or complaints. If temporary signals are used (F2.17) site checks are to be completed 2hourly or as required due to inclement weather or complaints.

Method for recording daily site TTM activity (eg CoPTTM on-site record)

- Hazard ID sheet
- CoPTTM on-site record.
- Checking process for Generic TMPs form to be completed prior to set up of a worksite when using this TMP.

Site safety measures

- All visitors/contractors to be inducted and hazard ID completed
- PPE gear to be worn by all on site
- Toolbox meeting to be held prior to work commencing.
- Arm bars to be installed around the work area.
- STMS/TC to monitor and assist pedestrians, cyclists and driveway access at all times when required.
- Pedestrian ramps to be installed when required.

Temporary safety barrier system	Will a temporary safety barrier system be used at this worksite?	No	If yes, has the temporary safety barrier system been designed by an installation designer and independently reviewed as being fit for purpose?	N/A
	Statement from temporary safety barrier installation designer attached			N/A

Other information

LEVEL 1 LAYOUT DISTANCES TABLE

Permanent speed limit or RCA-designated operating speed (km/h)		≤50	60	70	80	90	100		
Traffic signs									
A	Sign visibility distance (m)	50	60	70	80	90	100		
B	Warning distance (m)	50 or 30*	80	105	120	135	150		
C	Sign spacing (m)	25 or 15*	40	50	60	70	75		
Safety zones									
D	Longitudinal (m)	10 or 5*	15	30	45	55	60		
E	Lateral (m)	1	1	1	1	1	1		
Tapers									
G	Taper length (m)*	30	50	70	80	90	100		
K	Distance between tapers (m)	40	50	70	80	90	100		
Delineation devices									
Cone spacing in taper (m)		2.5	2.5	5	5	5	5		
Cone spacing: Working space (m)		5	5	10	10	10	10		
<p>* Larger minimum distances apply on all state highways and also on all multi-lane roads. The smaller minimum distances may be applied on other roads to accommodate road environment constraints.</p> <p>* On non-state highways with speeds 50km/h or less, a 10m taper (with cones at 1m centres) may be used when there are road environment constraints (eg intersections and commercial accesses).</p> <p>On all roads where shoulder width is less than 2.5m and the activity does not affect the live lane, a 10m shoulder taper is permitted (with at least 5 cones at no greater than 2.5m centres).</p> <p>A taper of 30m (with cones at 2.5m centres) must be used where manual traffic control (stop/go), portable traffic signals or priority give way are employed.</p>									
Lane widths									
Speed (km/h)		30	40	50	60	70	80	90	100
F	Lane width (m)	2.75	2.75	3.0	3.0	3.25	3.25	3.5	3.5

Except for delineation device spacings, which are maximum values, the distances specified in the above tables are minimum values.

Attached Diagrams

Pedestrian Management

1. CC1 – Works on berm or footpath
2. CC2 – Traffic not crossing road centre
3. CC3 - Works on berm or footpath – vehicle parked on berm
4. CC4 – Footpath diverted onto shoulder or parking lane
5. CC5 – Footpath Controller
6. ATMS05 – Pedestrian Escort (1st Choice)
7. F2.1 – Pedestrian Diversion (berm) (2nd Choice)
8. F2.2 – Pedestrian Diversion (berm) (3rd Choice)

APPROVED

CAR R1066208
Jason Wildman
SMS Number 307 43

9. F2.3 – Pedestrian Diversion (carriageway) (4th Choice)
10. F2.4 – Footpath Closed (5th Choice) **Requires TMC approval**

Works on berm/shoulders/Lane Width Reduction

11. F2.5 – Works on berm
12. F2.6 – Works on parking lane
13. F2.7 – Shoulder Closure
14. F2.11 – Lane Width Reduction
15. F2.12 – Lane Width Reduction (median)

Inspection Activities

16. F4.10 – Inspection Activity
17. ATMS07 – Inspection Activity – Centre of Road

Lane Closures/Diversions/e-STOP/MTC/Traffic Lights/Centre of Road

18. F2.13 – Two Lane Diversion
19. ATMS02 - 2 Way e-STOP
20. F2.14 – 2 Way MTC
21. ATMS04 – e-STOP with MTC
22. F2.22 – 3-4 Way MTC
23. F2.15 – Stop Stop
24. F2.16 – Priority Give Way **Requires TMC approval**
25. F2.17 – Traffic Lights – **Requires TMC approval for unattended sites**
26. F2.18 – Works in centre of road
27. F2.19 – Intersection
28. F2.20 – Intersection
29. F2.21 – Works in middle of intersection
30. F2.30 – Left Lane Closure (1 way, 2 lane)
31. F2.31 – Right Lane Closure (1 way, 2 lane)

Hazards/Aftercare

32. F2.26 – Hazard – Flooding
33. F2.27 – Hazard – New Seal
34. F2.28 – Hazard – Surface Hazard
35. F2.29 – Hazard – Seal Repairs on a curve

Mobile Operations/Semi Statics

36. CC8 – Valve towards left of lane
37. CC9 – Valve towards right of lane
38. CC12 – Two way – Two Lane Road
39. F4.1 – Mobile Operation – 5m from edgeline
40. F4.2 – Mobile Operation – within 5m of edgeline
41. F4.3 – Mobile Operation – with pilot
42. F4.4 – Mobile Operation – work vehicle in lane
43. ATMS06 – Semi Static (right or left lane)
44. Mobile Closure – L1 – Install & Removal

Cycle Lanes

45. F2.8 – Cycle Lane Diversion
46. F2.9 – Cycle Lane Diversion
47. ATMS03 – Cycle Lane e-STOP

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307.43

Hutt City Council

Signature

14 November 2024


Section J diagrams

- 48. J2.16a
- 49. J2.19a
- 50. J2.20a
- 51. J2.20b
- 52. J2.20c
- 53. J2.20d
- 54. J2.20e

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307.43

Hutt City Council



14 November 2024

Contact details						
	Company / Council	Name	24/7 contact number	CoPTM ID	Qualification	Expiry date
Principle	Wellington Water	Ben Wilson	027 3355 334	-	-	-
TMC	Hutt City Council	Jason Wildman	027 330 3097	30743	Cat (ABC) NP	26/10/25
Engineers' representative	Wellington Water	Ben Wilson	027 3355 334	-	-	-
Service Delivery Manager	Wellington Water	Steve Watt	021 507 440	-	-	-
Contractor Interim Contacts	Action Civil	Dave Murtagh	027 442 2971	-	-	-
	Agricontracts Hutt Ltd (CAS)	Jaden Munn	027 319 4575	-	-	-
	Aidan Kelly Contracting (AKC)	Cory Hikuroa	021 455 361	-	-	-
	ATMS	David Quintela	027 213 5654	-	-	-
	Alliance Services Ltd	Chris Barlow	021 640 282	-	-	-
	Anzel Limited	Darryl Tatana	021 281 1102	-	-	-
	Arthur D Riley & Co Ltd	Chris Parkinson	04 472 7614	-	-	-
	Brian Perry Civil	Blair Mould	027 229 3270	-	-	-
	Stantec	AJ Weir (Alice) Andrea Brett Eaton	027 331 9930 021 222 8756 021 861 772	-	-	-
	City Care Ltd	Mark Thompson	027 542 6244	-	-	-
	Constructions Contracts Limited	David Howard	021 243 6656	-	-	-
	Cubic Metre	Andrew McWhirter	021 345 79	-	-	-
	Daniel Renshaw Drainage Contractor Ltd	Daniel Renshaw	027 450 8799	-	-	-
	Davies Waste Solutions	Jan Godfrey	04 528 9909	-	-	-
	Dawson Waste Services Ltd	Dave Phillipson	022 657 2402	-	-	-
	Detection Services	Ross Beckett	04 915 0530	-	-	-
	DMK Contracting	Deon Kumm	027 202 5142	-	-	-
	Downer New Zealand	Sam Farnworth	021 896 603	-	-	-
	Drain Doctor NZ Ltd	Ian Pauley	027 484 8887	-	-	-
	E Carson & Sons	Eddie Carson	027 442 4343	-	-	-
	E N Ramsbottom Ltd	Michelle Hoffman	027 471 6246	-	-	-
	Fulton Hogan	Duncan Mundell	027 4786 203	-	-	-
	G & C Diggers	Mark Dennes	022 350 7550	-	-	-
	G P Friel Ltd	Dave Phillipson	022 657 2402	-	-	-
	Greenstone Contracting Ltd	David Williams	04 566 0890	-	-	-
	Groundworks Ltd	Hamish Rees	027 765 6139	-	-	-
	Horokiwi Paving Limited	Peter Green	027 443 2206	-	-	-
	Hydrotech Limited	David Neru	09 600 0888	-	-	-
	Inline Drainage Limited	Patrick Carson	027 294 0952	-	-	-
	Intergroup Ltd	Alex Phelan	021 927 801	-	-	-
	Ives Plumbing Ltd	Daniel Barnett	021 758 621	-	-	-

	JB's Environmental Ltd	John Matangi	021 750 920	-	-	-
	Jet Black Asphalts Ltd	Neville Playford	027 208 9309	-	-	-
	Juno Civil	Jim Juno	021 227 7001	-	-	-
	Laser Plumbing Wellington East	Simon Walker	027 449 1180	-	-	-



APPROVED

CAR R1066208
Jason Wildman
STMS Number 307.43

Hutt City Council

Jason Wildman

14 November 2024

	Mac Engineering	Regan McMurchie	021 1567 908	-	-	-
	Marais Laying NZ Ltd	Adrien Merceron	027 555 7802	-	-	-
	McCormack Group	Willy McCormack	027 449 3985	-	-	-
	McLatchie & Sharp Ltd	Adam Clarke	027 443 3760	-	-	-
	McMaster Civil	Richard McMaster	021 963 509	-	-	-
	Mills Albert Ltd	Dave Mills	021 720 123	-	-	-
	Mottmac	Patrick Wharewera-Jones	027 746 8395	-	-	-
	Mottmac	Matthew Cooper	021 688 013	-	-	-
	Plimmer Plumbing Ltd	Steven Fawcett	027 215 3667	-	-	-
	P & N Siteworks Ltd	James Hosie	027 235 8363	-	-	-
	Pope & Gray Contractors	Sid Taylor	027 255 1948	-	-	-
	RS Cabling Limited	Nathan Rose	027 275 4317	-	-	-
	Rasmac Contractors Ltd	Lawrence Rasmussen	027 444 3041	-	-	-
	Reline NZ Ltd	Paul Southern	021 175 021	-	-	-
	S & R Asphalts Ltd	Scott Hay	027 440 2405	-	-	-
	S B Maintenance Ltd	David O'Sullivan	027 2810 9998	-	-	-
	SAP Contractors Limited	Glenn Churches	027 272 1666	-	-	-
	Sierra Delta Civil Ltd	Sam Dews	027 592 2290	-	-	-
	Silver Lining Contracting Ltd	Renee Wilkie	021 0828 0647	-	-	-
	Steve Quinn Professional Lawn Mowing Ltd	Steve Quinn	027 451 6343	-	-	-
	Stewart Electrical	Tim Stewart	021 507 245	-	-	-
	Stone Contractors Ltd	Allan Glover	021 529 681	-	-	-
	T E D Drainage Ltd	karl Taylor-Edwards	027 675 5996	-	-	-
	Tasman Civil	Keith Robertson	027 4384 536	-	-	-
	Tatana Contracting	Darryl Tatana	0800 368 938	-	-	-
	Vac-U-Digga	Kathy Fandham	021 246 3615	-	-	-
	Wal Gordon Plumbing Ltd	Wal Gordon		-	-	-
	Wellington Pipelines Limited	James Fruean	027 499 9223	-	-	-
	Wellington Developments Ltd	Harold Paul	021 0273 7643	-	-	-
	Wet Worx Limited	Walter Alexander	021 239 4211	-	-	-
	A1 Locates	Brad Thomas	021 296 9477	-	-	-
	Kelcon Limited	Wayne Kelland	027 263 8731	-	-	-

CAR R1066208
Jason Wildman
STMS Number 307.43

TTM Interim Contacts	ATMS	Vena Lam Sam	021 767 165	39930	Cat A,B,C	22/09/24
	ATMS	Martyn Sauaiga	027 348 9478	72781	Cat A,B (P) Cat C (NP)	19/08/25
	Hanging Around Traffic Management	Sam Redhill	021 505 900	-	-	-
	Men At Work - Traffic Management	Kurt Puryer-Smith	027 274 2369	-	-	-
	Men At Work - Traffic Management	Todd Lynch	027 282 0998	-	-	-
	SAP Contractors	Glenn Churches	027 272 1666	-	-	-
	Stapp Contracting Traffic Management	Shane Pihema	027 249 9882	-	-	-
	Traffic Management NZ Ltd	Steven Loftus	027 491 9494	-	-	-
	Leading Traffic	Chantelle Mereriana Ngaia	027 2555 5002	-	-	-
	Leading Traffic	Ben Teika	027 555 0997	-	-	-
	Trafficflow	Steven Huriwaka	021 944 037	-	-	-
Others as required	WTOC		0800 869 286	-	-	-
	Metlink Contact Centre		0800 801 700	-	-	-
	Hutt City Council Corridor Manager	Kara Collins	027 258 3801	-	-	-

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307.43

Hutt City Council

14 November 2024

TMP preparation							
Preparation	Pania Werahiko	04/11/2024	<i>P. Werahiko</i>	149481	STMS (A) NP -R	-	11/01/2026
					STMS (B) NP -R		25/01/2026
	Name (STMS qualified)	Date	Signature	ID no.	Qualification	TTMP	Expiry date

* additional column added to indicate the attended (or confirmed booking) date of the named designer on the NZTA Temporary Traffic Management Planners (TTMP) workshop as required by the NZTA technical note, issued 9 December 2019

This TMP meets CoPTTM requirements					Number of diagrams attached		54
TMP returned for correction (if required)							
	Name	Date	Signature	ID no.	Qualification	Expiry date	
Engineer/TMC to complete following section when approval or acceptance required							
Temporary safety barrier system	The attached temporary road safety barrier design has been independently reviewed as being fit for purpose					Not required	
TMP Approved							
	Name	Date	Signature	ID no.	Qualification	Expiry date	
Acceptance by TMC (only required if TMP approved by engineer)							
	Name	Date	Signature	ID no.	Qualification	Expiry date	

Qualifier for engineer or TMC approval			
<p>Approval of this TMP authorises the use of any regulatory signs included in the TMP or attached traffic management diagrams.</p> <p>This TMP is approved on the following basis:</p> <ol style="list-style-type: none"> 1. To the best of the approving engineer's/TMC's judgment this TMP conforms to the requirements of CoPTTM. 2. This plan is approved on the basis that the activity, the location and the road environment have been correctly represented by the applicant. Any inaccuracy in the portrayal of this information is the responsibility of the applicant. 3. The TMP provides so far as is reasonably practicable, a safe and fit for purpose TTM system. 4. The STMS for the activity is reminded that it is the STMS's duty to postpone, cancel or modify operations due to the adverse traffic, weather or other conditions that affect the safety of this site. 			
Notification to TMC prior to occupying worksite/Notification completed			
Type of notification to TMC required		Notification completed	<div>Date</div> <div>Time</div>

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307.43

ROAD SPACE BOOKING

Address:				
Contractor:				
Dates & Times (attended):	From:		To:	
Dates & Times (unattended):	From:		To:	
Generic TMP used:				
Diagram (s) used:				
CAR #				
Work Activity and Reasons TTM to remain in place:				
Contractor Name:				
Contractors Signature:				
TMC Approval:				

Please attach photos of site active site set up (these photos are to include both ends of the site (inclusive of any side roads), pedestrian/cycle management and the working area.

ON-SITE RECORD MOBILE OPERATIONS (*On-site record must be completed and retained with the applied TMP for 12 months*)

Today's date

STMS in charge of TTM

Name	NZTA warrant	TTM ID Number	NZTA warrant expiry date	STMS signature	Time

In charge STMS pre-start check

Mandatory Items to be checked as fit for purpose	High-visibility garments are fit for purpose, in an acceptable condition and worn correctly?	Vehicle Xenon (or LED)/Beacons are fit for purpose?	LAS/RD6/AWVMS/VMS/Horizontal arrow boards are fit for purpose?	TMA's are fit for purpose	Two-way radios available, operating OK and batteries are fully charged	Correct signs for work operation are fitted to all vehicles and are fit for purpose
Time the check was completed:		In charge STMS signature:				

Operation record (*To be completed for all inspection worksites/runs, mobile runs, semi-static sites*)

Affected Road Environment Details			Work Activity Timing	
Affected Road name(s)	Worksite start point	Worksite end point	Start	End

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council

Checks *(must be completed and documented at least every 30 minutes)*

Mobile closure

Time	Distances between vehicles maintained	Lateral positioning of vehicles maintained	LAS/RD6/AWVMS/VMS/Horizontal arrowboards continue to operate correctly	Road clear and available for planned work?	Static equipment maintained?	Safety zones maintained?	Working space adequate and maintained?

Comments relating to any changes and or improvements to the approved TTM/TMP

Time of comment	Detail



ON-SITE RECORD

On-site record must be retained with TMP for 12 months.

Today's date

Location details

Road names(s):

House number/RPs:

Suburb:

Working space

Person responsible for working space

Name

Signature

Where the STMS/TC is responsible for both the working space and TTM they sign above and in the appropriate TTM box below

TTM

STMS in charge of TTM

Name

TTM ID Number

Warrant expiry date

Signature

Time

Worksite handover accepted by replacement STMS

Name

ID Number

Warrant expiry date

Signature

Time

Tick to confirm handover briefing completed

Delegation

Worksite control accepted by TC/STMS-NP

Name

ID Number

Warrant expiry date

Signature

Time

Tick to confirm briefing completed

Temporary speed limit

Street/road name (RPs or street numbers):

TSL action

Date:

Time:

TSL speed:

Length of TSL (m):

From:

To:

TSL installed

TSL remains in place

TSL removed

Street/road name (RPs or street numbers):

TSL action

Date:

Time:

TSL speed:

Length of TSL (m):

From:

To:

TSL installed

TSL remains in place

TSL removed

Street/road name (RPs or street numbers):

TSL action

Date:

Time:

TSL speed:

Length of TSL (m):

From:

To:

TSL installed

TSL remains in place

TSL removed

Street/road name (RPs or street numbers):

TSL action

Date:

Time:

TSL speed:

Length of TSL (m):

From:

To:

TSL installed

TSL remains in place

TSL removed

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council


Worksite monitoring

TTM to be monitored and 2 hourly inspections documented below.

Items to be inspected	TTM set-up	2 hourly check	2 hourly check	2 hourly check	2 hourly check	2 hourly check	TTM removal
High-visibility garment worn by all?							
Signs positioned as per TMP?							
Conflicting signs covered?							
Correct delineation as per TMP?							
Lane widths appropriate?							
Appropriate positive TTM used?							
Footpath standards met?							
Cycle lane standards met?							
Traffic flows OK?							
Adequate property access?							
Barrier deflection area is clear? (Refer to Barrier design statement)							
Add others as required							
Time inspection completed:							
Signature:							
Comments:							
Time	Adjustment made and reason for change						

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council

Checking process for generic TMPs						
<i>This form, or a similar company record, must be completed prior to set up of a worksite where a generic TMP is used.</i>						
Location details						
Road name(s)			House number/RP(s)			Suburb
Road name(s)			House number/RP(s)			
Generic TMP reference no.		TMD no(s).			Note: The checking process must include all the TMDs to be used	
Category	Points to consider	Y	N	Comment/Mitigation		
Road level	Is this at the correct road level?					
Shape	Are the following catered for in the generic TMP? <ul style="list-style-type: none"> • Intersections • Vertical Curves (hills) • Horizontal Curves (corners) • Sufficient advance warning 					
Direction and protection	Check that there is: <ul style="list-style-type: none"> • sufficient length to place the planned direction and protection • sufficient road width to place the planned direction and protection ie minimum lane width is 2.75m • adequate sight distance on both sides • sufficient room to accommodate required positive traffic control 					
Proposed speed restrictions	Is a TSL required? Refer to the TSL decision matrix in CoPTTM (section E Appendix B)					
Plant and equipment	Will your plant and equipment fit within the designated working space?					
Personal safety	Are all workers able to carry out their work within the designated working space? If not are they covered by the rules for inspections?					
Layout diagrams	Is diagram(s) detailed in the generic TMP? Does the diagram(s) match the written section of the TMP?					
RCA notification	Has the RCA been notified?					
Completed by:						
STMS/TC in charge of worksite (All names to be entered before site set-up)						
	Name	Signature	Date	Qualification	ID number	
	<div style="border: 2px solid red; padding: 5px; text-align: center;"> APPROVED CAR R1064208 Jason Wilder STMS Number 307 43 Hutt City Council  </div>					
	Name	Signature	Date	Qualification	ID number	



















TEMPORARY SPEED LIMIT (TSL) DECISION MATRIX WORKSHEET

INSTRUCTIONS

Select the appropriate road condition description for each of the four factors, and in the right hand circle list the chosen TSL for that road condition. Transfer lowest TSL to the bottom circle.

Appendix B

Possible
Temporary
Speed Limit

	EXCELLENT	AVERAGE	BELOW AVERAGE	POOR	
	  	 	 	  	
1. Minimum Lane Width	3.5m	3.25m	3.00m	2.75m	
2. Pavement / Surface Condition	The shoulder and lane is clear of loose or greasy material and the traveled way is smooth	The road is close to normal condition except for a few minor defects (eg small pot holes or a few pieces of loose aggregate) 70km/h where new seal has been swept but not marked	Defects and / or loose material on the lane (eg unattended reseals) 50km/h for protection of a new seal	There are major defects and / or significant loose material on the lane (eg recently milled surface, large stones, steel plates)	
3. Visibility and Alignment	There is greater than 140m visibility to the first cone in taper, and the worksite has not imposed a change in alignment	There is less than 140m visibility to the first cone in taper, or vehicles are deflected by 20 degrees or less from the original direction of travel 	There is less than 60m visibility to the first cone in taper, or vehicles are deflected by 20-45 degrees from the original direction of travel 	There is less than 30m visibility to the first cone in taper, or vehicles are deflected by more than 45 degrees from the original direction of travel 	
4. Site Clutter	Low site clutter, clear vehicle lanes, cycle lanes and footpaths	Some site clutter either plant or materials, vehicle lanes, cycle lanes and footpaths are lightly trafficked	Considerable site clutter requires additional management to guide vehicles though the site. Some queues of road users	Has numerous driver distractions including construction traffic. Cycle lanes or footpaths are closed. 30km/h for portable traffic signals, MTC operations or where traffic has to traverse the actual active working space (either in a delineated single lane or where traffic is not separated from the working space)	 

Is the lowest speed 80km/h or less and at least 10km/h below the permanent speed?

Yes
No

Use this Temporary Speed Limit

No Temporary Speed Limit Required

APPROVED

CAR R1066223
STMS Number 307 43
14 November 2024

14 November 2024


[Click here to reset](#)

Roads of Significance

TMPs on the following roads cannot be self-approved. Approval from the HCC TMC is required.

1. Wainuiomata Hill Road (both directions) from Rishworth Street to Parkway
2. Wainui Road from Rishworth Street to Whites Line East
3. Whites Line East from Wainui Road to Randwick Road
4. Randwick Road
5. Waione Street including Seaview Roundabout
6. The Esplanade (both directions) including Hutt Road roundabout
7. State Highway 2 onramp (Petone)
8. Jackson Street from Hutt Road to Cuba Street
9. Cuba Street
10. Hutt Road
11. Railway Avenue
12. Ewen Bridge from Railway Avenue to Queens Drive including roundabout
13. Woburn Road
14. Ludlam Cres
15. Whites Line East from Randwick Road (including roundabout) to Wainui Road
16. Lower Hutt CBD
17. Melling Bridge
18. Block Road
19. High Street from Queens Drive roundabout to Fairway Drive roundabout
20. Fairway Drive from High Street to Kennedy Good Bridge
21. Kennedy Good Bridge to State Highway 2
22. Eastern Hutt Road from High Street to Stokes Valley Road both directions (including both roundabouts)
23. Eastern Hutt Road from Stokes Valley Road to Reynolds Bach Drive



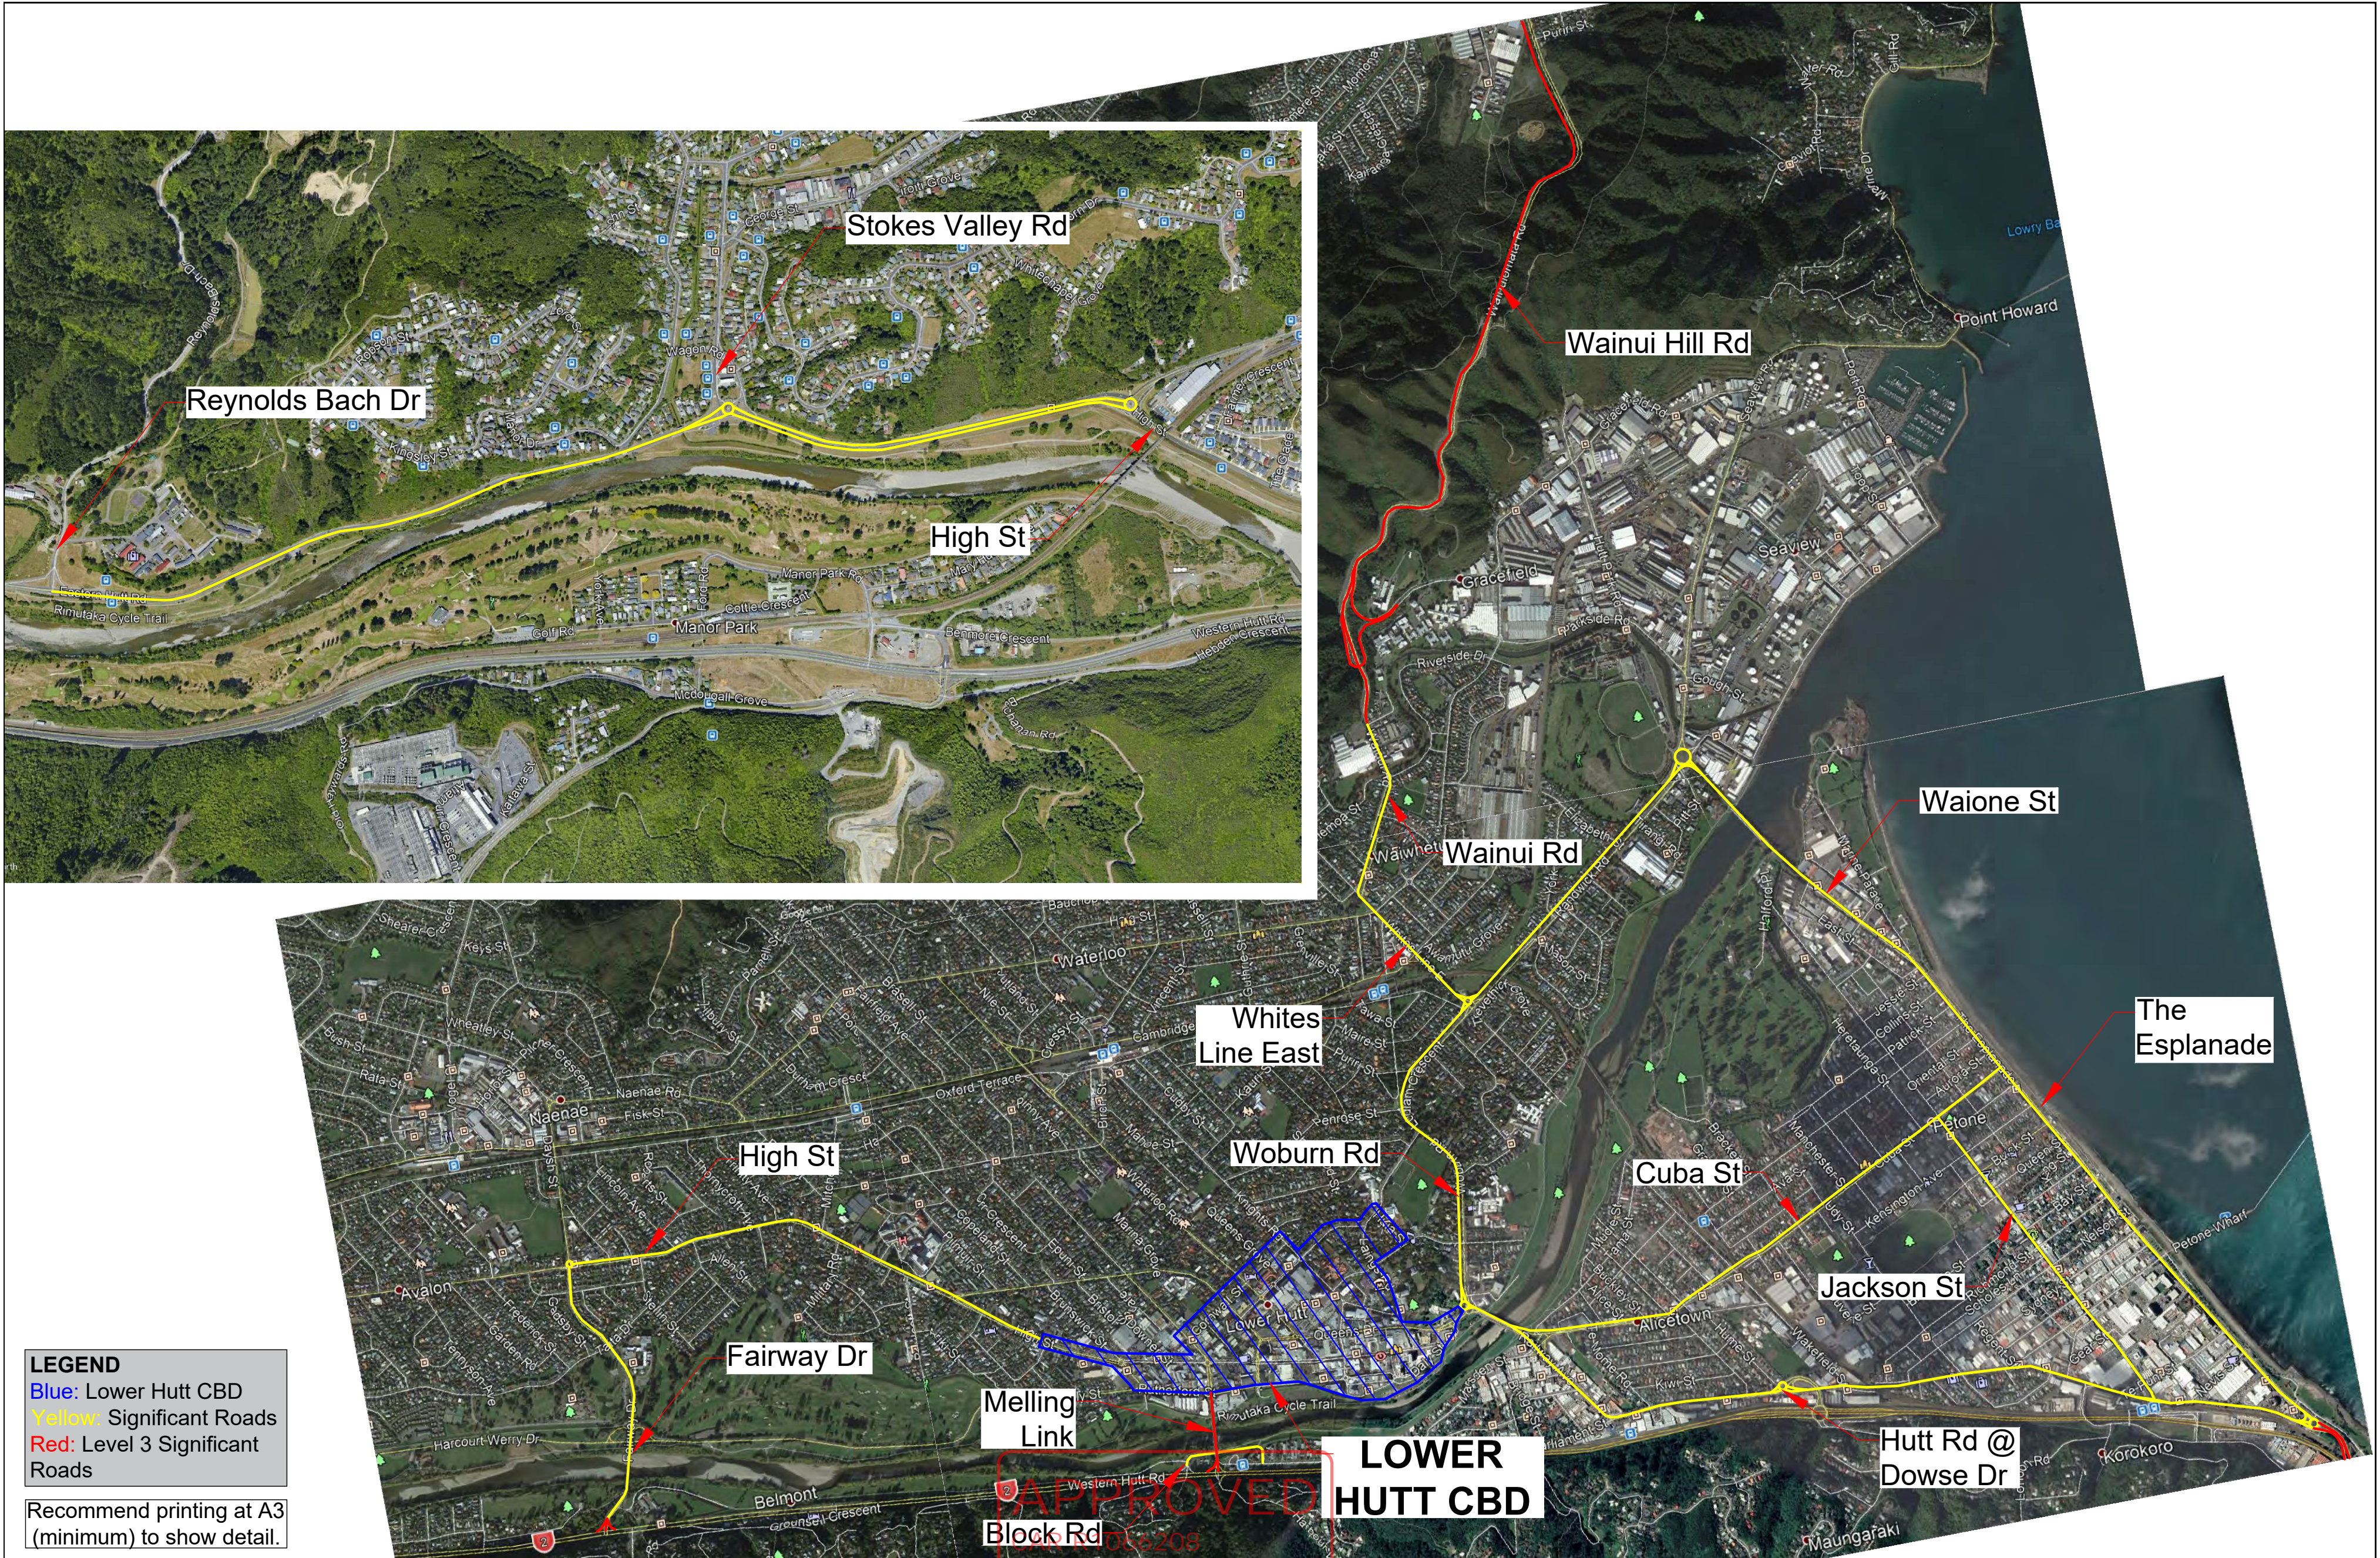

LEGEND
Blue: Lower Hutt CBD
Yellow: Significant Roads
Red: Level 3 Significant Roads

Recommend printing at A3 (minimum) to show detail.

4					
3					
2					
1	Reference Purposes Only		D Wood		25/1/19
No	Revision:	Drawn	Job Manager	Project Direction	Date



Although the information displayed has been prepared with care and in good faith, this map is designed to be illustrative only. The council cannot guarantee the accuracy or completeness of the information and accepts no liability for any loss suffered as a result of reliance on it. Property boundary/Asset display may not be survey accurate, and can only be verified by a registered surveyor.
This map is drawn on the New Zealand Transverse Mercator projection, using New Zealand Geodetic Datum 2000
Cadastral information sourced from Land Information New Zealand: Crown Copyright Reserved.
Aerial photography flown over Jan-Mar 2008/10. Copyright 2008/10 Hutt City Council and New Zealand Aerial Mapping Limited.

14 November 2024

Drawn: D Wood	Designer: D Wood	Project: Hutt City Roads of Significance. (Roads which require TMC approval)
Drafting Check	Design Check	
Approved (Project Director)	D Simmons	
Date		
Scale: (Not to Scale)		Original Size A3

Methodology:

PEDESTRIAN PROVISION


Detail:

FOOTPATH CLOSED - PEDESTRIANS ESCORTED

Restrictions:

ROAD LEVEL:
ALL**SPEED LIMIT:**
ALL**ATMS05**

STMS to consider if additional safety measures are appropriate to protect hazards / guide pedestrians past the site e.g. safety fencing / cone bars. This is particularly important around excavations. In some instances requirements may change between attended and unattended sites.

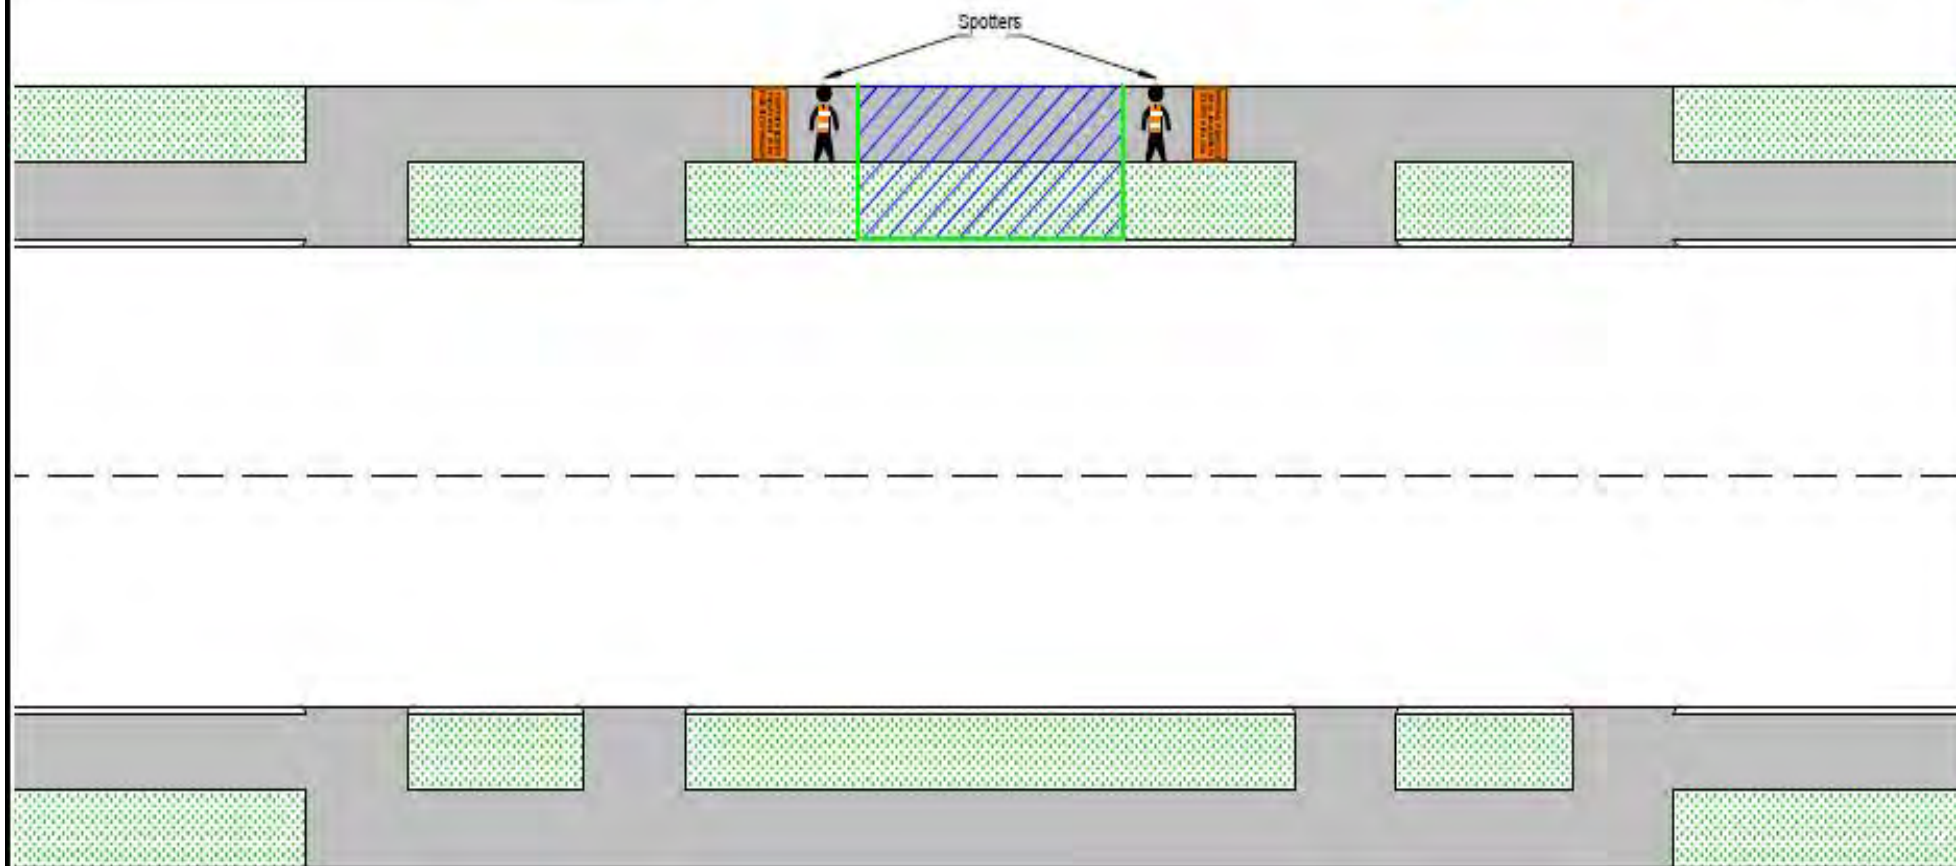**Notes:**

- One spotter can be used over short distances where they can suitably control pedestrians through the working space i.e. 20m.
- This plan can ONLY be used during attended times.

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council

14 November 2024

**FOOTPATH CLOSED
PLEASE WAIT TO BE
ESCORTED THROUGH**

FOOTPATH


Footpath diverted onto berm behind working space

First preference

F2.1
Level 1

Notes

1. Minimum pedestrian footpath widths:
 - Residential/Rural/Suburban Centre - 1.2m
 - CBD - 2m
2. Where the length of the temporary footpath exceeds 20m, these widths may have to be increased so footpath users do not have to wait to pass
3. Temporary footpath surfaces must be suitable for footpath users
4. Use safety fence to enclose the working space, or at attended worksites, cones connected with cone bars can be used to enclose the working space but only for a short period of time
Note: Cone bars are not recommended where heavy equipment (eg a digger) is being used. A safety fence is preferred in these cases
5. This TMD must be used in conjunction with appropriate TTM for any work carried out on the shoulder or in the live lane

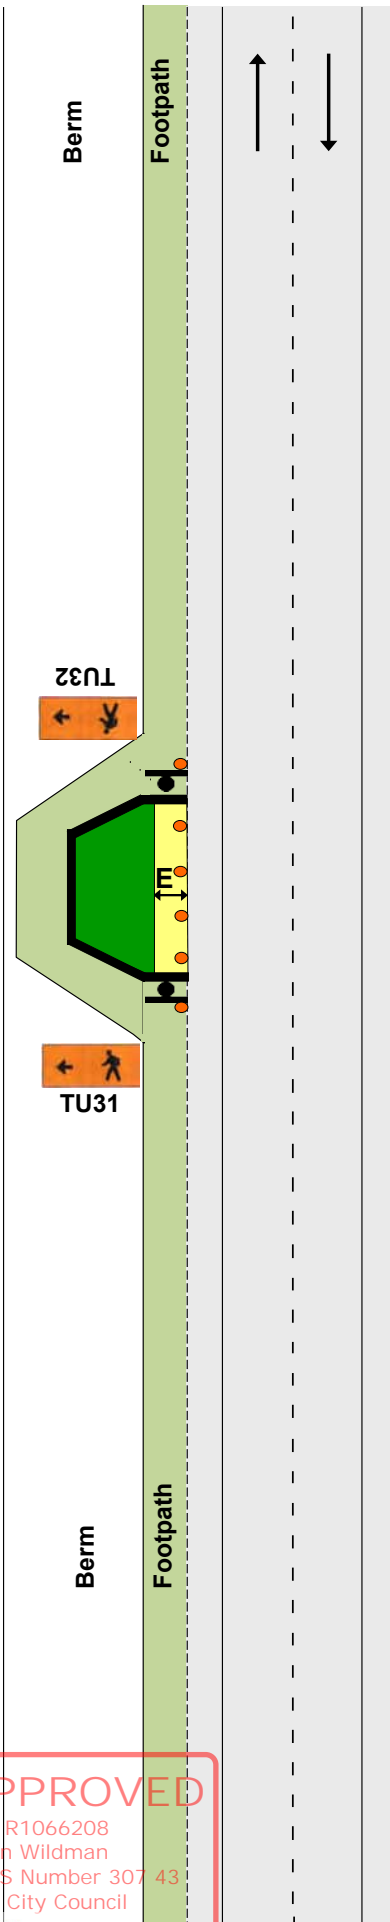

APPROVED

CAR R1066208
 Jason Wildman
 STMS Number 307 43
 Hutt City Council

Section F

14 November 2024


FOOTPATH

Footpath diverted onto berm between working space and carriageway
Second preference

F2.2
Level 1

Notes

1. Minimum pedestrian footpath widths:
 - Residential/Rural/Suburban Centre - 1.2m
 - CBD - 2m
2. Where the length of the temporary footpath exceeds 20m, these widths may have to be increased so footpath users do not have to wait to pass
3. Temporary footpath surfaces must be suitable for footpath users
4. Use safety fence to enclose the working space, or at attended worksites, cones connected with cone bars can be used to enclose the working space but only for a short period of time
Note: Cone bars are not recommended where heavy equipment (eg a digger) is being used. A safety fence is preferred in these cases
5. Use barrier or safety fence to delineate the traffic side of the footpath, or at attended worksites cones connected with cone bars can be used to delineate the traffic side of the footpath for a short period of time (not for use on state highways)
6. There must be a lateral safety zone between the traffic side of the footpath and the live lane:
 - 0.5m for barrier
 - 1m for safety fence or cone bars
7. This TMD must be used in conjunction with appropriate TTM for any work carried out on the shoulder or in the live lane

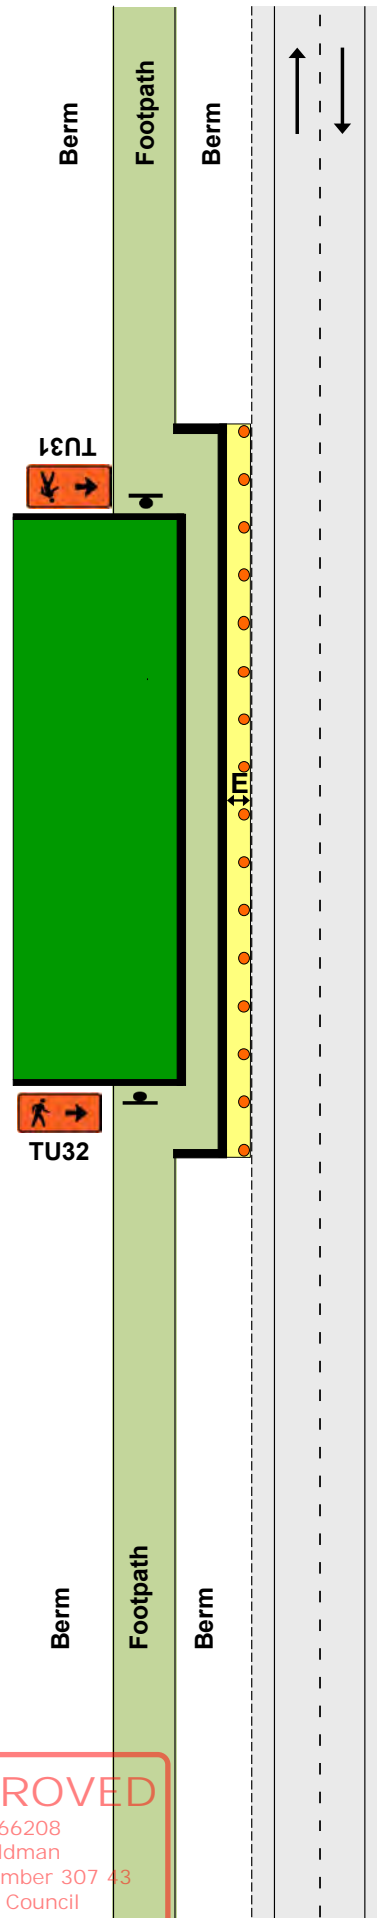

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council

Jason Wildman

14 November 2024

Section F

FOOTPATH


Footpath diverted onto carriageway

Third preference

F2.3
Level 1

Notes

1. Minimum pedestrian footpath widths:
 - Residential/Rural/Suburban Centre - 1.2m
 - CBD - 2m
2. Where the length of the temporary footpath exceeds 20m, these widths may have to be increased so footpath users do not have to wait to pass
3. Use safety fence to enclose the working space, or at attended worksites, cones connected with cone bars can be used to enclose the working space but only for a short period of time
Note: Cone bars are not recommended where heavy equipment (eg a digger) is being used. A safety fence is preferred in these cases
4. Use barrier or safety fence to delineate the traffic side of the footpath, or at attended worksites cones connected with cone bars can be used to delineate the traffic side of the footpath for a short period of time (not for use on state highways)
5. There must be a lateral safety zone between the traffic side of the footpath and the live lane:
 - 0.5m for barrier
 - 1m for safety fence or cone bars
6. Use kerb ramps to assist mobility vehicles, pushchairs, etc
7. At night-time, corners of safety fence may be illuminated with flashing amber warning lights
8. This TMD must be used in conjunction with appropriate TTM for any work carried out on the shoulder or in the live lane

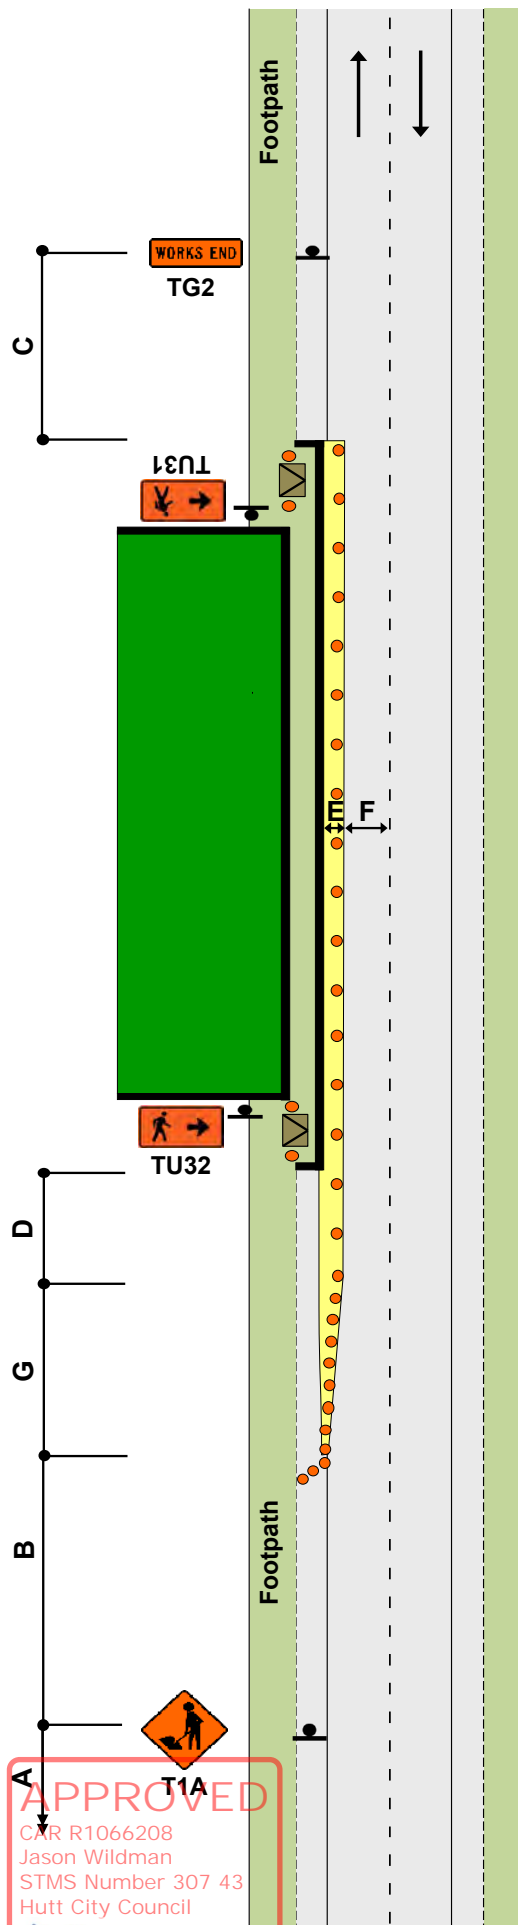

FOOTPATH

Footpath closed - permanent speed less than 65km/h


Fourth preference

F2.4

Level 1

Notes

1. Use T2A and PEDESTRIANS supplementary plate to alert road users to the potential of footpath users crossing the carriageway
2. Use safety fence at each end of working space
3. Use kerb ramps
4. Use another TMD as well, where working space/safety zone encroaches on live lane
5. This TMD must be used in conjunction with appropriate TTM for any work carried out on the shoulder or in the live lane

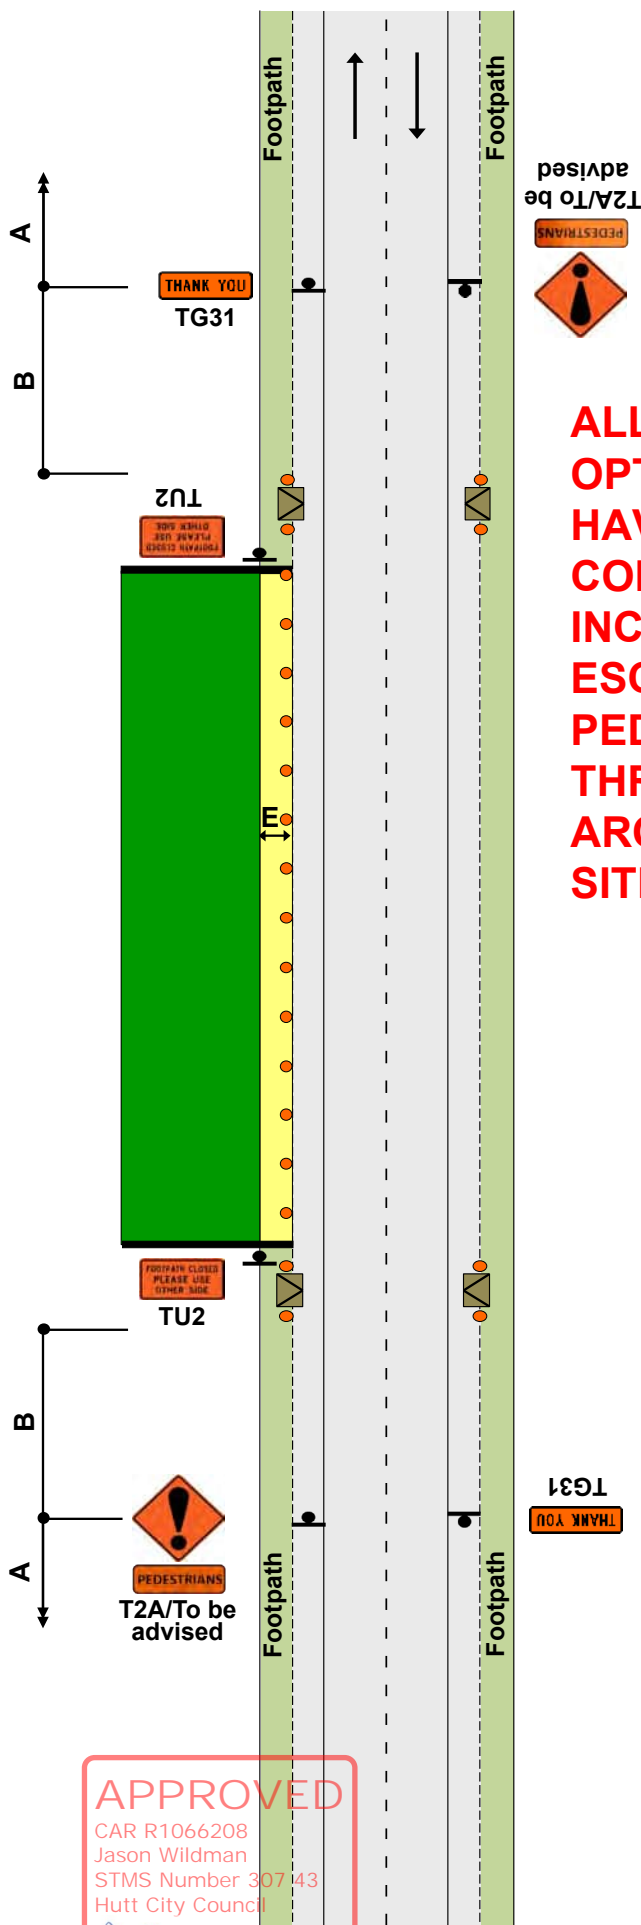

**ALL OTHER
OPTIONS TO
HAVE BEEN
CONSIDERED
INCLUDING
ESCORTING
PEDESTRIANS
THROUGH/
AROUND THE
SITE**


APPROVED

CAR R1066208
Jason Wildman
STMS Number 30743
Hutt City Council

Wildman
14 November 2024

Section F

2. CC2 Traffic not crossing road centre - heavy vehicle parked in carriageway

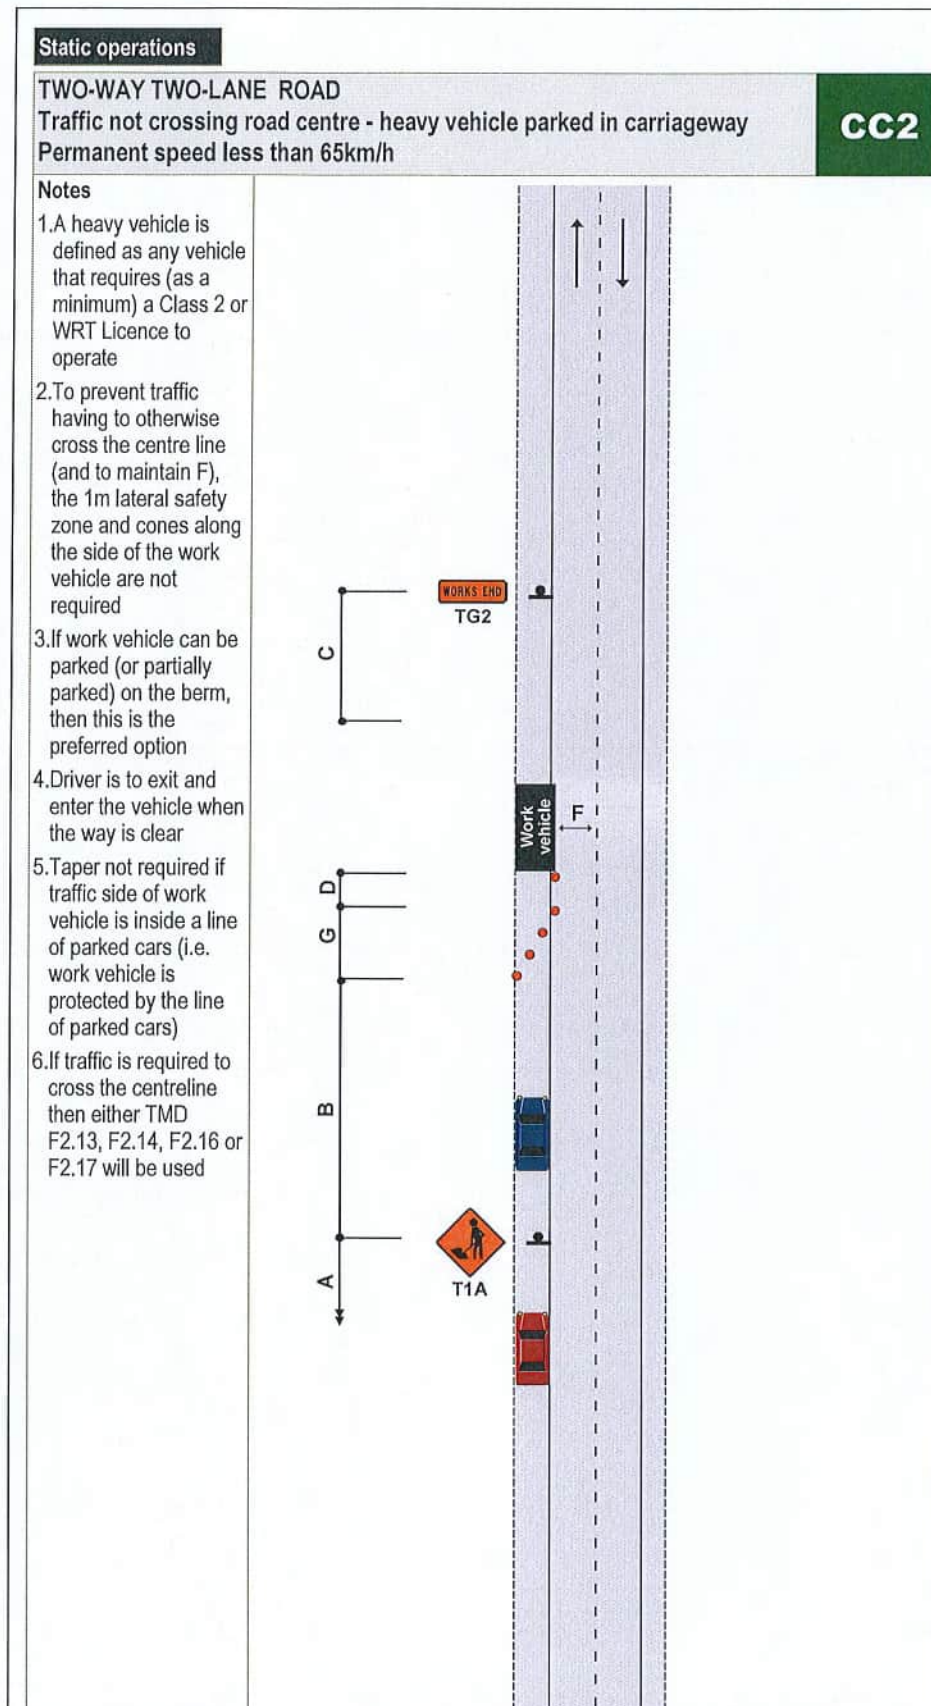

APPROVED

CAR R1066208

Jason Wildman

STMS Number 307 43

Hutt City Council

John

14 November 2024

CC7 - Valve in shoulder or on berm

Mobile operations

TWO-WAY TWO-LANE ROAD


Personnel on berm - Valve in shoulder or on berm

50km/h or less

CC7
Level 1

Notes

1. The vehicle must be able to be driven with a Class 1 drivers license
2. There must be clear sight distance to the vehicle of at least 75m. This means that this operation cannot be completed within 75m of a corner or the brow of a hill
3. Worker to exit and enter the vehicle when there is a gap in traffic
4. The worker must not work within 10m of the vehicle (10m roll ahead)

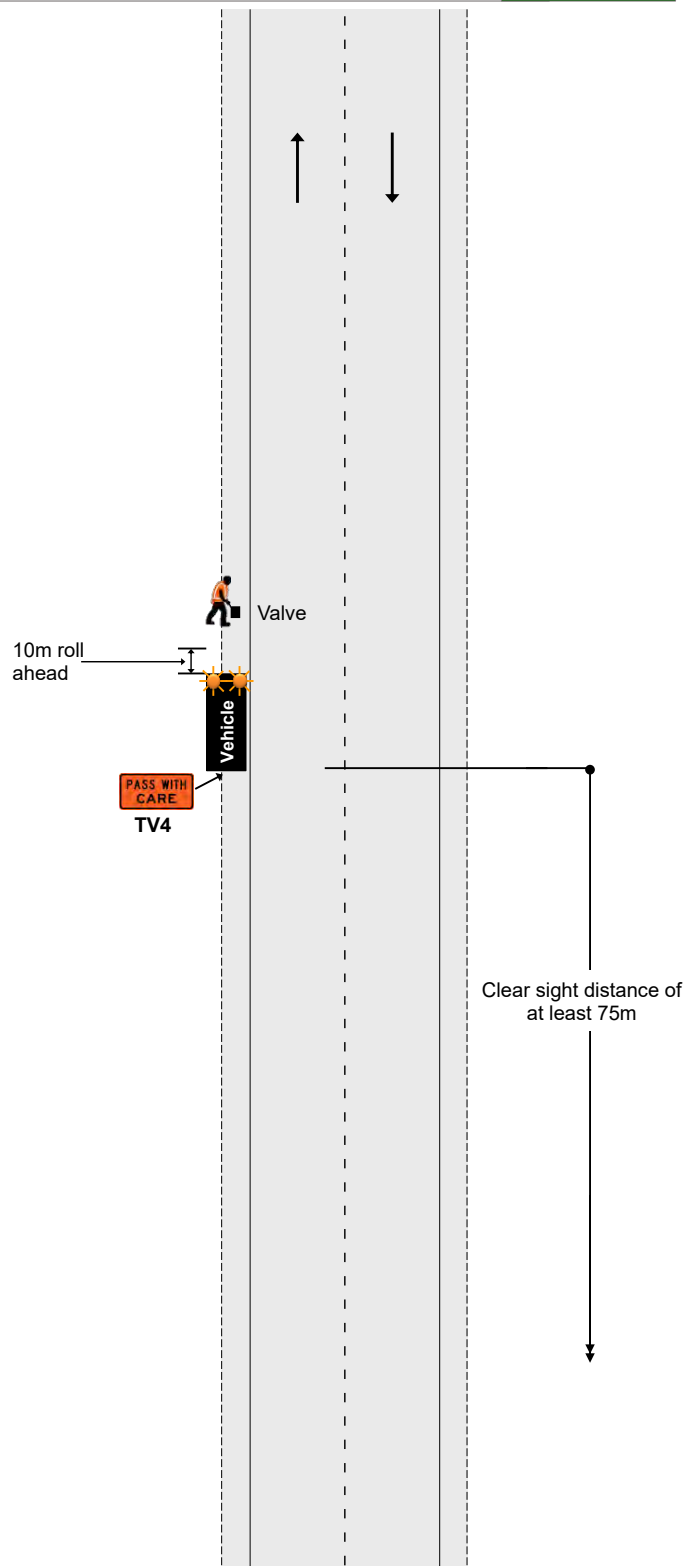

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43

14 November 2024

SHOULDER AND ROADSIDE ACTIVITIES


Work on berm and/or footpath

Permanent speed less than 65km/h

F2.5
Level 1

Notes

1. Where work is carried out on the berm or footpath and a work vehicle is parked in a legal parallel car park, provided the vehicle is only accessed from the off traffic side, advance warning T1A road works and TG2 WORKS END are optional
2. Traffic management must be provided where footpath users or cyclists are affected
3. This layout may only be used during daylight hours
4. Large plant and machinery must not be used in this situation, a more substantial closure is required

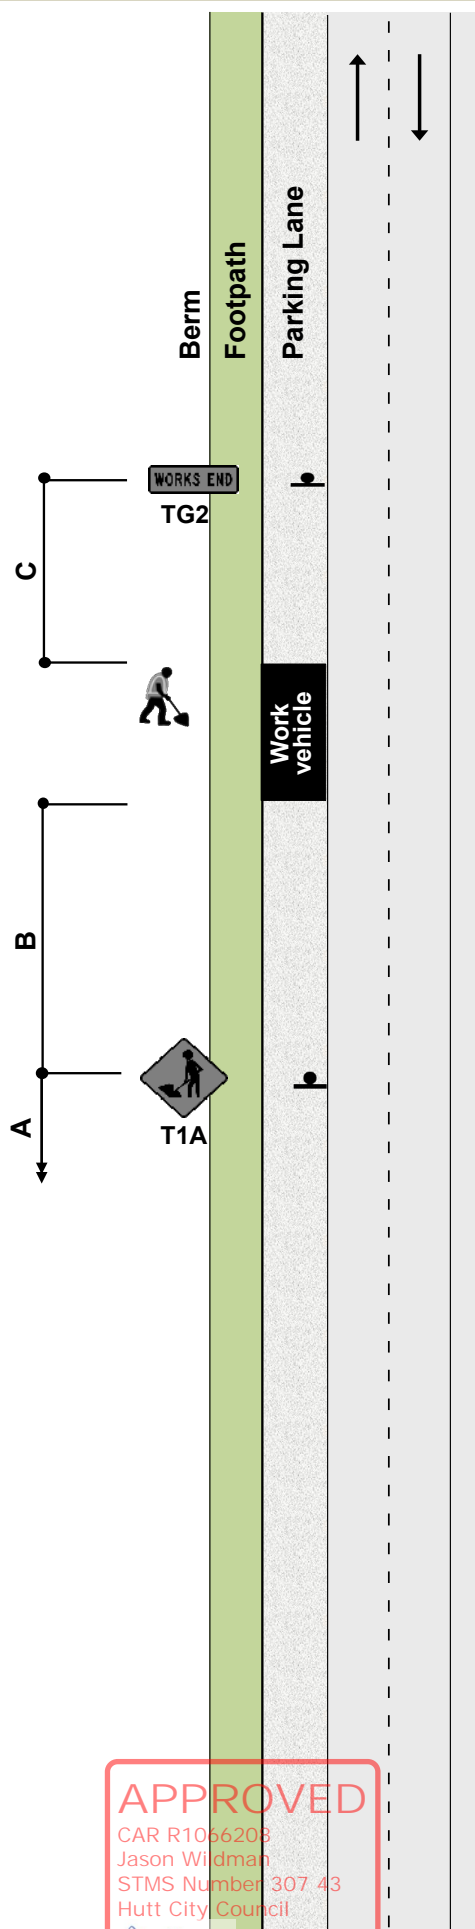

APPROVED

CAR R1066208
 Jason Wildman
 STMS Number 307 43
 Hutt City Council

Jason Wildman

14 November 2024

Section F

SHOULDER AND ROADSIDE ACTIVITIES

Work in parking lane

Permanent speed less than 65km/h

F2.6
Level 1

Notes

1. Where work is carried out in the legal parking lane (a place where a vehicle would normally park with a footpath and/or kerb and channel alongside), the following minimum standard of TTM must be provided:

- a 10m taper in front of the work vehicle
- cones alongside the work vehicle and the working space
- a longitudinal safety zone
- a 1m lateral safety zone along the working space
- a T1A (or other appropriate advance warning sign) mounted on the back of the work vehicle


2. T1A road works and TG2 WORKS END signs are optional

3. The work vehicle must be no larger than a light truck and may have an amber flashing beacon

4. Traffic management must be provided where footpath users or cyclists are affected

5. This layout may only be used during daylight hours

6. Large plant and machinery must not be used in this situation, a more substantial closure is required

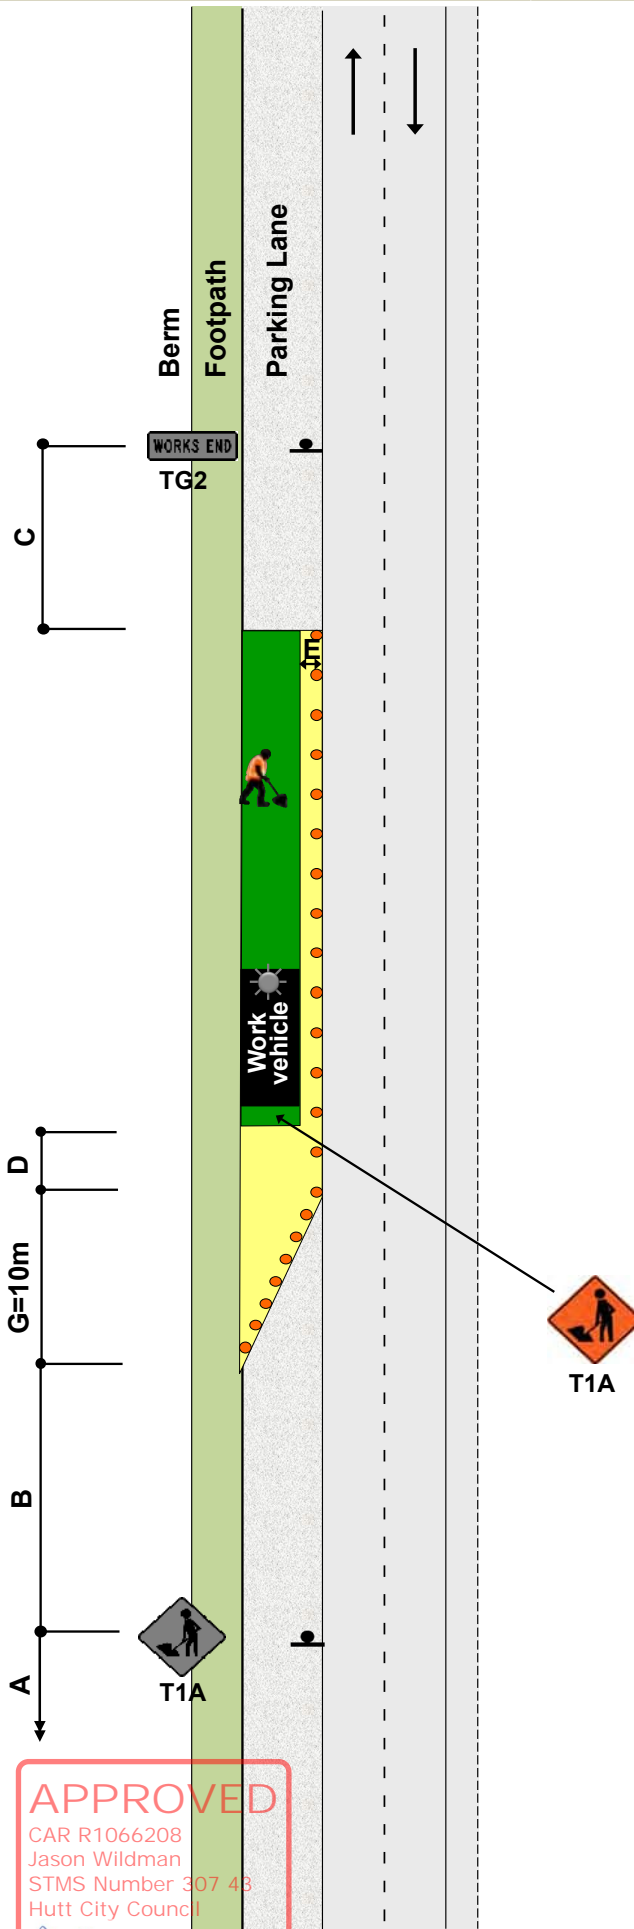

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council

Wildman
14 November 2024

Section F

SHOULDER AND ROADSIDE ACTIVITIES

Shoulder closure

F2.7

Level 1

Notes

1. A 10m taper is allowed where shoulder width is less than 2.5m
2. *For shoulders exceeding 2.5m width, apply the following calculation; calculation of taper length for lateral shift of less than 3.5m is:


$$\frac{W \times G}{3.5}$$

3.5

W = Width of shoulder

G = Taper length in metres from the level 1 layout distance table

1 layout distance table

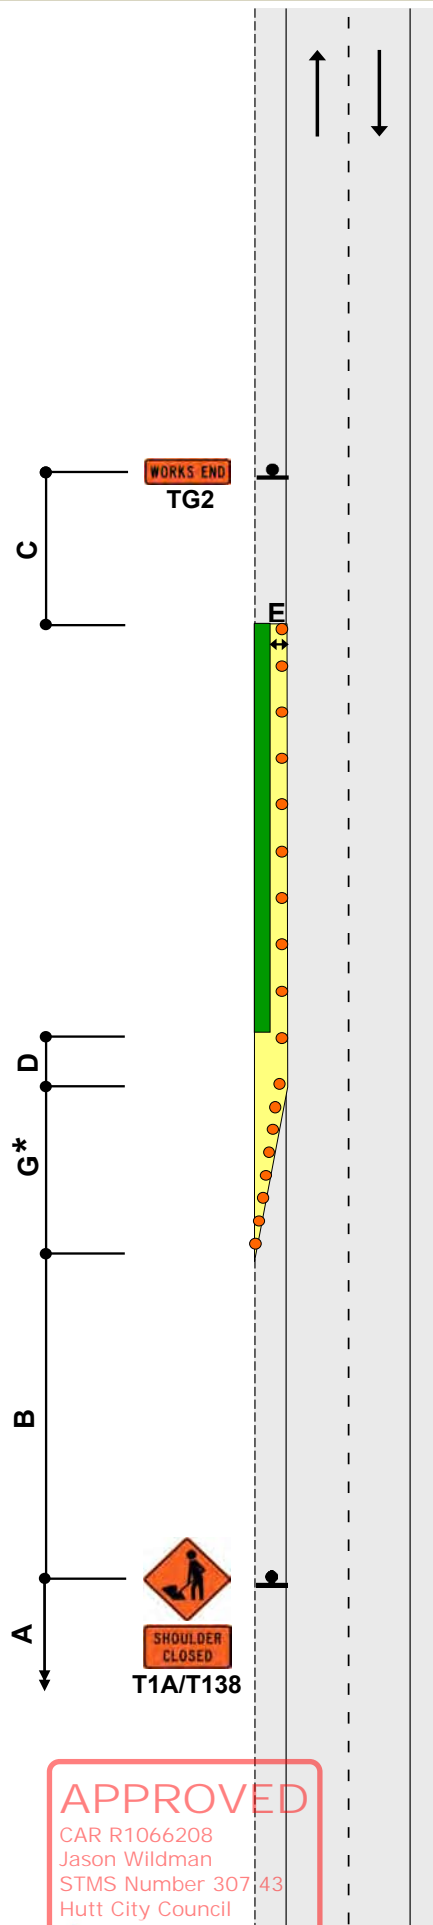


Static operations

TWO-WAY TWO-LANE ROAD
Traffic not crossing road centre

F2.11
Level 1

Notes

- 1.*Calculation of taper length for lateral shift of less than 3.5m is:
 $W \times G$
3.5
W = Width of lateral shift
G = Taper length in metres from the level 1 layout distance table
- 2.If traffic likely to cross the centreline, place cones on the centreline with RD6L signs at each end
- 3.Use TSLs if required by TSL decision matrix
- 4.If TSLs not required, the T1A and TG2 signs on the right hand side of the road are also not required
- 5.The T144 X0km/h AHEAD sign is optional

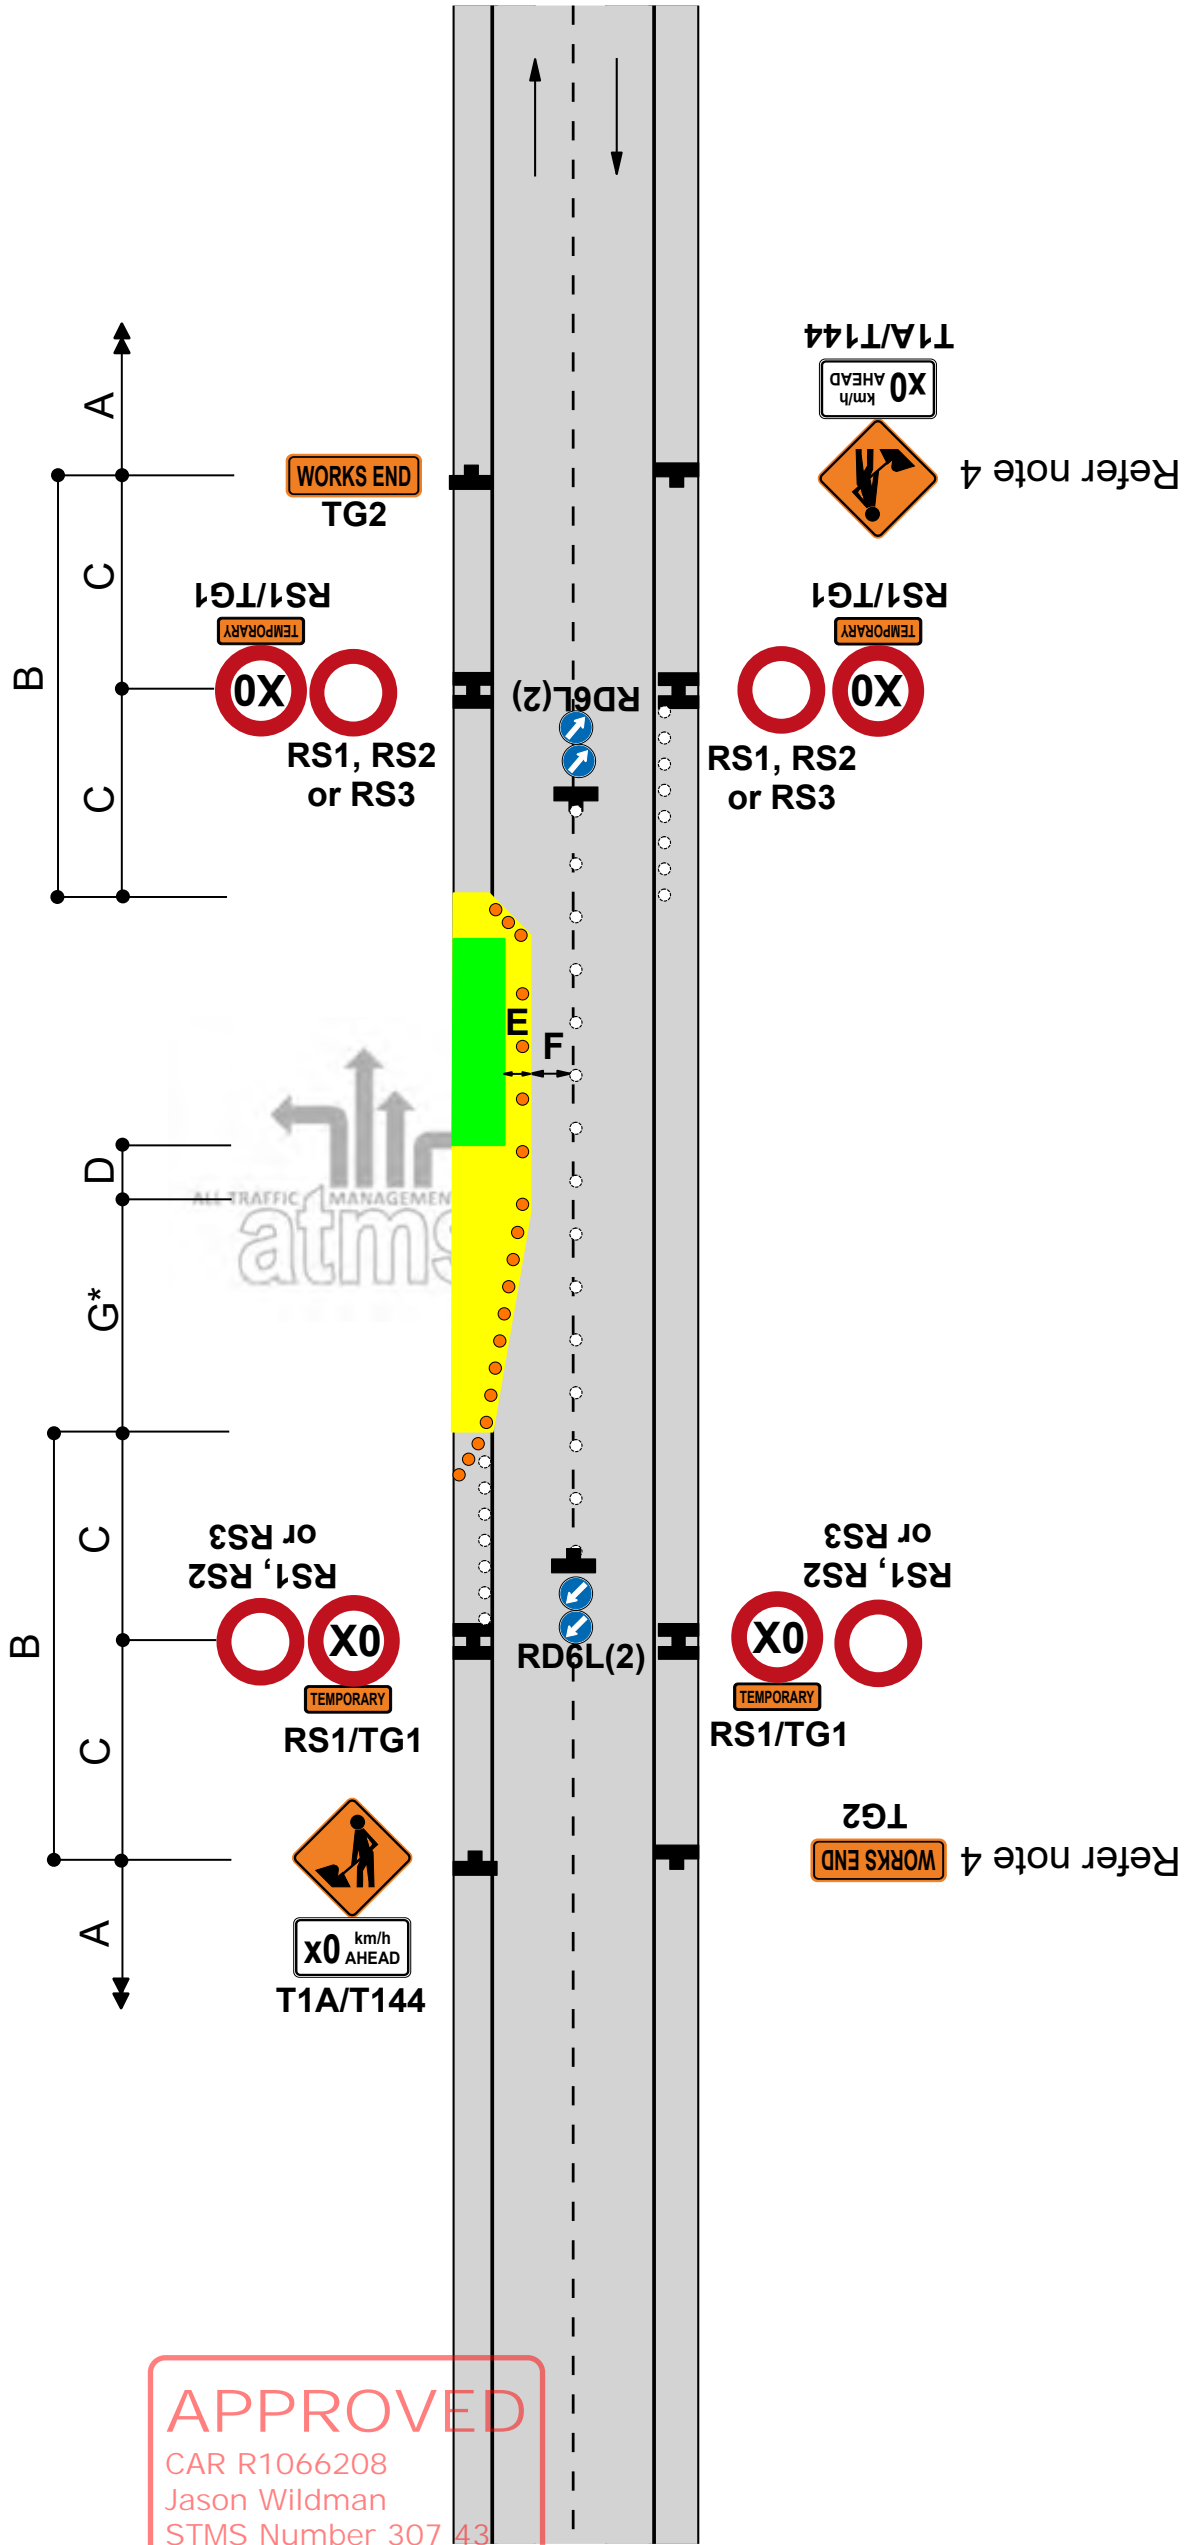

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council

14 November 2024

TWO-WAY TWO-LANE ROAD
Traffic not crossing road centre
Signs on median


F2.12
Level 1

Notes

1. Use this diagram if signs will not be visible on left-hand side of road, or if it is safer to place signs on median and this will not interfere with turning traffic movements
2. Where a median exists which is more than 2m wide, the signs may be positioned on the median. Signs must be placed back-to-back unless on a solid median
3. Where there is a solid median, signs are not required in the opposing direction
4. *Calculation of taper length for lateral shift of less than 3.5m is:

$$\frac{W \times G}{3.5}$$

 W = Width of lateral shift
 G = Taper length in metres from the level 1 layout distance table
5. Use TSLs if required by TSL decision matrix
6. The T144 X0km/h AHEAD sign is optional

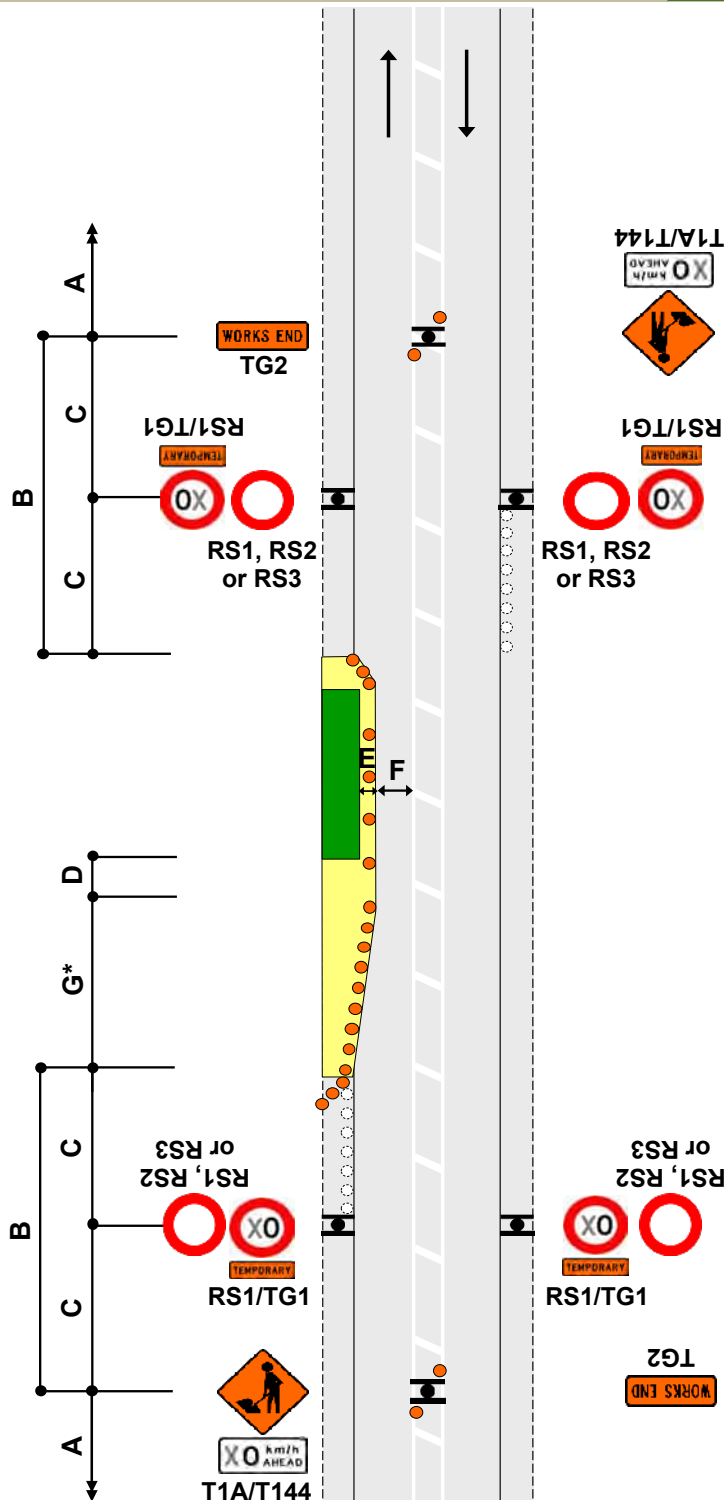

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council

Jason Wildman

14 November 2024

Section F

INSPECTION ACTIVITIES AND NON-INVASIVE WORKS

On shoulder and on the live lane

This TMD may also be applied on level LV roads


F4.10

Level 1

Notes

1. Inspectors must move from live lanes to avoid traffic. They must not expect traffic to drive slowly or drive around them
2. On level LV and level 1 roads, a person completing an inspection or non-invasive works cannot be on a live lane for more than 5 minutes
3. Unless otherwise approved by the RCA, all inspections on the live lane of level 1 roads require a spotter. The RCA may provide a list of roads, times and/or activities suitable for inspection by a single inspector
4. There must be CSD to the inspector when on the live lane. If this cannot be achieved, a spotter must be placed in a position where CSD can be attained and verbal instructions be given to the inspector. If this is not possible, a static or mobile operation is required.
5. A spotter is not required for inspections and non-invasive works on level LV roads or working off the live lane of a level 1 road
6. Where an unaccompanied inspector is not able to maintain adequate attention (eg due to work tasks or poor visibility), a spotter will be required or another type of traffic management operation used
7. For inspection activities that are carried out by a TC on level LV and level 1 roads the STMS must be immediately contactable but does not have to be within 30 minutes travel time of the worksite
8. An unaccompanied inspector may walk across a level LV or level 1 road
9. A vehicle is not required on a level LV or level 1 road with a permanent speed of less than 65km/h if the inspector remains on a footpath
10. On roads with a permanent speed of less than 65km/h an amber flashing beacon is not required on the vehicle if the inspector or non-invasive works is on an unsealed shoulder (or further away from the carriageway - including a footpath)

Spotter required when inspector on the live lane of a level 1 road (unless RCA has selected the road as suitable for 'single inspector' inspections)

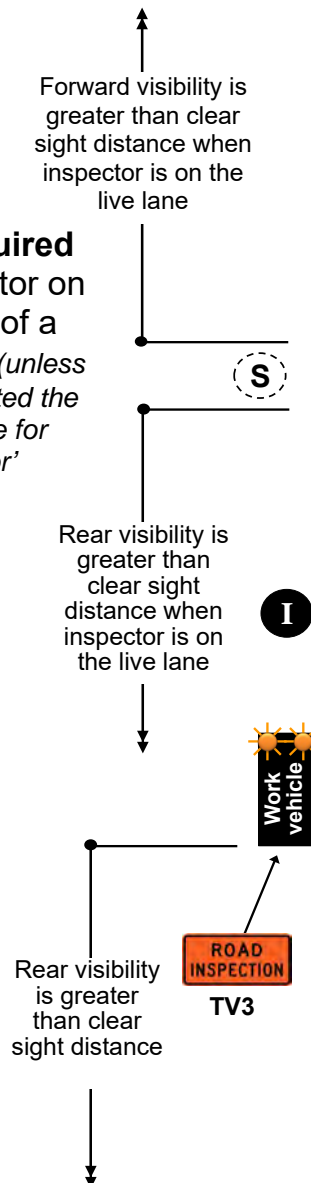

APPROVED

CAR R1066208
 Jason Wildman
 STMS Number 307 43
 Hutt City Council


Section F

14 November 2024

Mobile operations

INSPECTION ACTIVITIES AND NON-INVASIVE WORKS**Inspection Activity - Centre Of Road****This TMD may also be applied on level LV roads****ATMS07****Level 1****Notes**

1. Inspectors must move from live lanes to avoid traffic. They must not expect traffic to drive slowly or drive around them
2. On level LV and level 1 roads, a person completing an inspection or non-invasive works cannot be on a live lane for more than 5 minutes
3. Unless otherwise approved by the RCA, all inspections on the live lane of level 1 roads require a spotter. The RCA may provide a list of roads, times and/or activities suitable for inspection by a single inspector
4. There must be CSD to the inspector when on the live lane. If this cannot be achieved, a spotter must be placed in a position where CSD can be attained and verbal instructions be given to the inspector. If this is not possible, a static or mobile operation is required.
5. Where an unaccompanied inspector is not able to maintain adequate attention (eg due to work tasks or poor visibility), a spotter will be required or another type of traffic management operation used
6. For inspection activities that are carried out by a TC on level LV and level 1 roads the STMS must be immediately contactable but does not have to be within 30 minutes travel time of the worksite
7. Inspectors MUST use 2 vehicles placed on either side of road shoulder. Inspector & spotter will use footpath to carry cones and cross when way is clear. Cones will be placed (min of 4 each direction) for protection. Spotter must not engage in work activities.

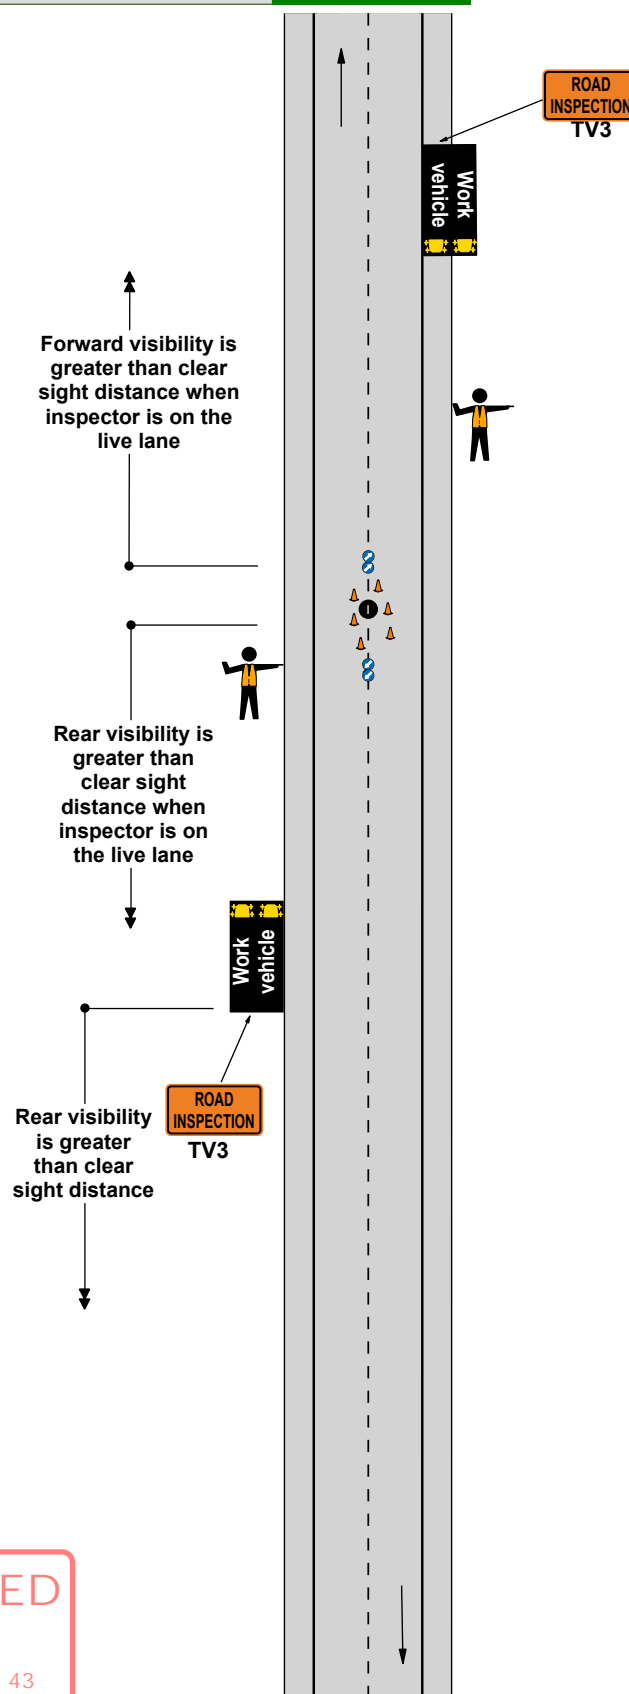**APPROVED**

CAR R1066208
 Jason Wildman
 STMS Number 307 43
 Hutt City Council

14 November 2024

TWO-WAY TWO-LANE ROAD

Single-lane alternating flow

Portable e-STOP

ATMS02
Level 1

Notes THIS TMD IS NOT TO BE USED FOR ANY UNATTENDED PERIOD

1. Provide details of make and model of portable traffic signals in the TMP

2. Use PN11 no stopping signs, if necessary as per the approved TMP

3. Install temporary RP61/RP62 signs



4. Minimum 5 cones in cone threshold.


5. Extend or place extra advance warning signs towards on-coming traffic beyond any expected traffic queues

6. CONTINGENCY PLAN:
F2.14 to be implemented should issues arise with e-STOP/ adverse weather conditions or where stop go is unsuitable.
ex; Short term stoppages is defined as "stopping traffic for a short period of time within a static site, at inconsistent intervals to assist with the entry/exit of vehicles or small tasks required to be undertaken in the live lane".

7. In circumstances where for safety reasons, the use of stop/go operations is deemed more appropriate, a site specific safe work method statement must be prepared.

8. The T144 30km/h AHEAD sign is optional on roads under 65km/h

9. e-STOP can only be used on an attended site. e-STOPS must be manned at all times.

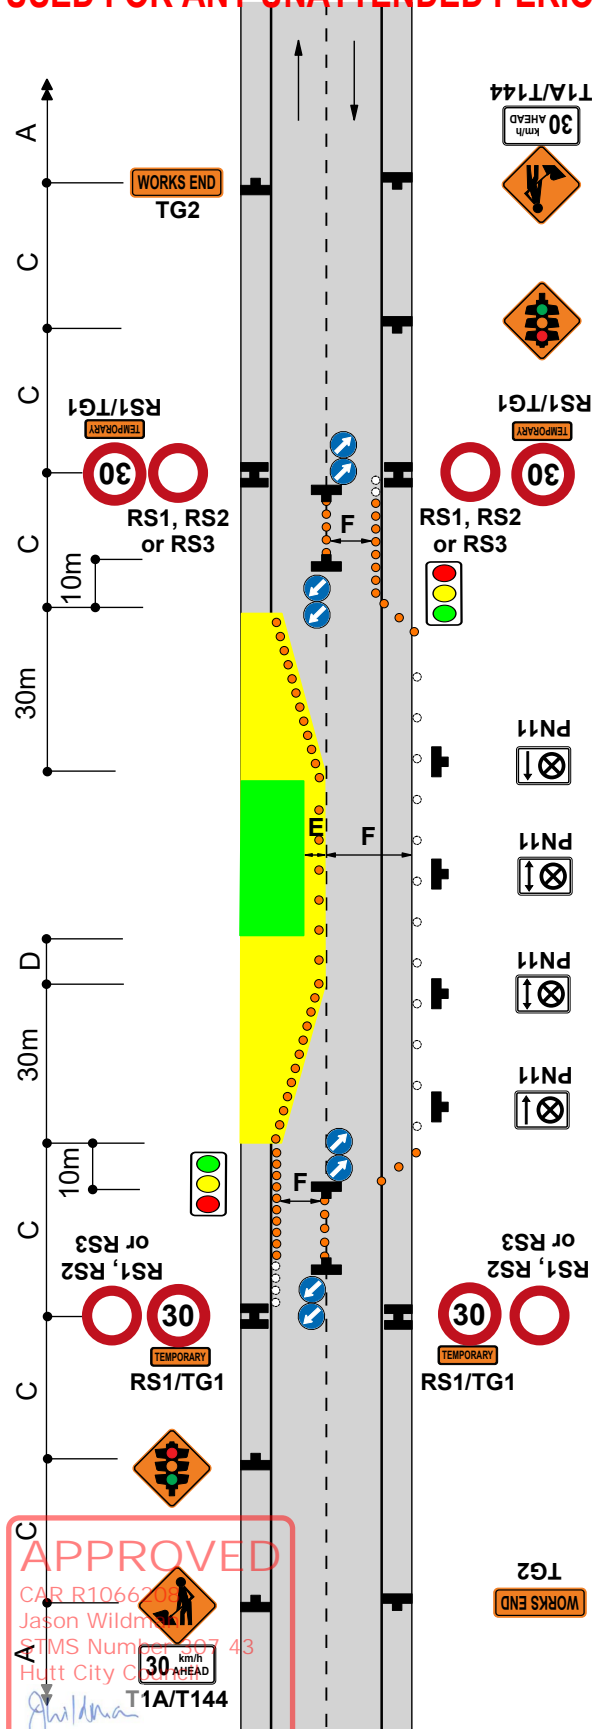


APPROVED
CAR R10662
Jason Wildman
ATMS Number 107 43
Hutt City Council
T1A/T144

14 November 2024

Static operations
TWO-WAY TWO-LANE ROAD
Single-lane alternating flow
Manual traffic control (STOP/GO or STOP/SLOW)
F2.14
Level 1
Notes

1. Extend or place extra advance warning signs towards on-coming traffic beyond any expected traffic queues
2. A 30m return taper at the end of the closure is mandatory
3. Cones are required on edge of the temporary lane opposite closure if road is not well defined
4. To allow heavy vehicles to manoeuvre, cones in the channel must be offset by at least 10m where the direction changes. Refer C8.2.12
5. Use PN11 no stopping signs, if necessary
6. MTC with RP4/RP41 STOP/GO or RP4/RP42 STOP/SLOW paddle on road shoulder located between 1st and 2nd cone in the cone threshold closest to the working space
7. Minimum 5 cones in cone threshold at:
 - 2.5m centres - less than 65km/h
 - 5m centres - more than 65km/h
8. Refer to C10.2.3 MTC essentials for further information
9. Delays cannot exceed the time approved by the RCA (normally 5 to 10 minutes)
10. The T144 30km/h AHEAD sign is optional

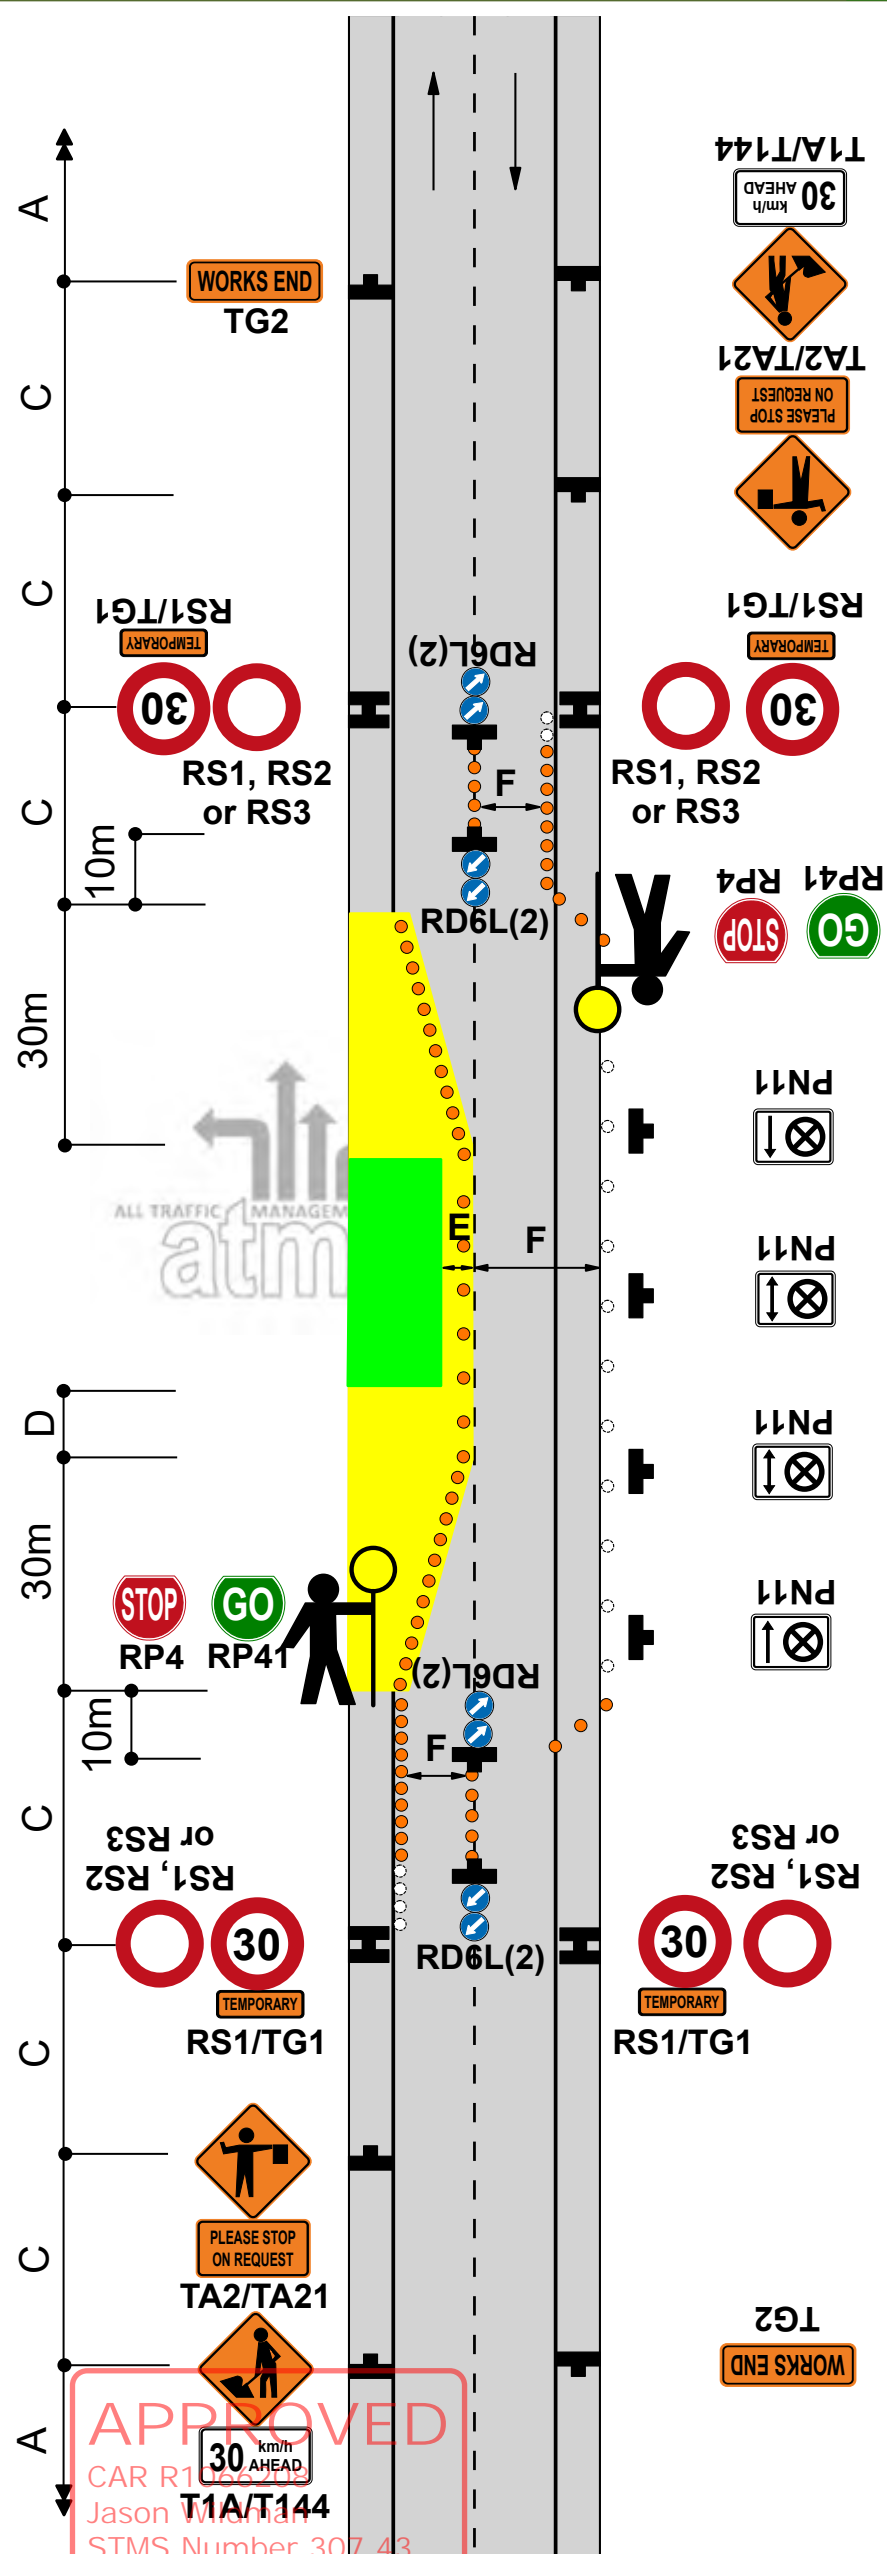
APPROVED

 CAR R1122
 Jason Williams
 STMS Number 307 43
 Hutt City Council

14 November 2024



Static operations


TWO-WAY TWO-LANE ROAD - Intersection or roundabout
Closure at an intersection
Portable e-STOP - with MTC on side roads

ATMS04

Level 1

Notes

- 1.This plan can be used at a 3 way intersection by removing one of the approaches. If you require a temporary traffic light/MTC set up, which is greater than a four way, you will require a site specific TMP.
- 2.Signs and layout shown in the box at the bottom of the diagram is to be repeated on each approach.
- 3.Provide details of make and model of portable traffic signals in the TMP
- 4.Use PN11 no stopping signs, if necessary as per the approved TMP
- 5.Install temporary RP61/RP62 signs

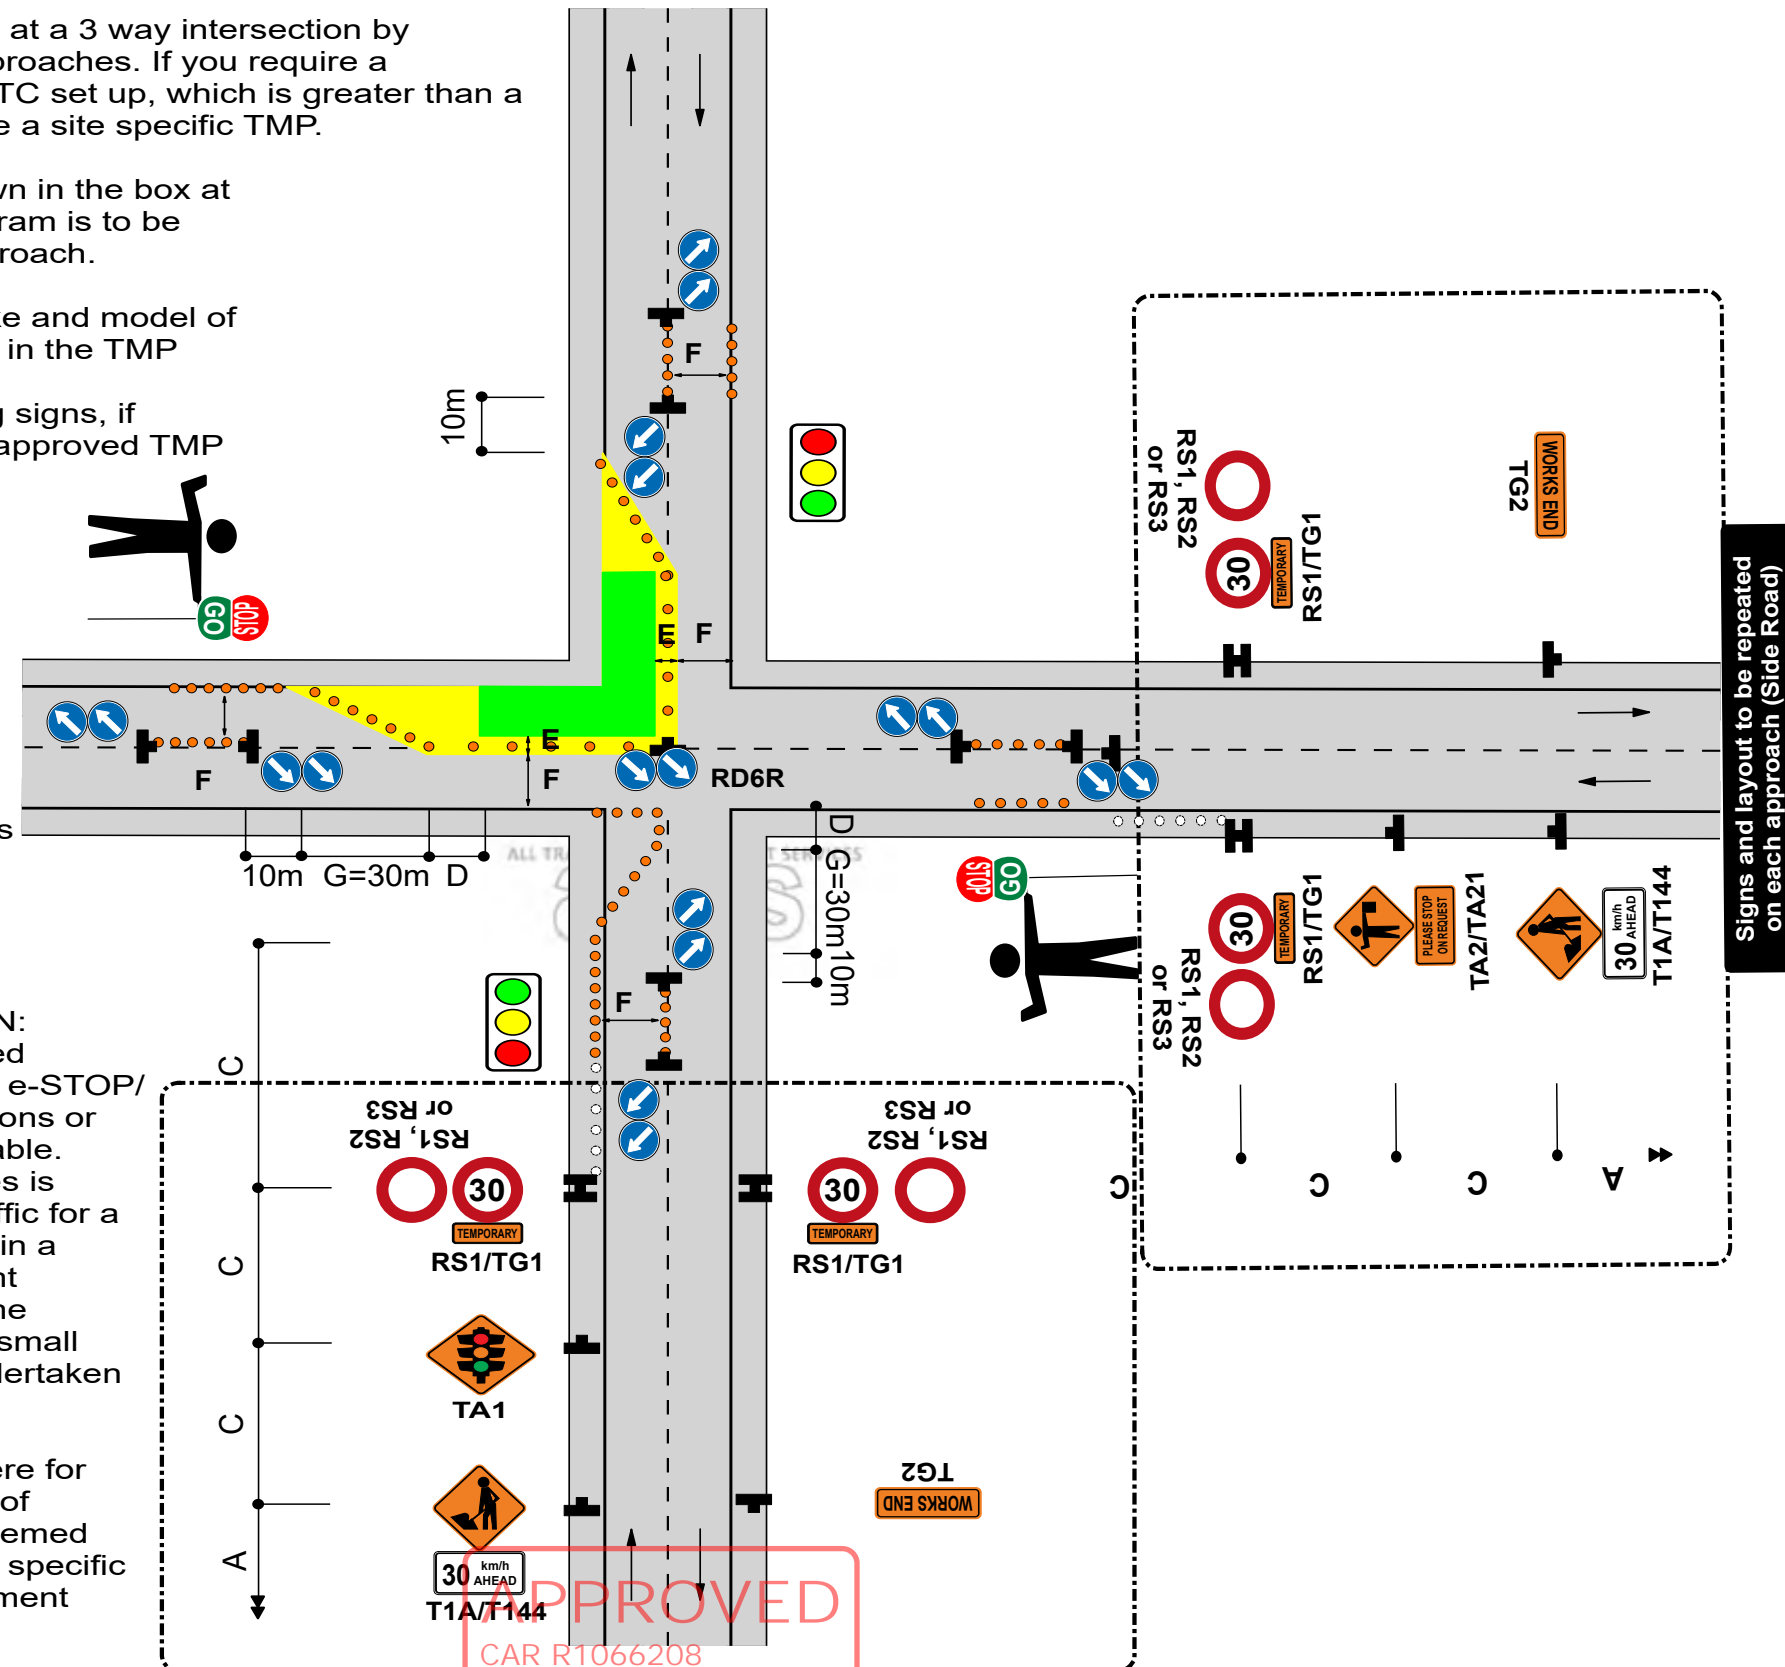- 6.Minimum 5 cones in cone threshold.
7. Extend or place extra advance warning signs towards on-coming traffic beyond any expected traffic queues
- 8.CONTINGENCY PLAN:
F2.22 to be implemented should issues arise with e-STOP/ adverse weather conditions or where stop go is unsuitable.
ex; Short term stoppages is defined as "stopping traffic for a short period of time within a static site, at inconsistent intervals to assist with the entry/exit of vehicles or small tasks required to be undertaken in the live lane".
9. In circumstances where for safety reasons, the use of stop/go operations is deemed more appropriate, a site specific safe work method statement must be prepared.
- 10.The T144 30km/h AHEAD sign is optional on roads under 65km/h
11. e-STOP can only be used on an attended site. e-STOPS must be manned at all times.



CAR R1066208

Signs and layout to be repeated
on each approach (Main Road)

Hutt City Council

ghildan

14 November 2024


Static operations

TWO-WAY TWO-LANE ROAD - Intersection or roundabout Closure at corner of an intersection Manual traffic control (Stop/Go or Stop/Slow)

F2.22
Level 1

Notes

1. This diagram may be used at a T intersection by removing any one of the roads
2. Signs and layout shown in the box at the bottom of the diagram is to be repeated on each approach
3. A 30m return taper at the end of the closure is mandatory
4. Use PN11 no stopping signs, if necessary
5. MTC with RP4/RP41 STOP/GO or RP4/RP42 STOP/SLOW paddle on road shoulder located between 1st and 2nd cone in the cone threshold closest to the working space
6. Minimum 5 cones in cone threshold at:
 - 2.5m centres - less than 65km/h
 - 5m centres - more than 65km/h
7. Refer to C10.2.3 MTC essentials for further information
8. On roads with a permanent speed limit of 100km/h, cones are required from the TSL to the taper if the speed is reduced by more than 30km/h
9. The T144 30km/h AHEAD sign is optional

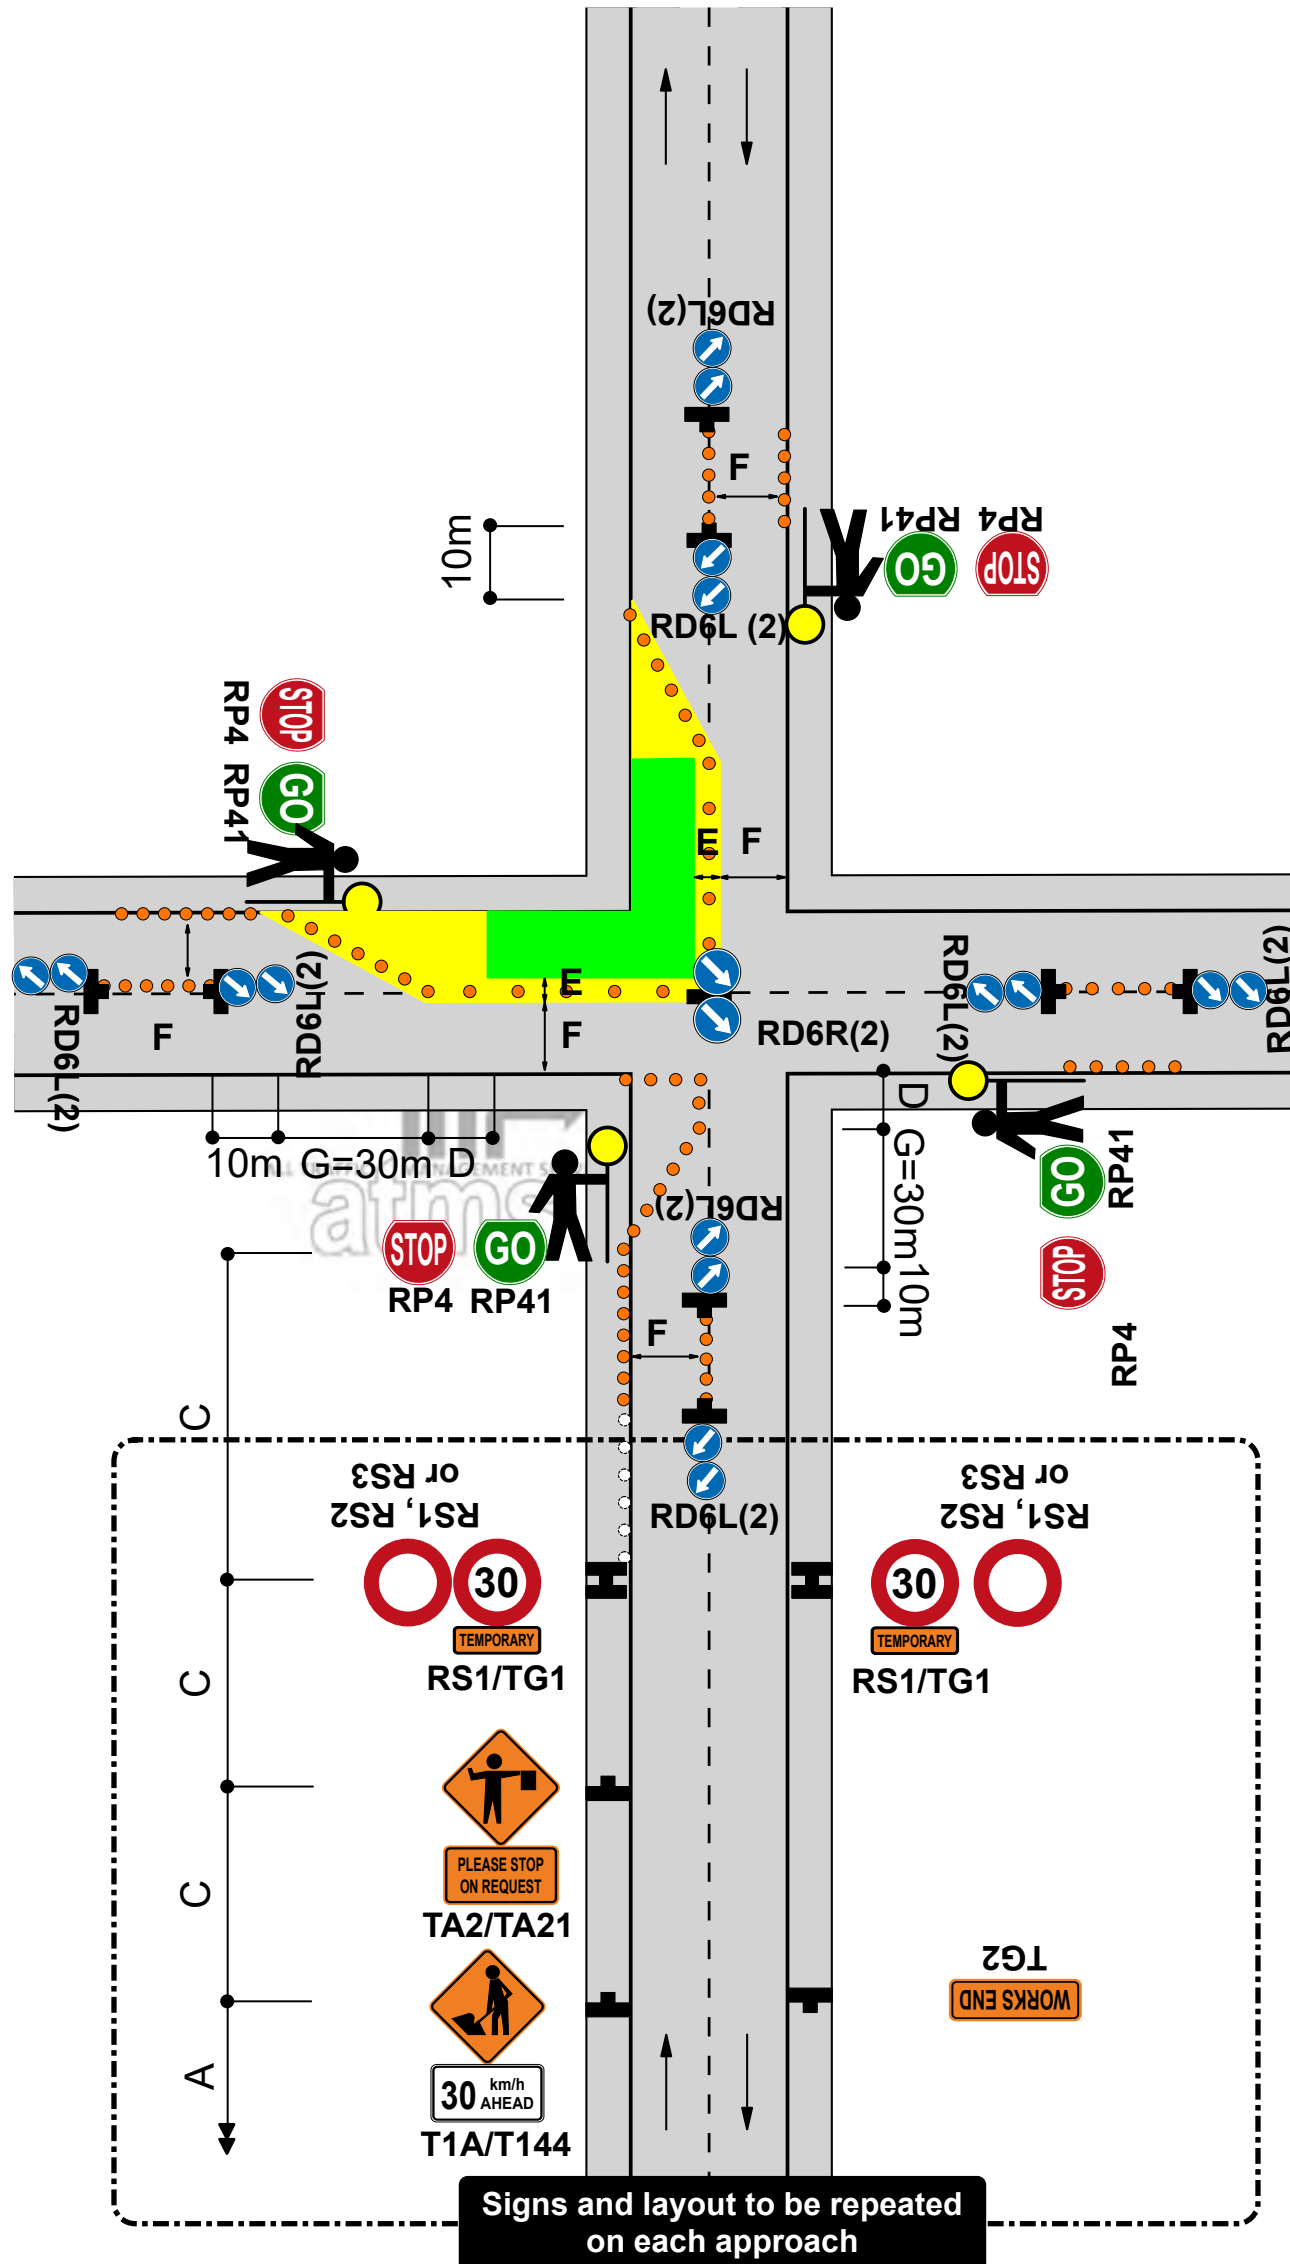

APPROVED


CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council

Wildman

14 November 2024


eSTOPS at locations with limited road width or shoulder
The same risk assessment process should be undertaken for placement of eSTOPS on these types of roads as if a manual traffic controller was to be placed there.

Ideally approval should be sought for a full road closure.
Where this is not possible, placement of the eSTOP on the live lane within a coned area as per the example below should be considered:

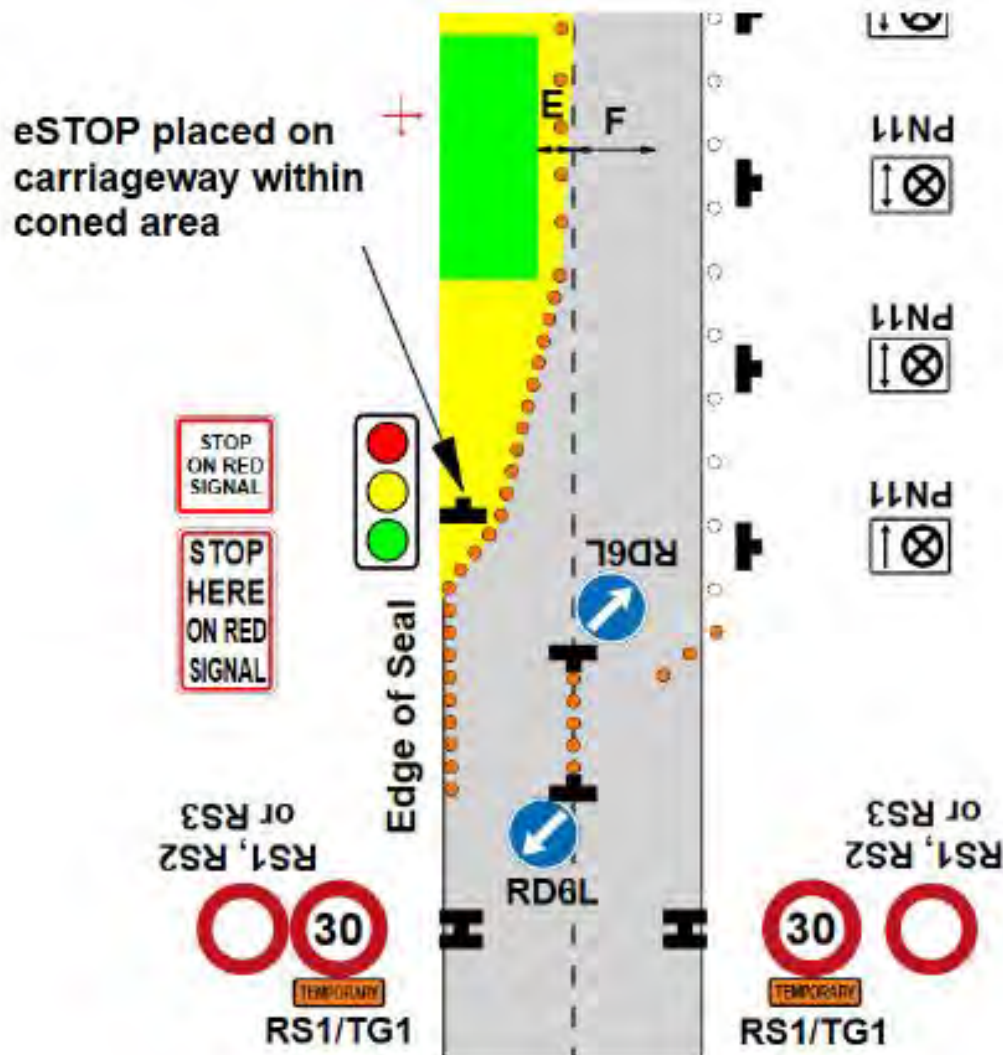

Static operations
TWO-WAY TWO-LANE ROAD
All traffic stopped temporarily
Manual traffic control (STOP/GO or STOP/SLOW)
F2.15
Level 1
Notes

1. Closure period not to exceed the limit set or approved by the RCA
2. Extend advance warning signs towards on-coming traffic beyond any expected traffic queues
3. MTC with RP4/RP41 STOP/GO or RP4/RP42 STOP/SLOW paddle on road shoulder located between 1st and 2nd cone in the cone threshold closest to the working space
4. Minimum 5 cones in cone threshold at:
 - 2.5m centres - less than 65km/h
 - 5m centres - more than 65km/h
5. MTCs must show same message to oncoming traffic (eg STOP/STOP or GO/GO)
6. Refer to C10.2.3 MTC essentials for further information
7. When road users are passing the working space in alternating flow, all construction equipment must be stopped on same side of the road if there is no separation from the live lane
8. Where damage is likely to occur to passing traffic eg during sealing, traffic must be stopped in both directions
9. The T144 X0km/h AHEAD sign is optional

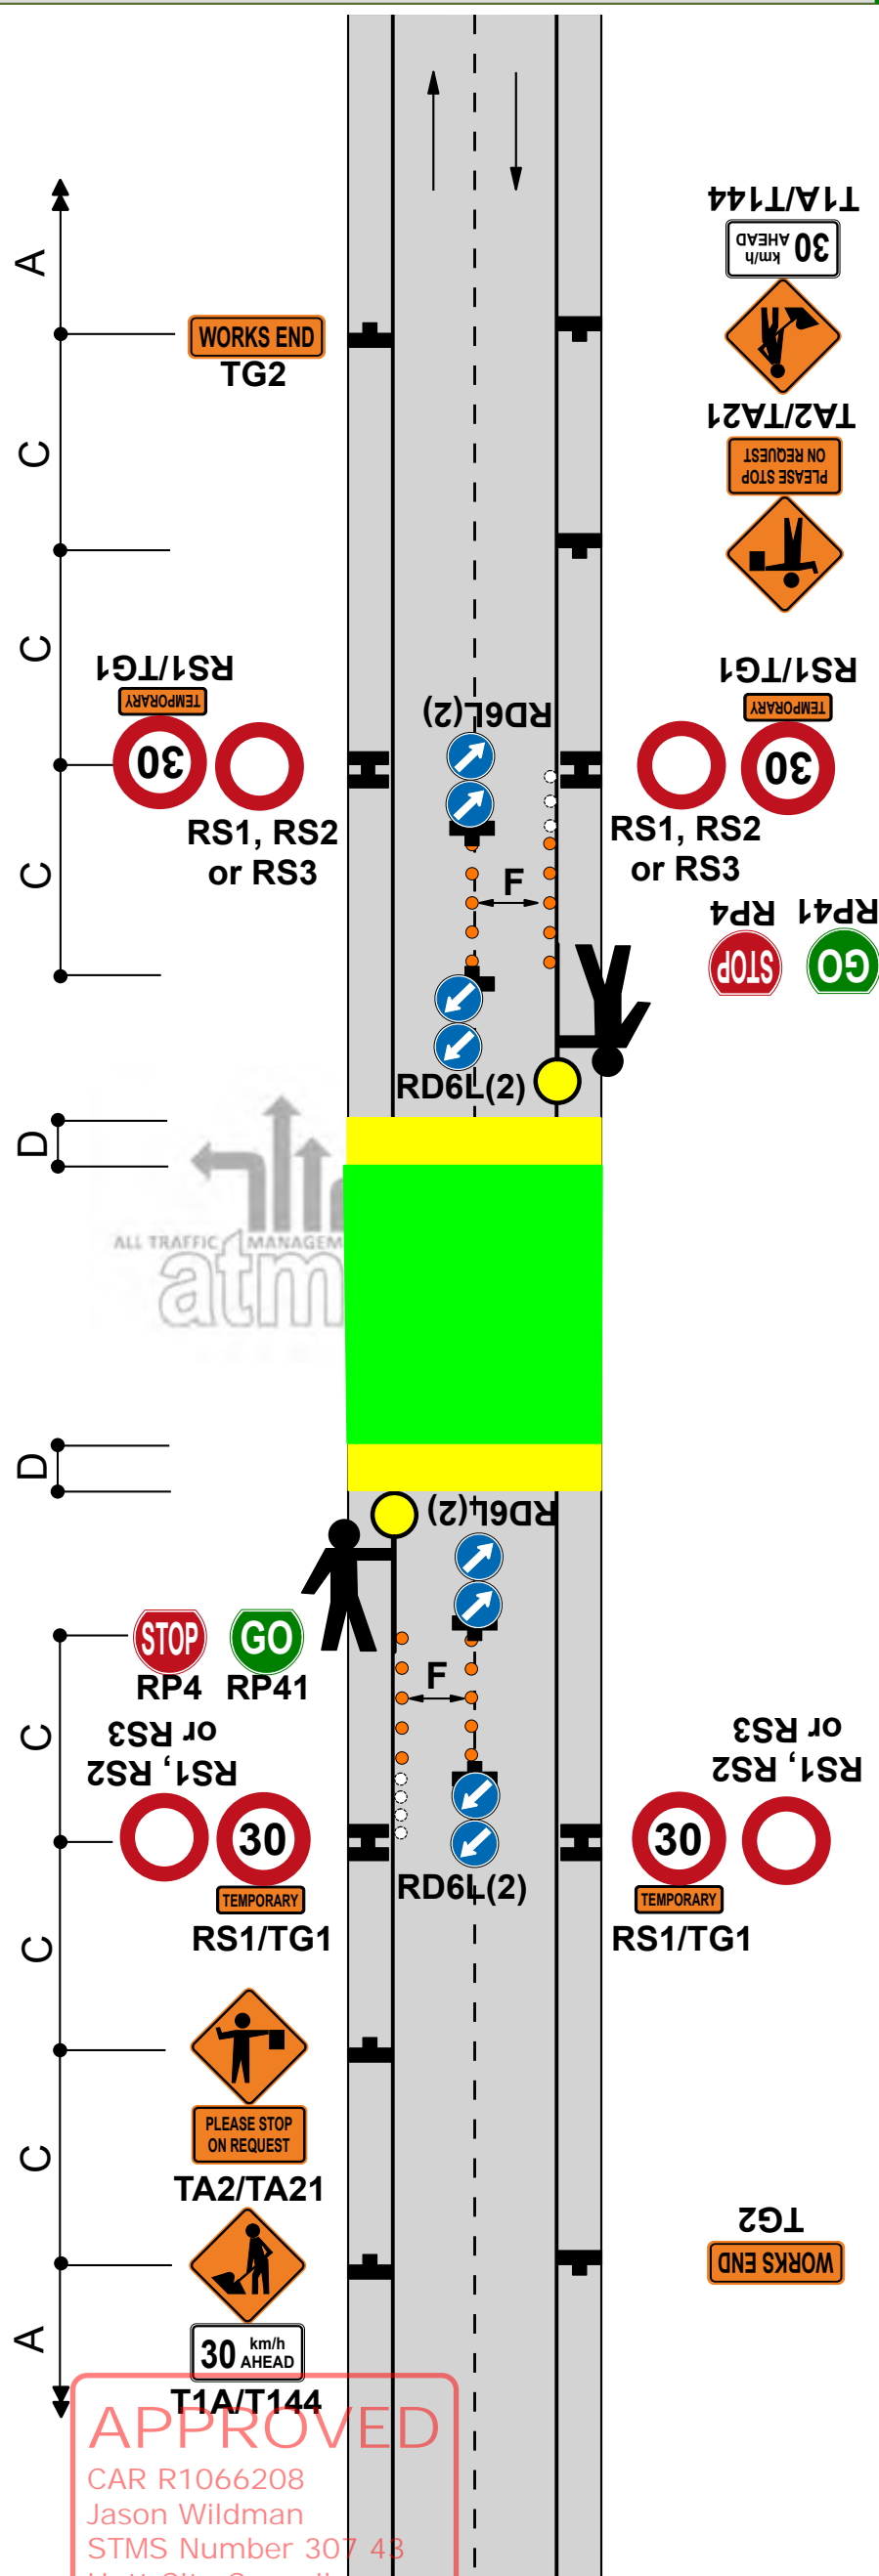

Static operations


TMC APPROVAL REQUIRED FOR BOTH ATTENDED AND UNATTENDED SITES

TWO-WAY TWO-LANE ROAD
Single-lane (traffic volume less than 1000vpd - 80vph)
Give way control

F2.16
Level 1

Notes

- 1.The RP51/RP22 and RP52 controls must be placed in the following priority order:
 - downhill traffic must give way to uphill traffic
 - traffic that has to cross into the opposing lane gives way, however where visibility for this vehicle is marginal the contractor may require the other vehicle with better visibility to give way
- 2.Intervisibility is required as indicated on diagram. This means that a vehicle at one sign is able to see whether the way ahead is clear
- 3.A 30m return taper at the end of the closure is mandatory
- 4.Use PN11 No Stopping signs, if necessary
- 5.Cones are required on edge of the temporary lane opposite closure if road is not well defined
- 6.The T144 X0km/h AHEAD sign is optional

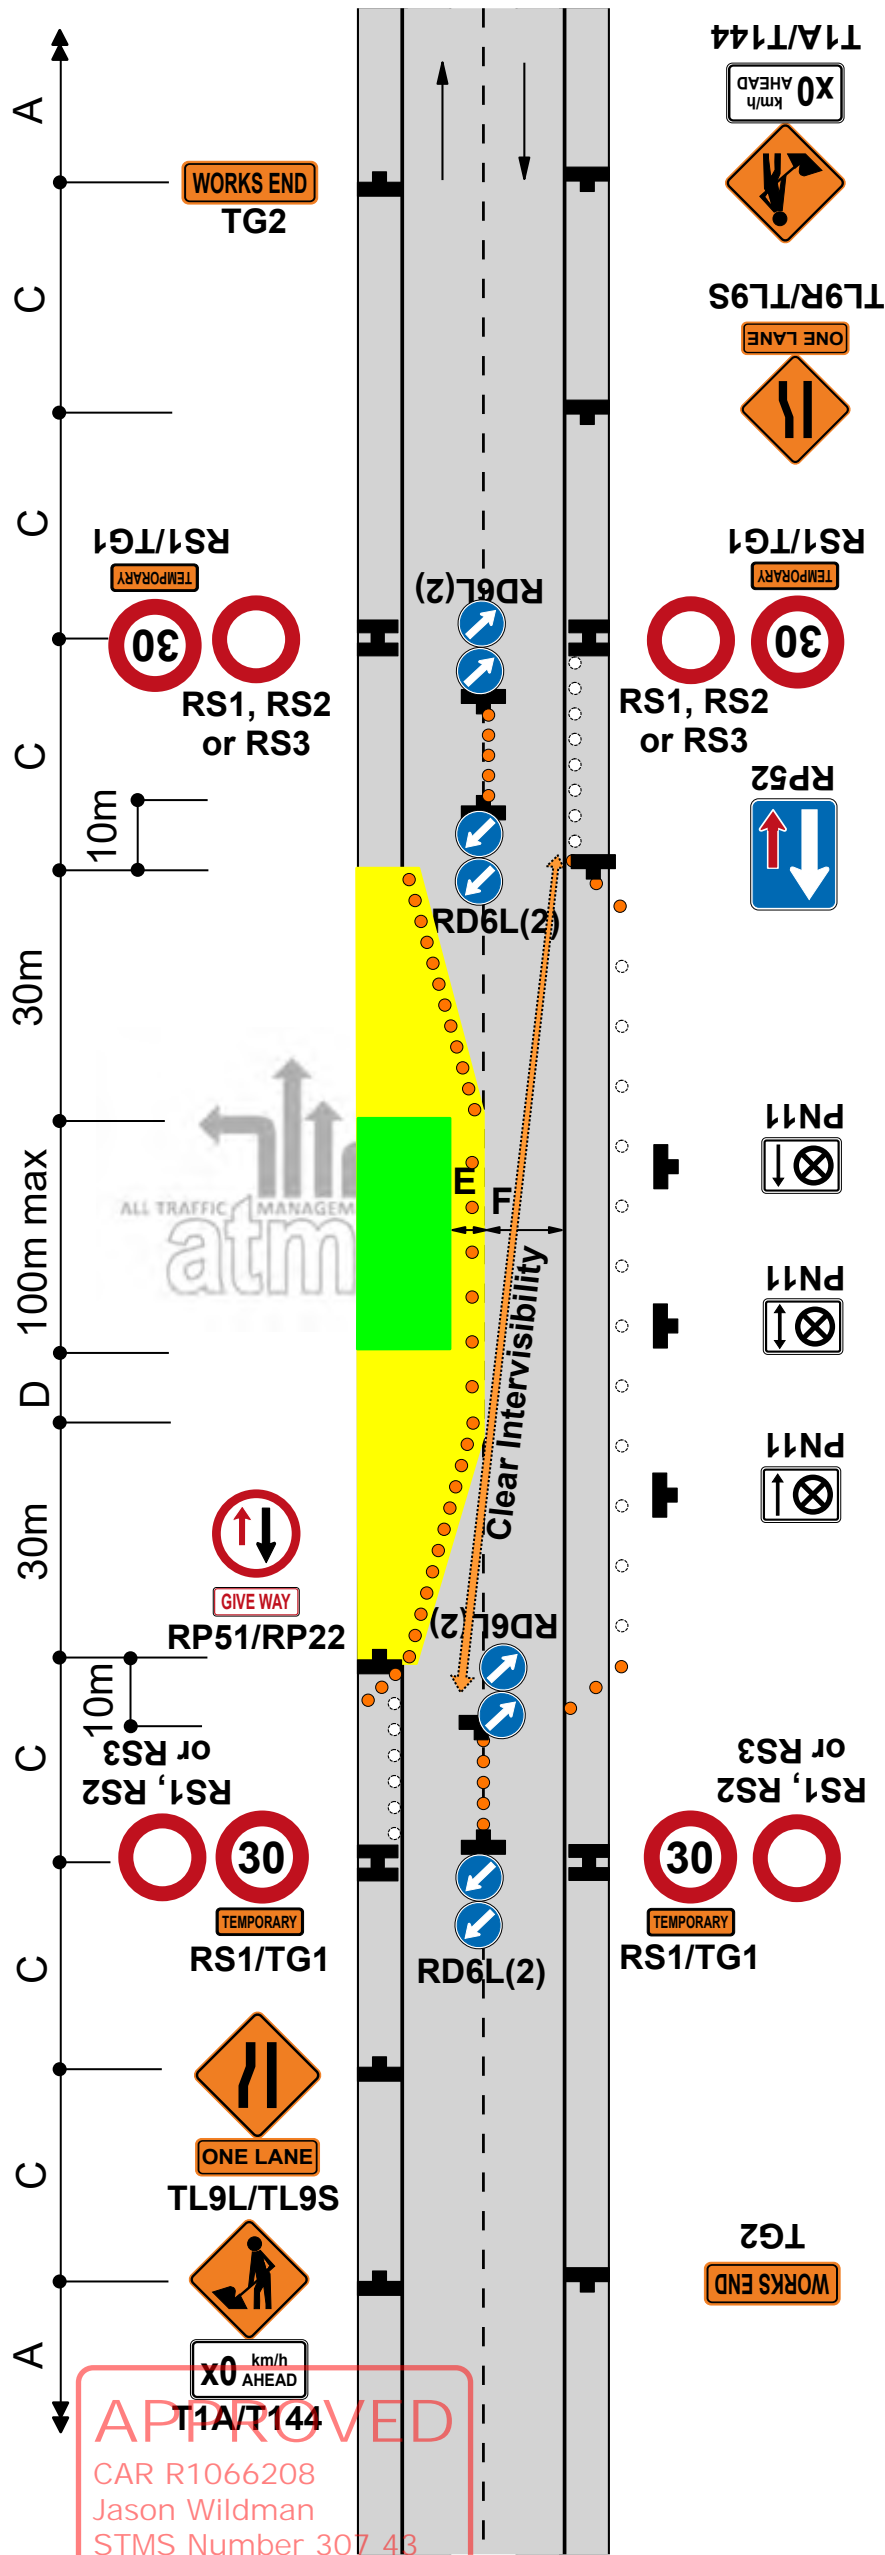

Static operations


TMC APPROVAL REQUIRED FOR SENSORED TRAFFIC SIGNALS TO BE USED FOR ANY UNATTENDED PERIOD

TWO-WAY TWO-LANE ROAD
Single-lane alternating flow
Portable traffic signals

F2.17
Level 1

Notes

1. Provide details of make and model of portable traffic signals in the TMP
2. Install temporary limit lines (must be able to be removed upon completion) or use RP61/RP62 signs
3. Approved temporary speed humps may also be used. Consider use of MTC while speed humps are installed
4. A 30m return taper at the end of the closure is mandatory
5. Cones are required on edge of the temporary lane opposite closure if road is not well defined
6. Extend or place extra advance warning signs towards on-coming traffic beyond any expected traffic queues
7. Use PN11 No Stopping signs, if necessary
8. Minimum 5 cones in cone threshold at:
 - 2.5m centres - less than 65km/h
 - 5m centres - more than 65km/h
9. The T144 30km/h AHEAD sign is optional

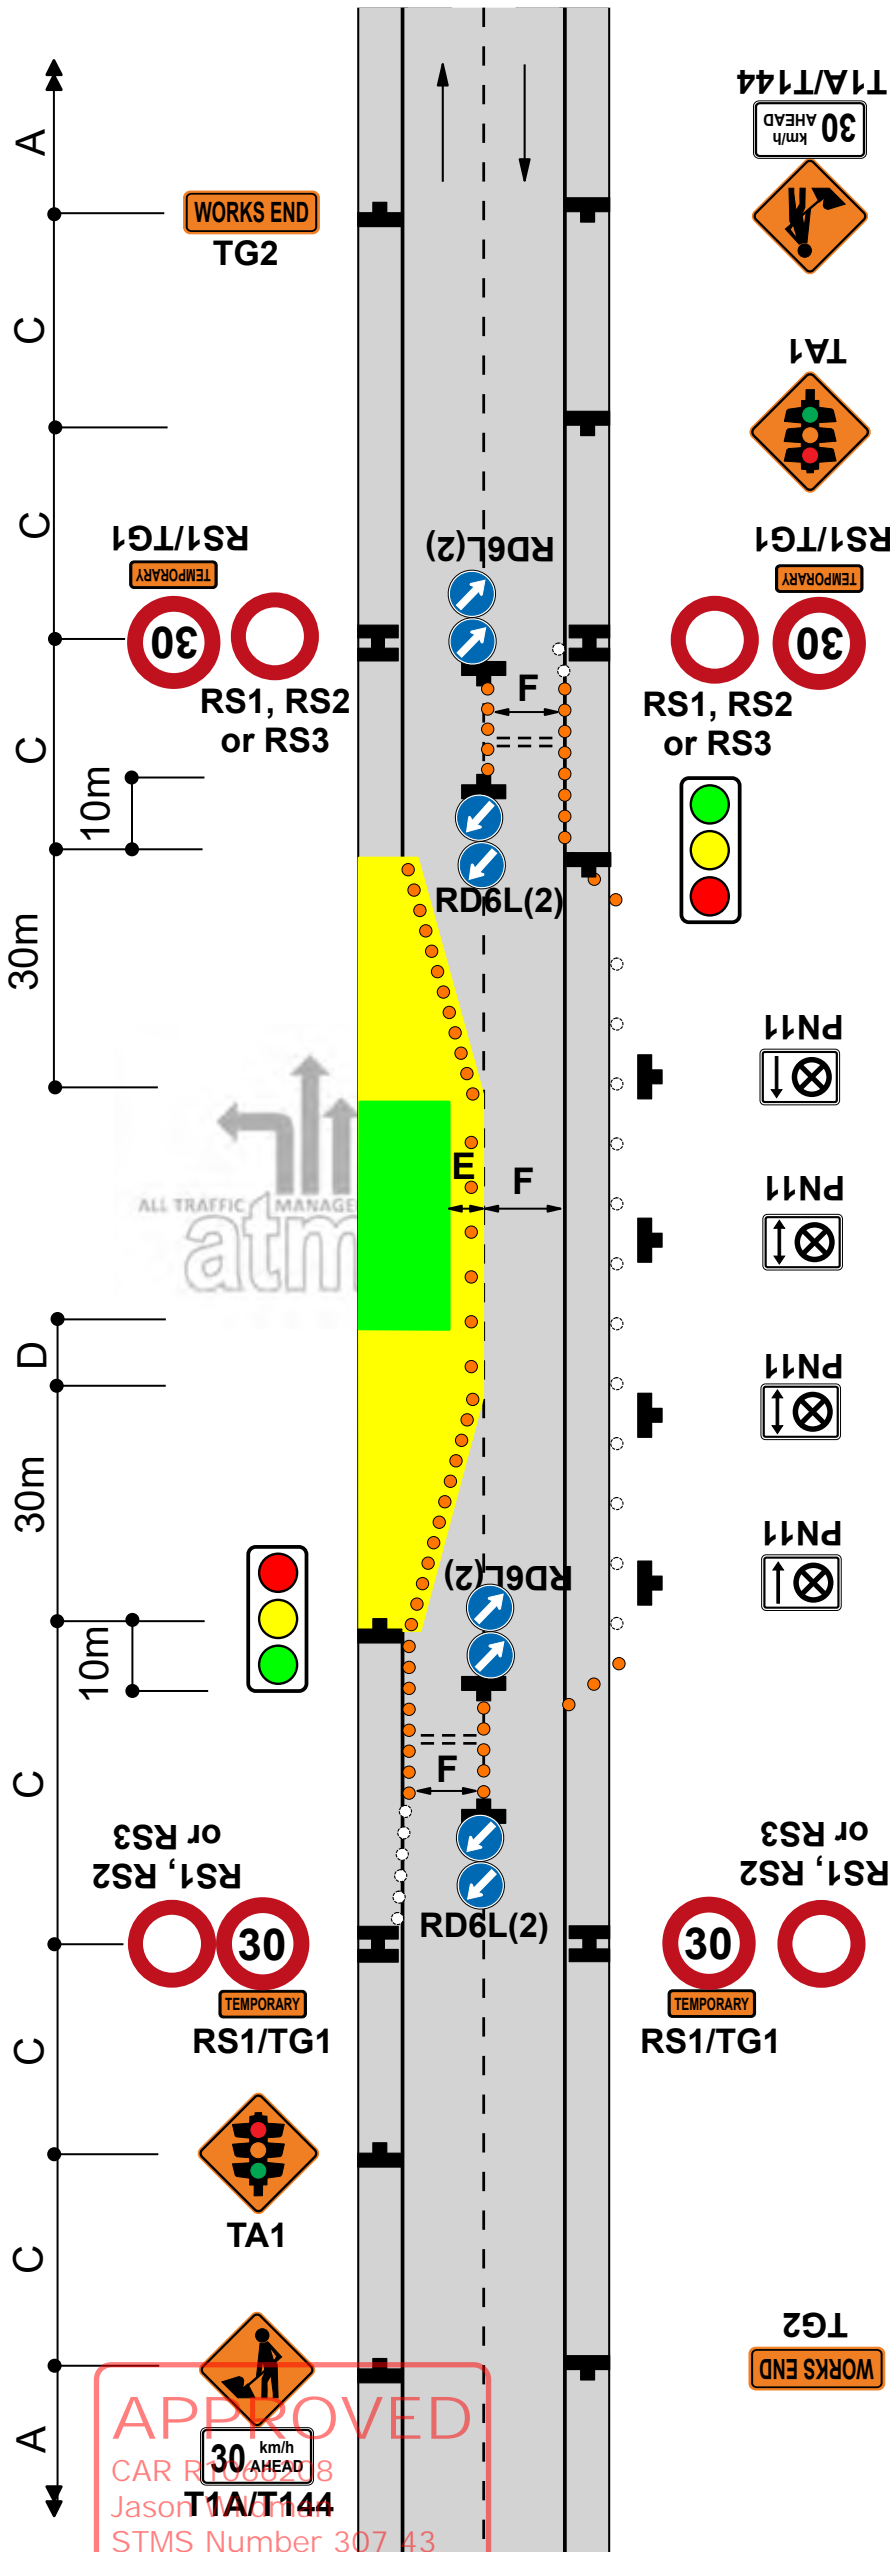

APPROVED
CAR R 602/8
Jason T144
STMS Number 307 43
Hutt City Council

14 November 2024


Static operations

TWO-WAY TWO-LANE ROAD
Work in centre of road

F2.18
Level 1

Notes

- 1. Cones are required on edge of the temporary lane opposite closure if road is not well defined
- 2. *Calculation of taper length for lateral shift of less than 3.5m is:
 $W \times G$
3.5
W = Width of lateral shift
G = Taper length in metres from the level 1 layout distance table
- 3. Use PN11 no stopping signs, if necessary
- 4. Use TSLs if required by TSL decision matrix
- 5. The T144 X0km/h AHEAD sign is optional

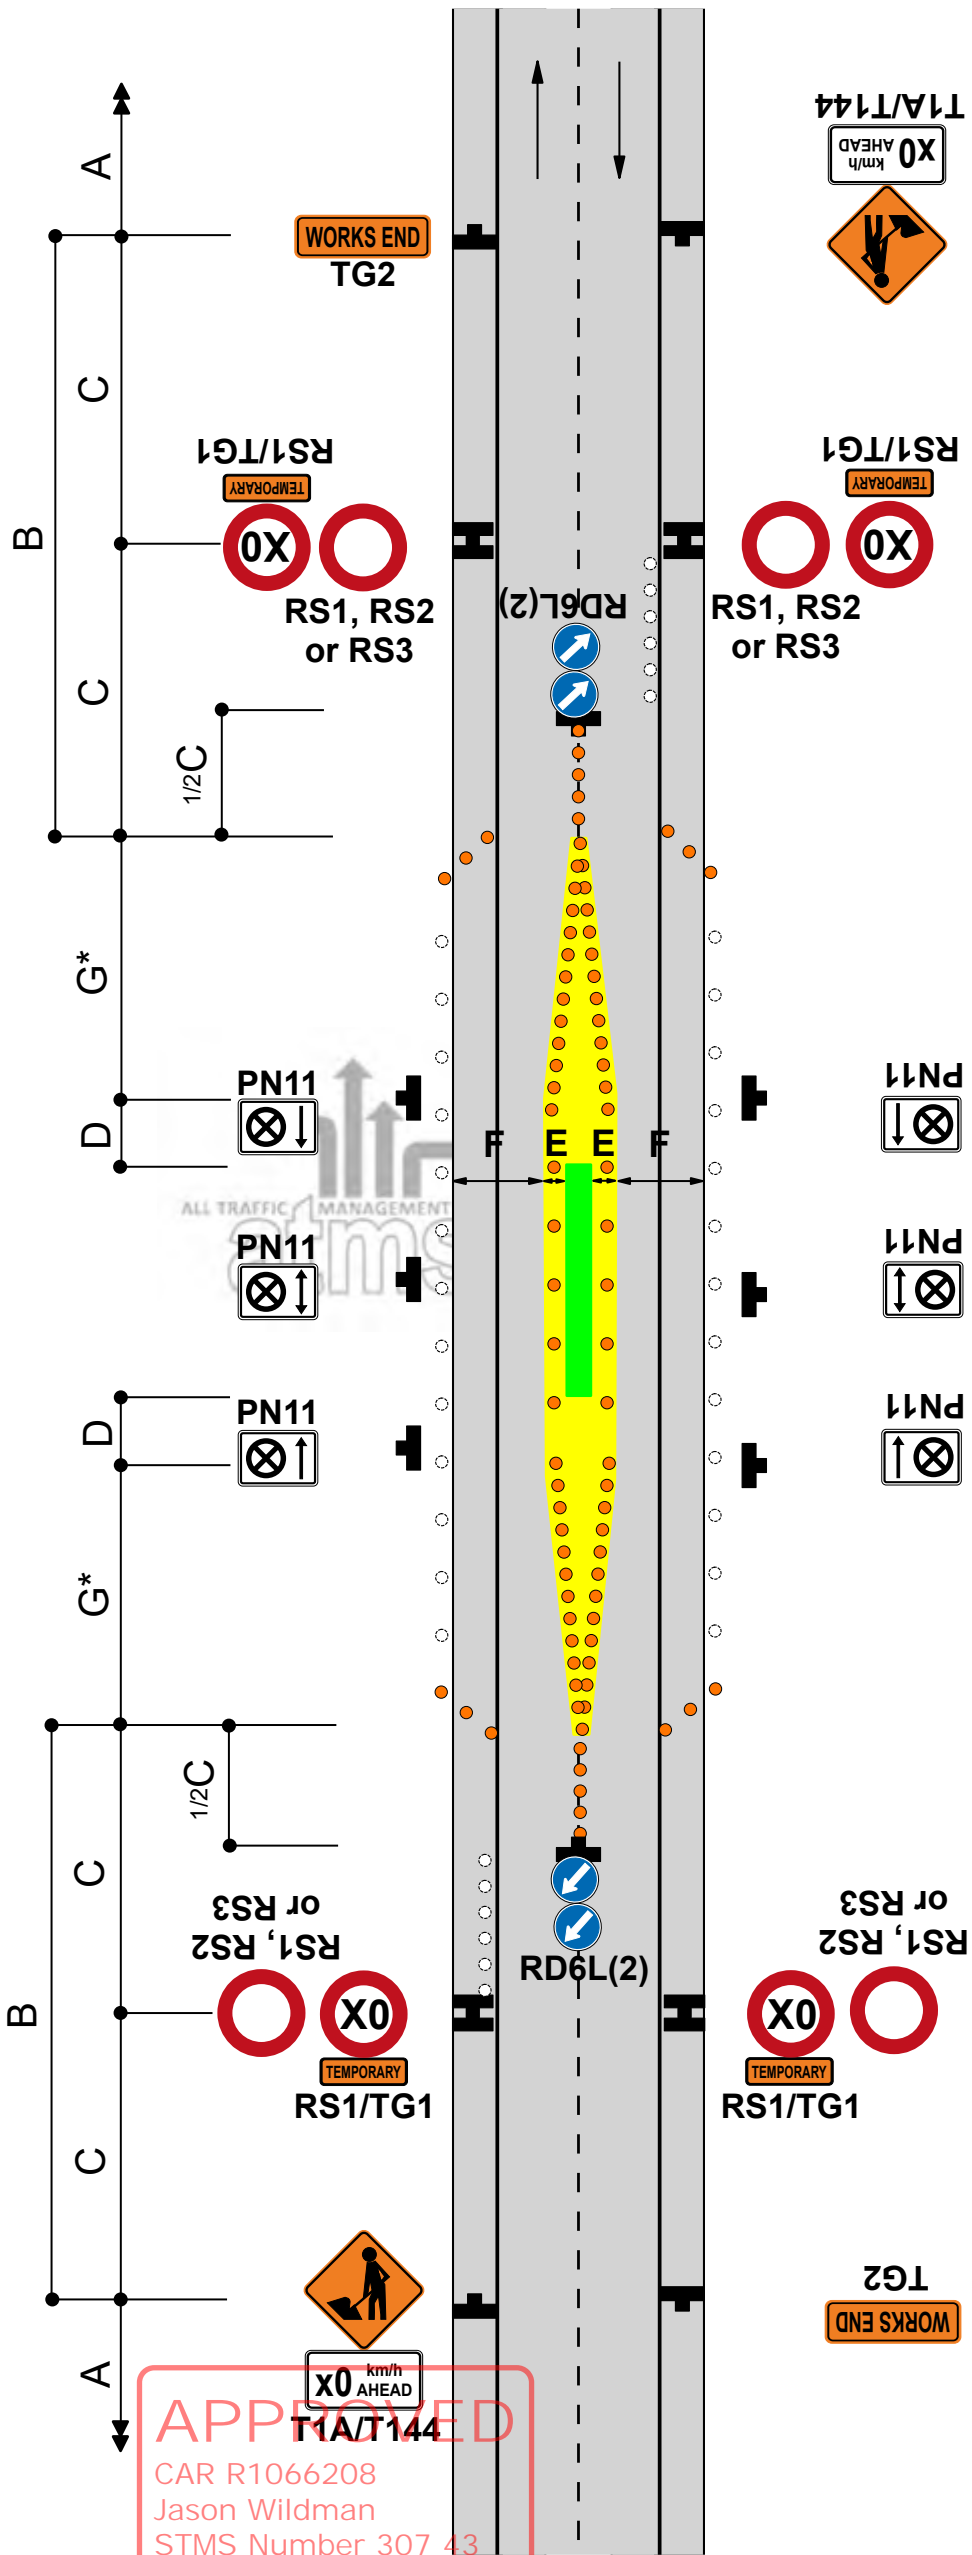

APPROVED


CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council

14 November 2024

Static operations

TWO-WAY TWO-LANE ROAD - Intersection or roundabout
Road works on side road after intersection - TSL on side road
Traffic not crossing road centre

F2.19
Level 1

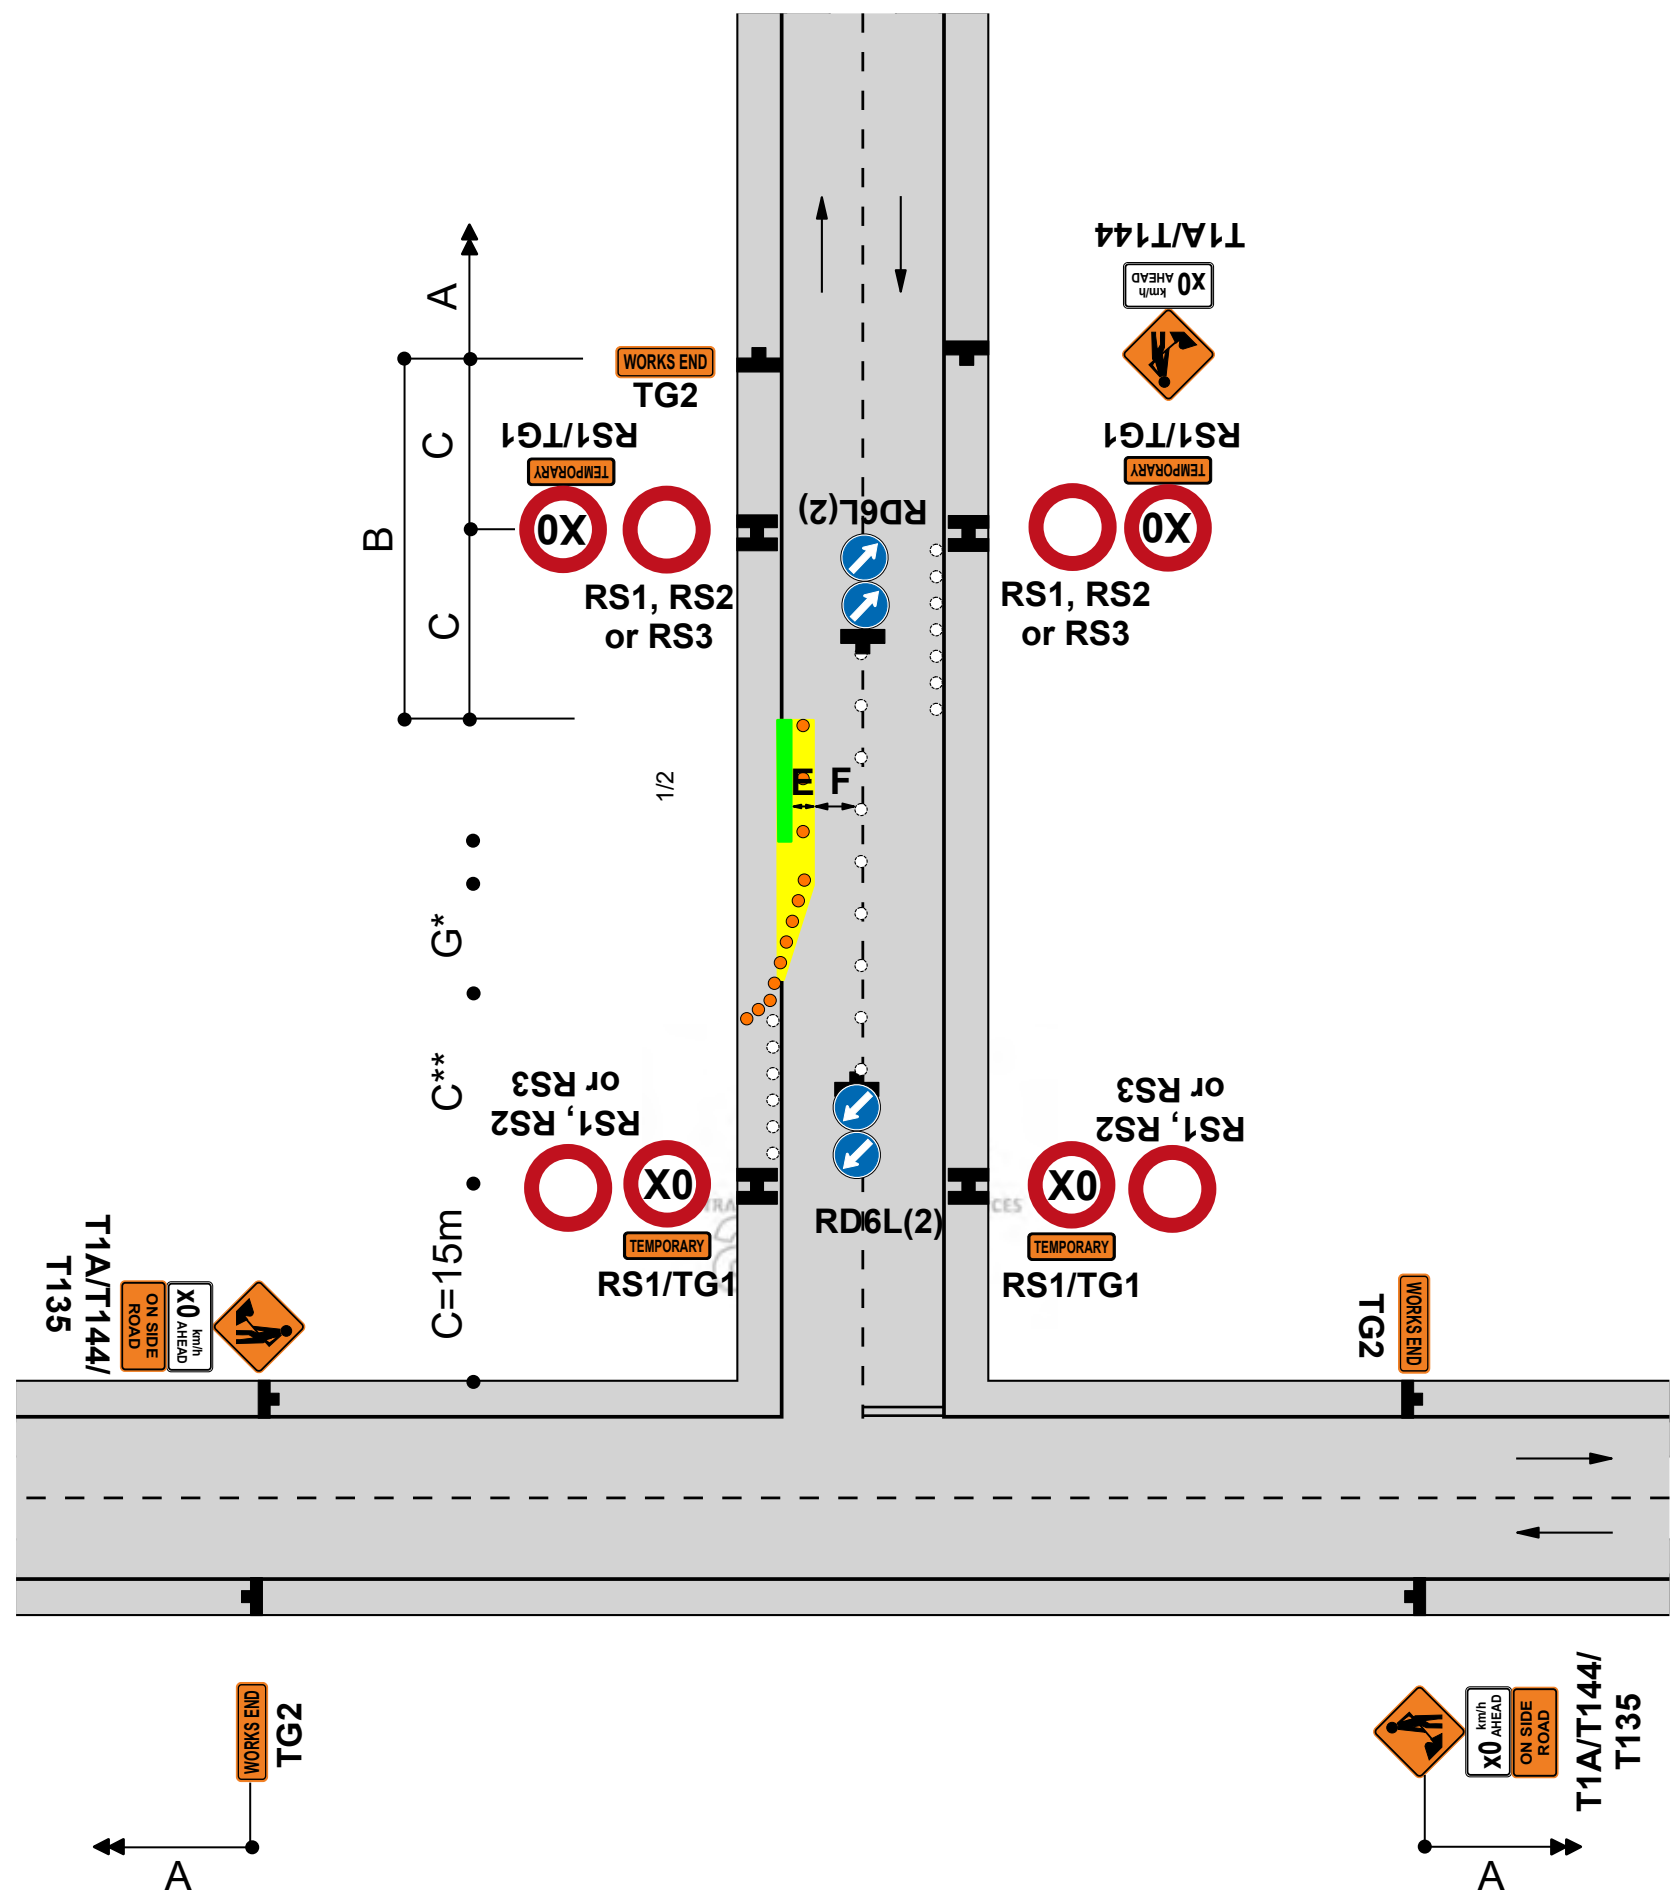

Notes

1. Sign spacing of TSL at the intersection can be reduced as per the table shown below
2. Where minimum dimensions cannot be achieved TMD F2.20 is to be used
3. Advance warning signs on main road must be at least the warning distance away from first cone in taper
4. *Calculation of taper length for lateral shift of less than 3.5m is:
 $W \times G \ W = \text{Width of lateral shift}$
 $3.5 \ G = \text{Taper length in metres from the level 1 layout distance table}$
5. If traffic likely to cross the centreline, place cones on the centreline with RD6L signs at each end
6. Use TSLs as required by TSL decision matrix
7. The T144 30km/h AHEAD sign is optional


APPROVED
CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council
14 November 2024

Speed (PSL)	Intersection to TSL	TSL to taper	Total
<50km/h	15m	15m	30m
60km/h	15m	25m	40m
>70km/h	15m	40m	55m

Static operations

TWO-WAY TWO-LANE ROAD - Intersection or roundabout
Road works on side road after intersection - TSL on main road
Traffic not crossing road centre

F2.20
Level 1

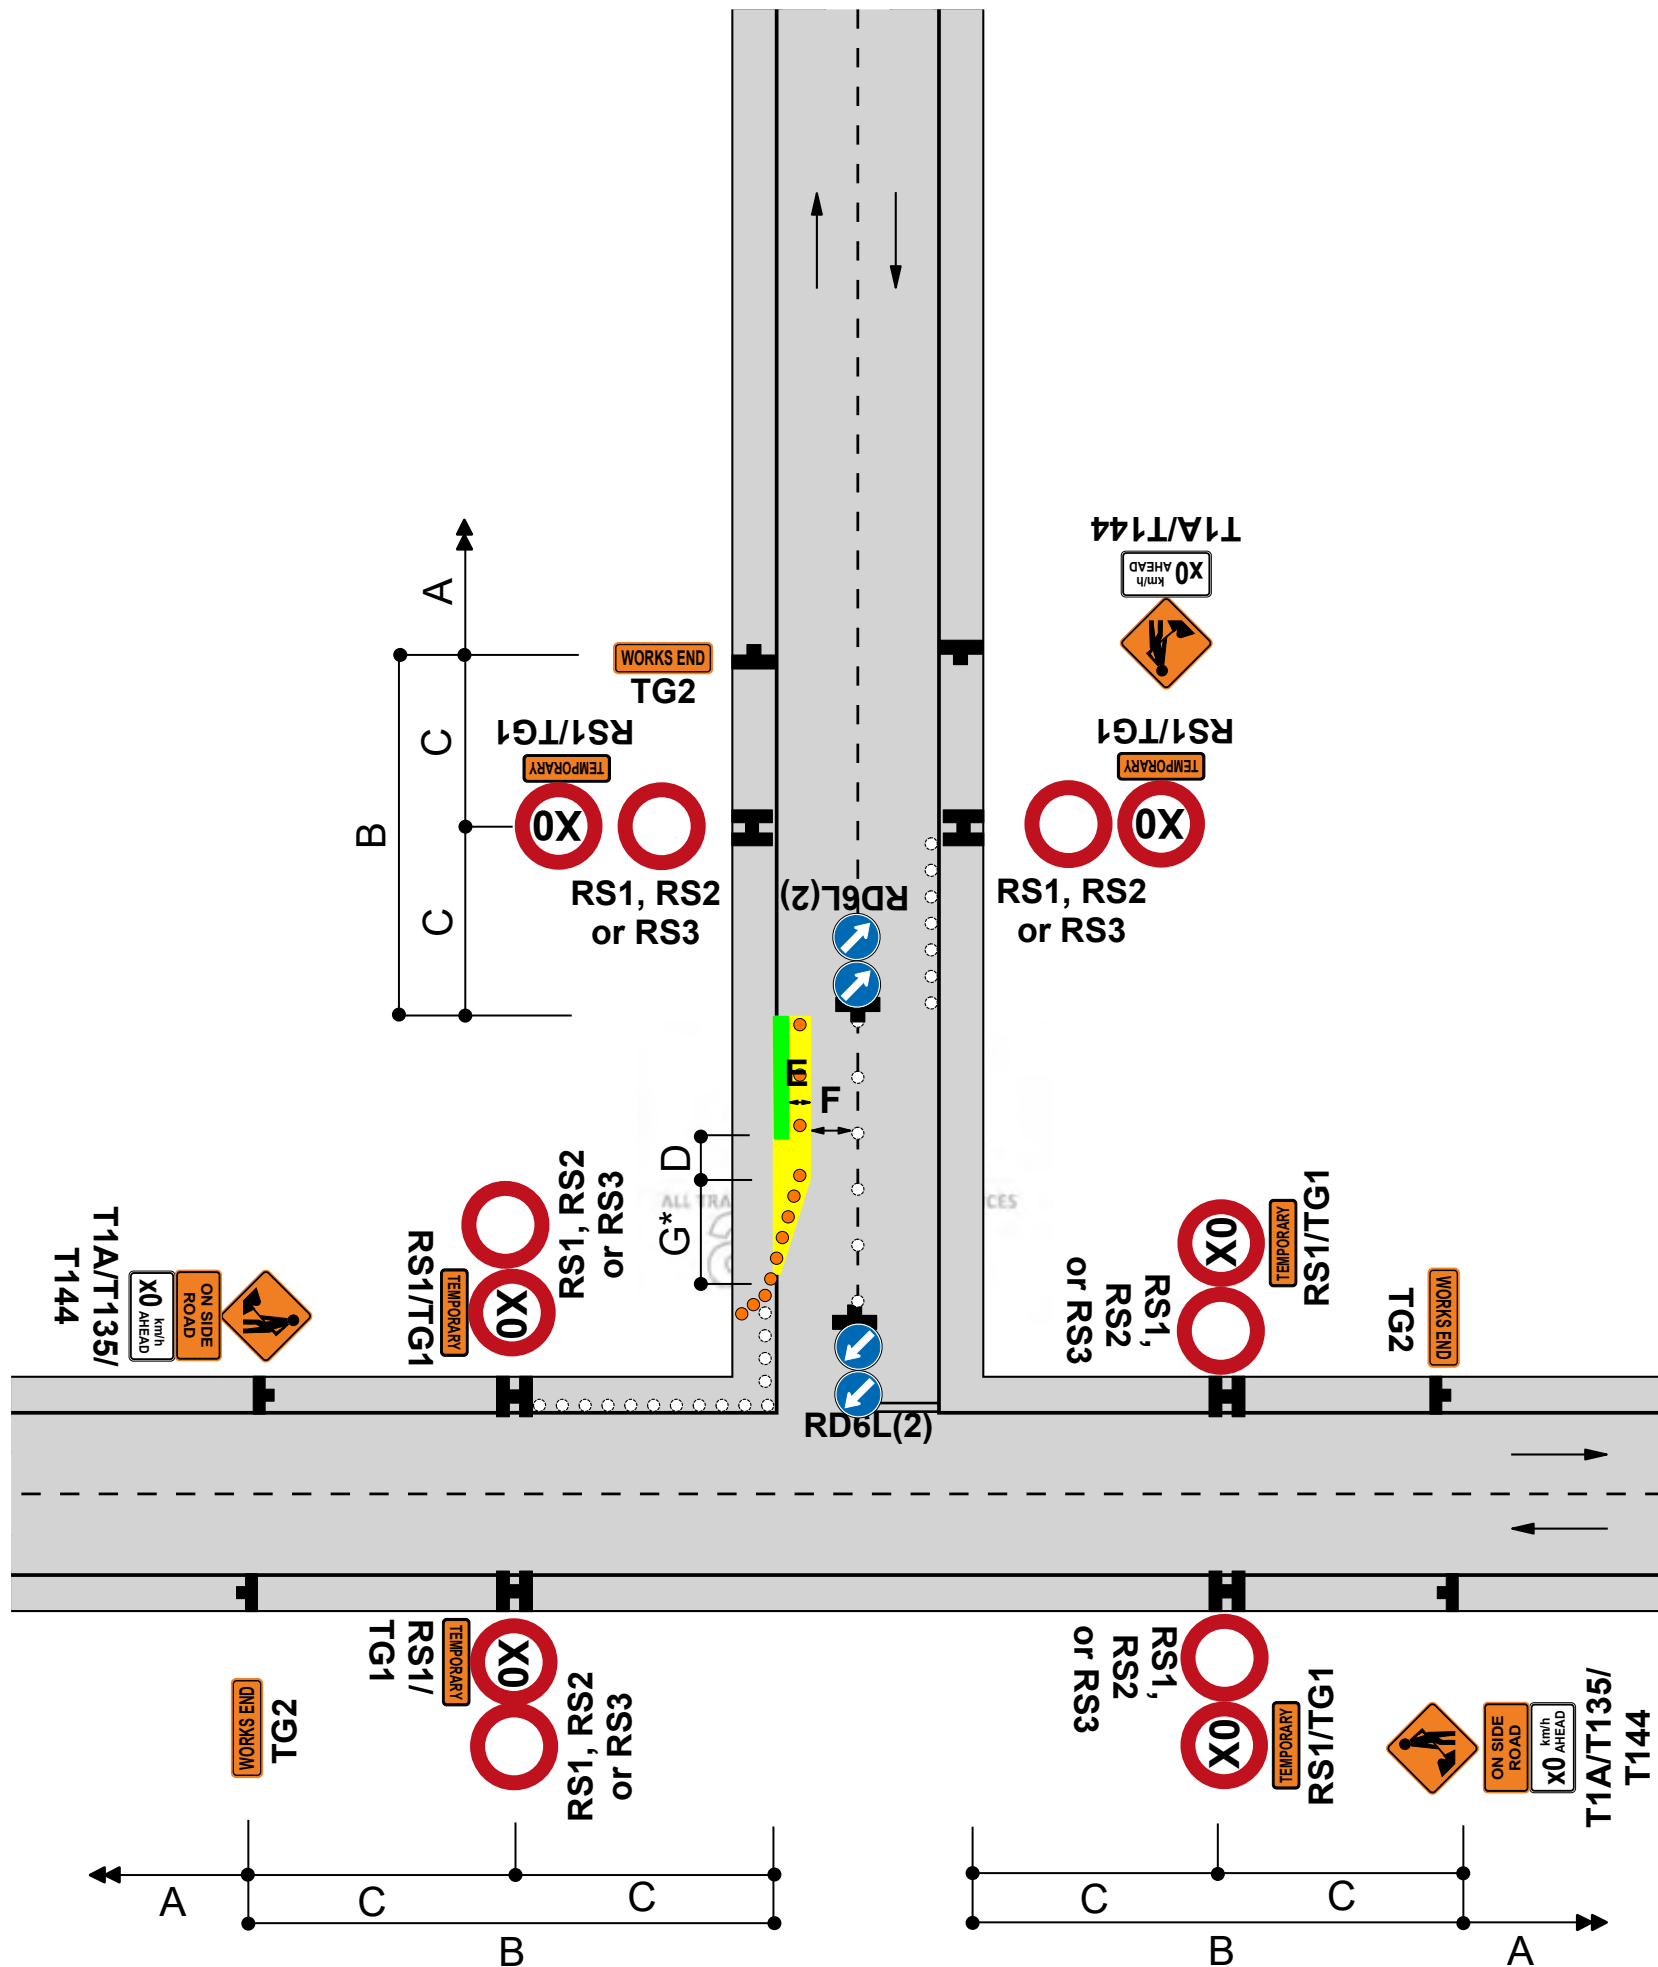

Notes

- *Calculation of taper length for lateral shift of less than 3.5m is:

$$\frac{W \times G}{3.5}$$

W = Width of lateral shift
G = Taper length in metres from the level 1 layout distance table
- If traffic likely to cross the centreline, place cones on the centreline with RD6L signs at each end
- Use TSLs as required by TSL decision matrix
- The T144 X0km/h AHEAD sign is optional

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council


Jason Wildman

14 November 2024

Static operations

TWO-WAY TWO-LANE ROAD - Intersection or roundabout
Work in middle of intersection

F2.21
Level 1

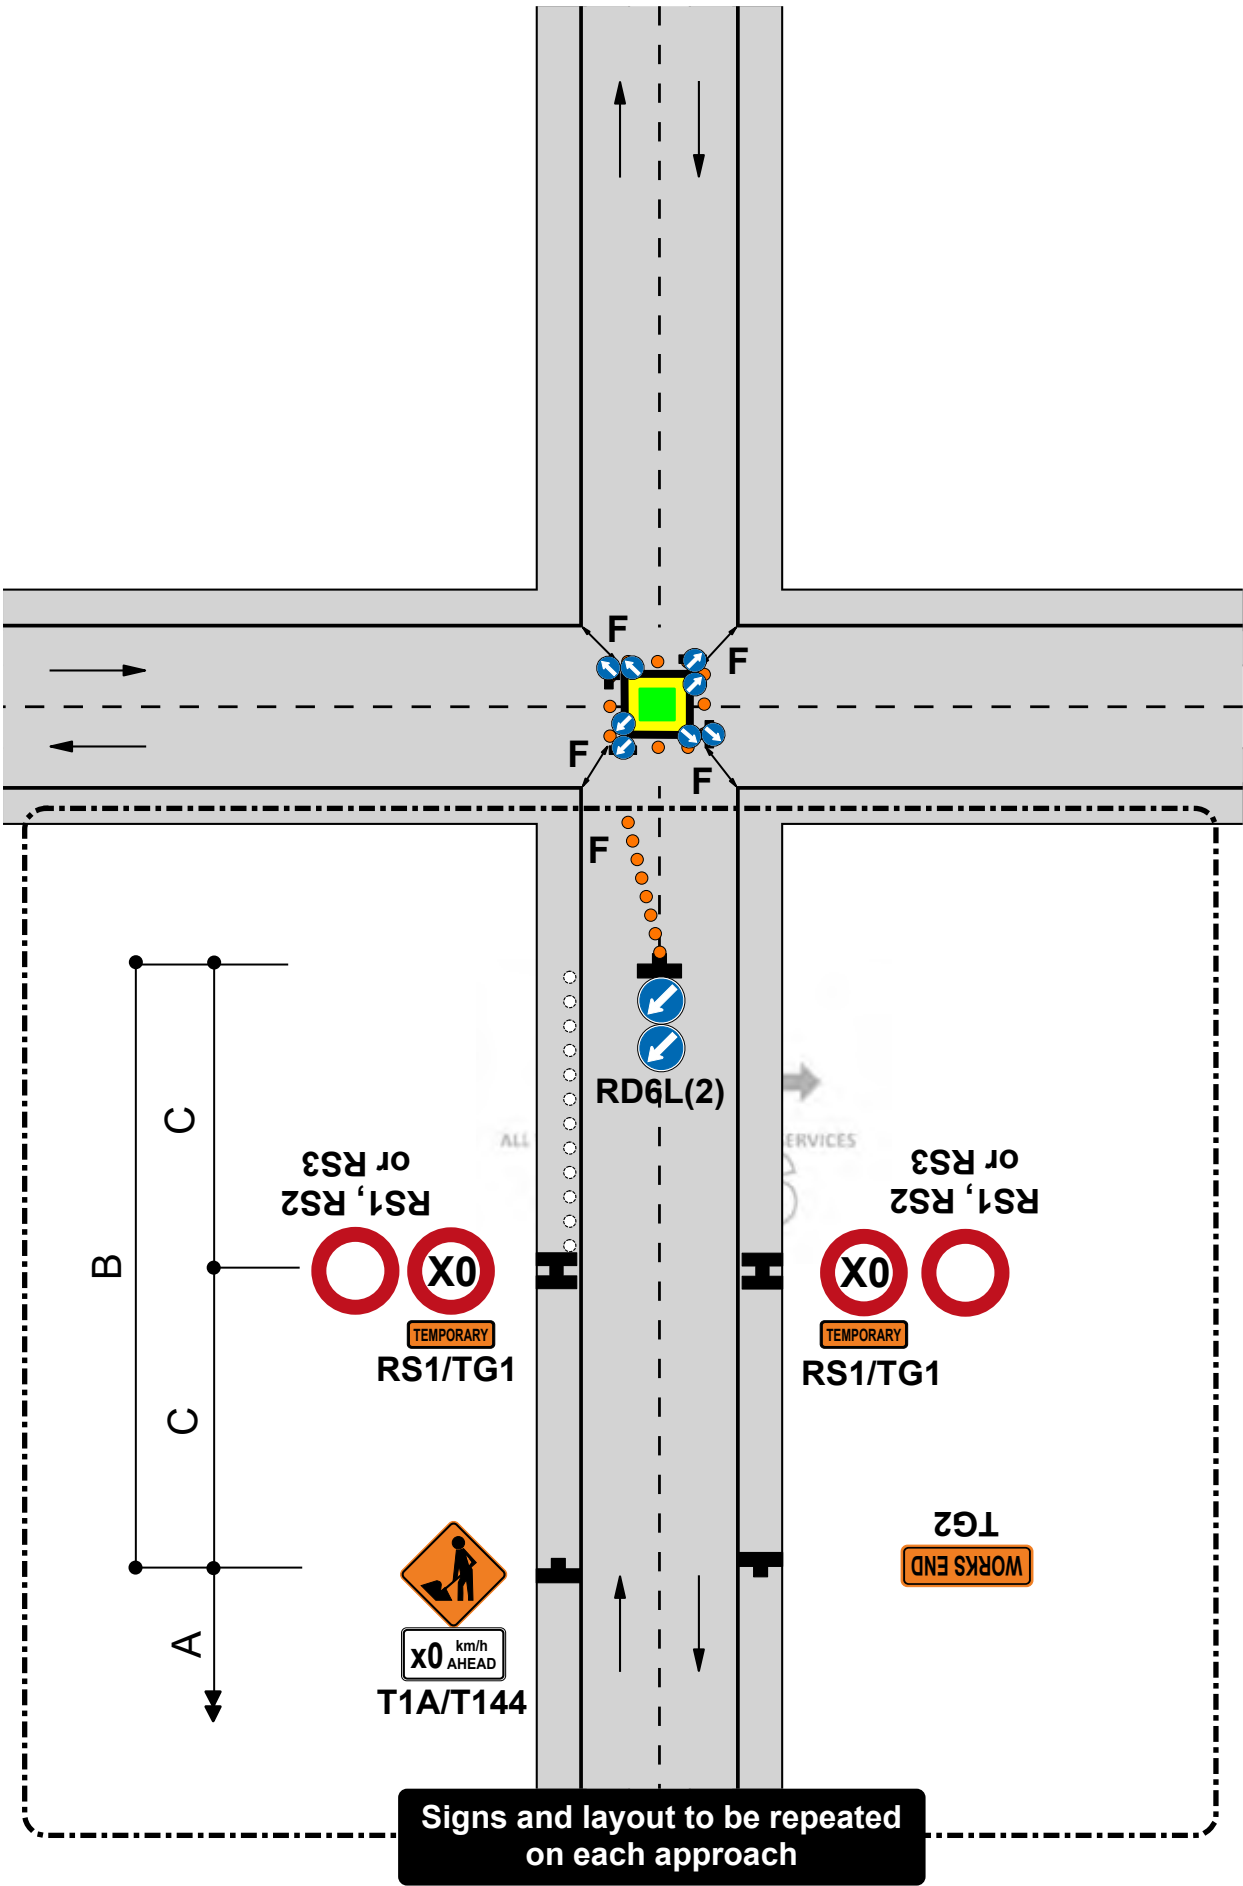

Notes

- 1.This diagram may be used at a T intersection by removing any one of the roads
- 2.Signs and layout shown in the box at the bottom of the diagram is to be repeated on each approach
- 3.RD6L signs are not required at an existing roundabout
- 4.Cone tapers are optional at existing roundabouts
- 5.Lane widths, F, may need to be increased to allow for turning movements of larger vehicles
- 6.Use TSLs if required by TSL decision matrix
- 7.The T144 X0km/h AHEAD sign is optional

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council

Wildman


Static operations

ONE-WAY TWO-LANE DIVIDED OR TWO-LANE ROAD
Left-lane closure

F2.30
Level 1

Notes

- 1. Use TSLs if required by TSL decision matrix
- 2. On roads with a permanent speed limit of 100km/h, cones are required from the TSL to the taper if the speed is reduced by more than 30km/h
- 3. The T144 X0km/h AHEAD sign is optional

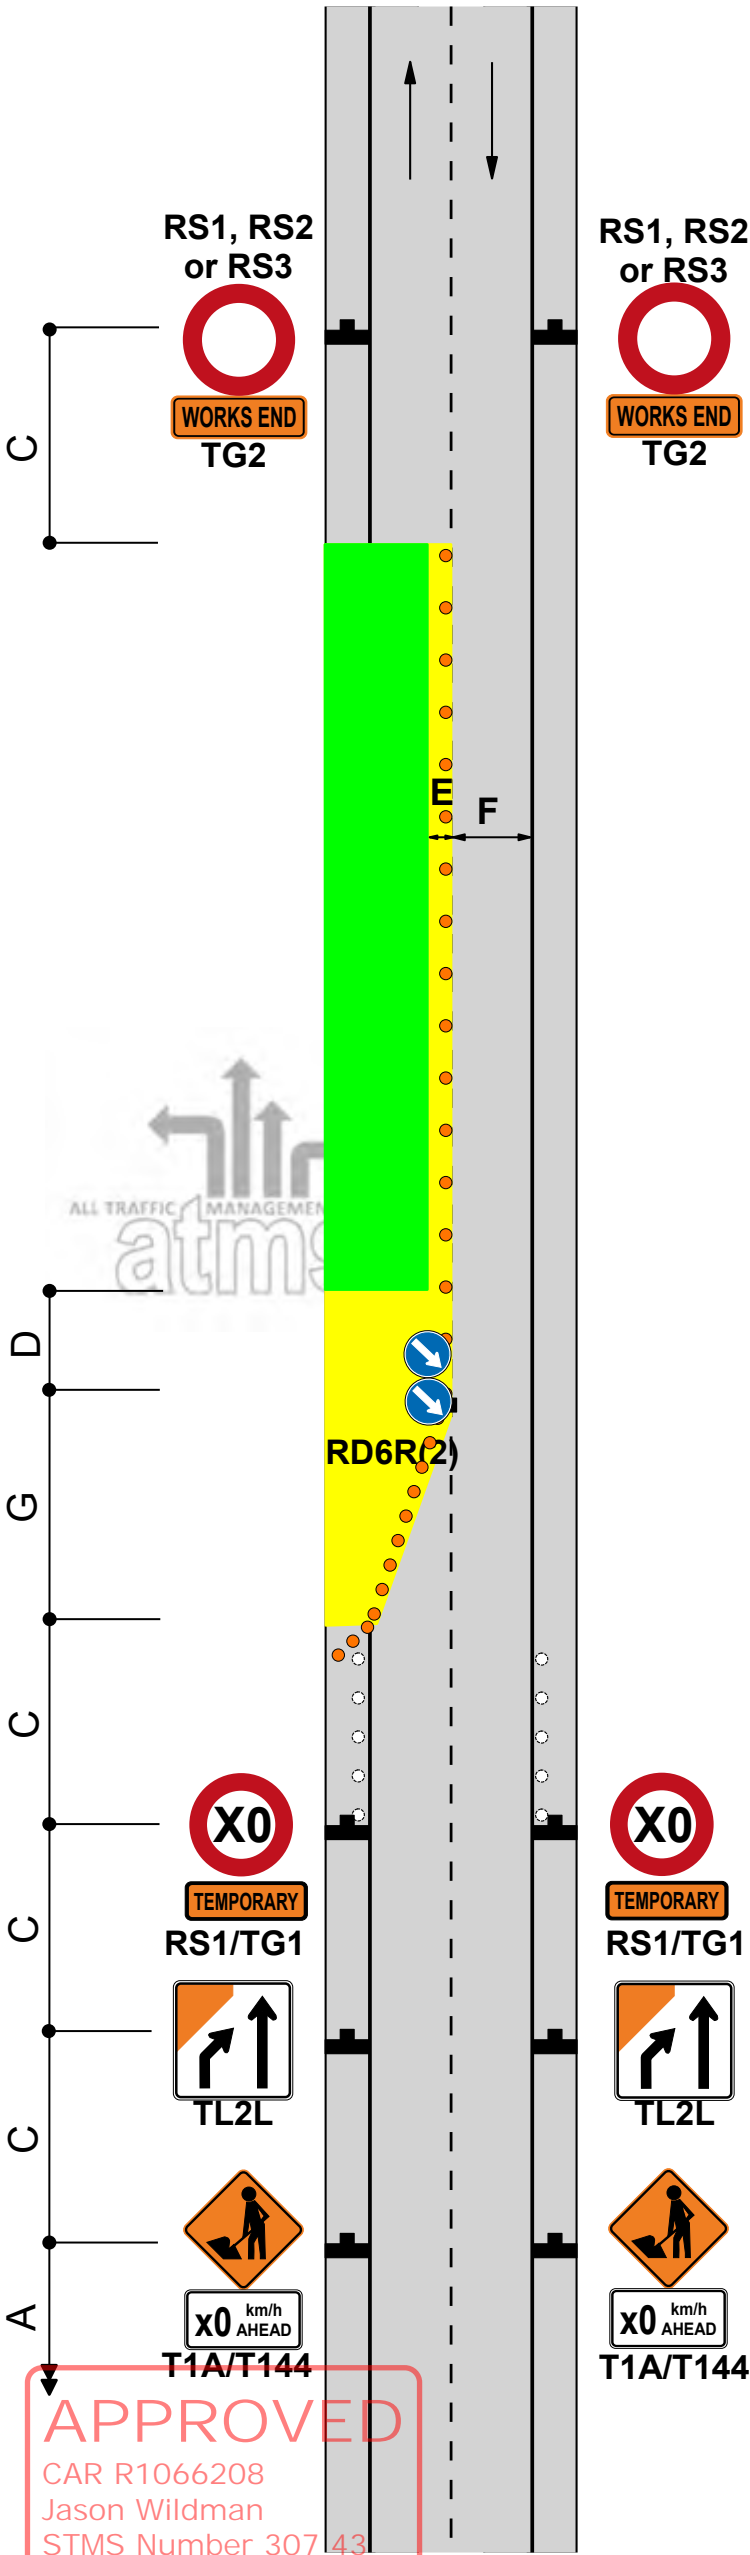

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council

14 November 2024


Static operations

ONE-WAY TWO-LANE DIVIDED OR TWO-LANE ROAD
Right-lane closure

F2.31
Level 1

Notes

1. Use TSLs if required by TSL decision matrix
2. On roads with a permanent speed limit of 100km/h, cones are required from the TSL to the taper if the speed is reduced by more than 30km/h
3. The T144 X0km/h AHEAD sign is optional

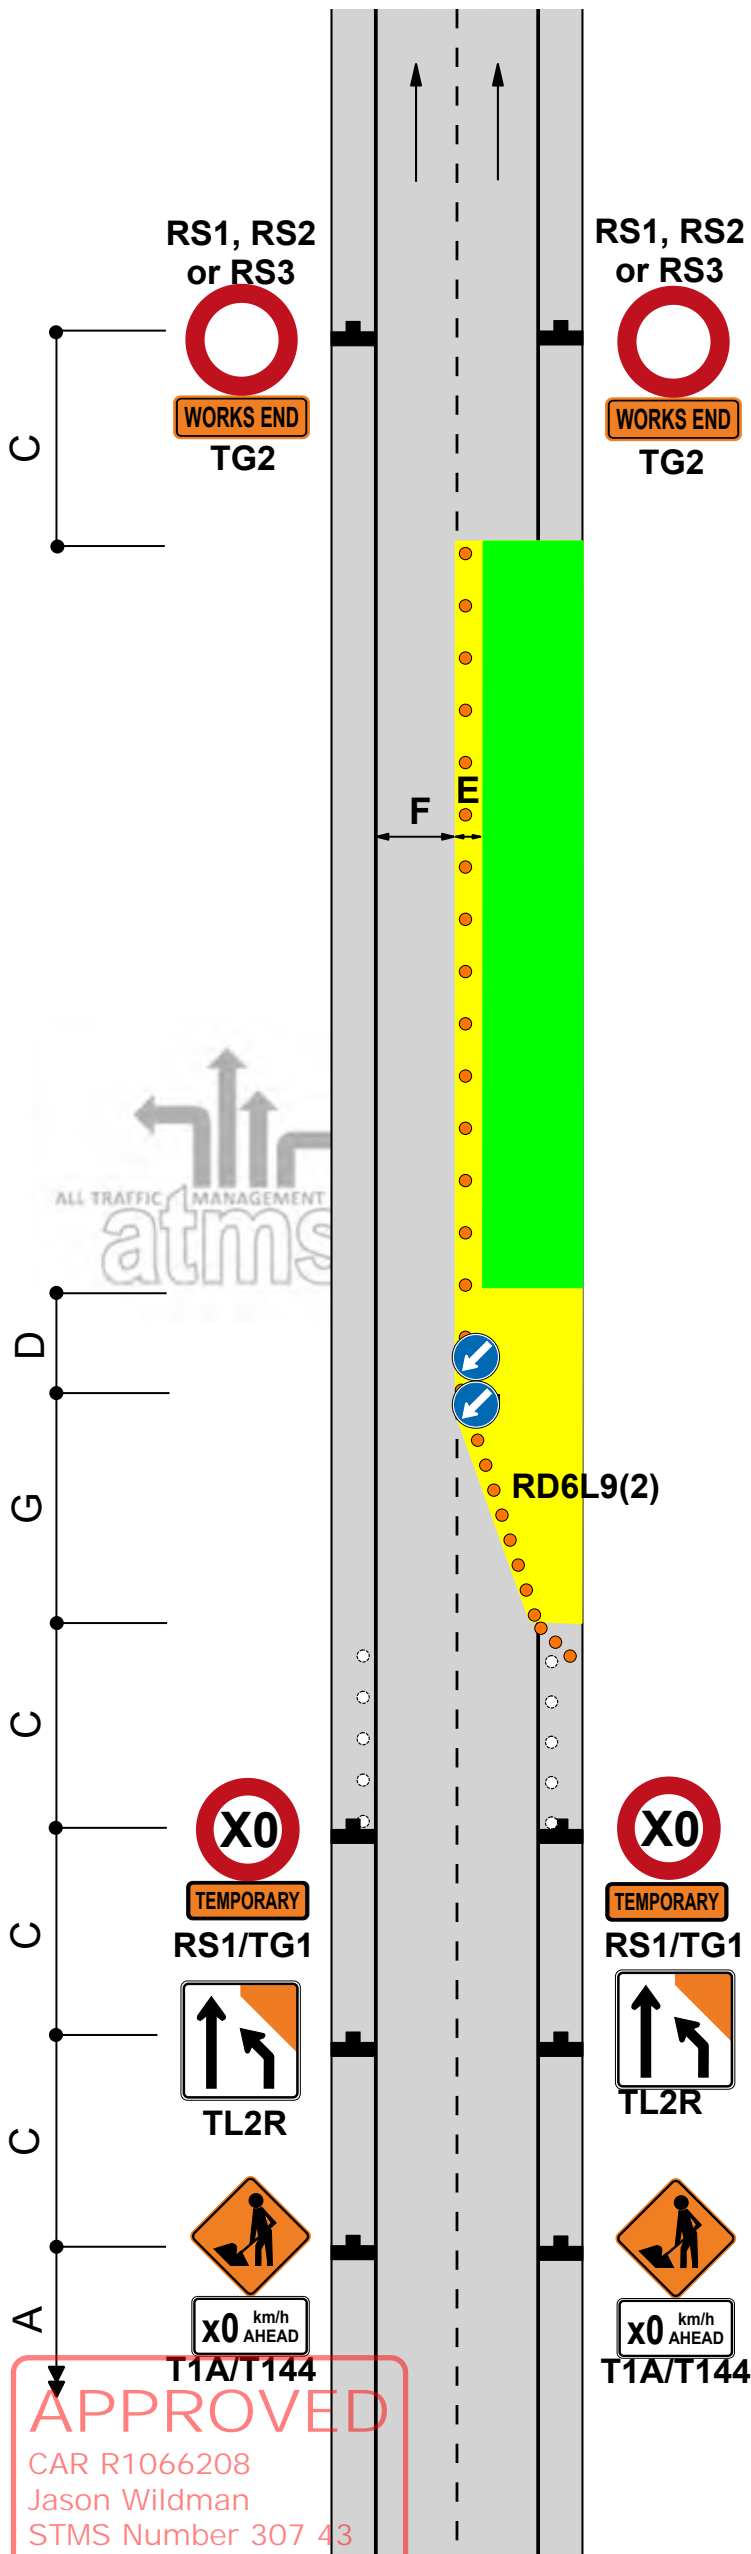

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council

Wildman


14 November 2024

TWO-WAY TWO-LANE ROAD - Road closures and detours
Road closure - detour route
Example

F2.24

Level 1


1. Block access to road with barricade
2. If a longer term site, use chevron sight board to direct traffic

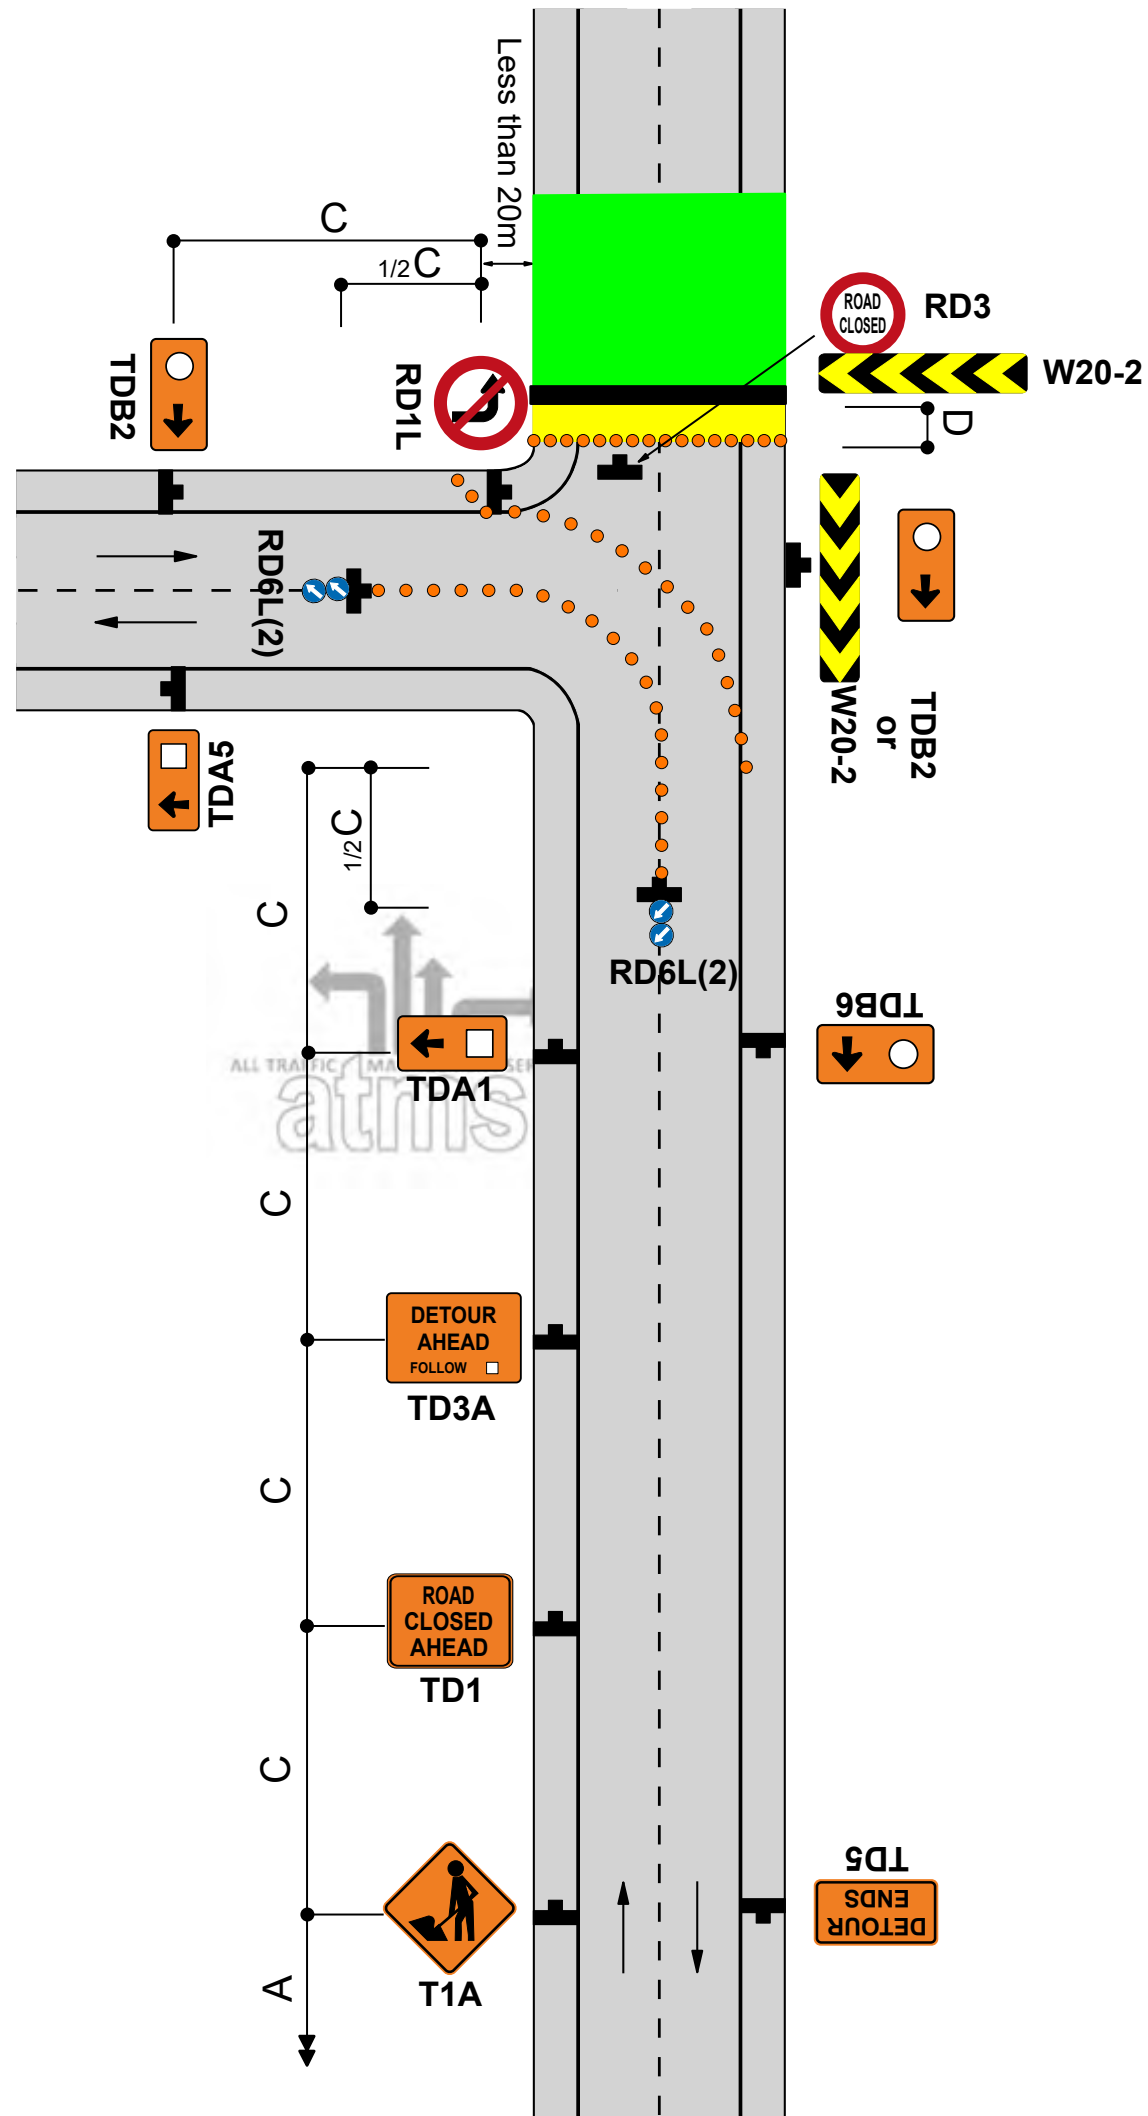

Section F

4th edition, November 2018

14 November 2024

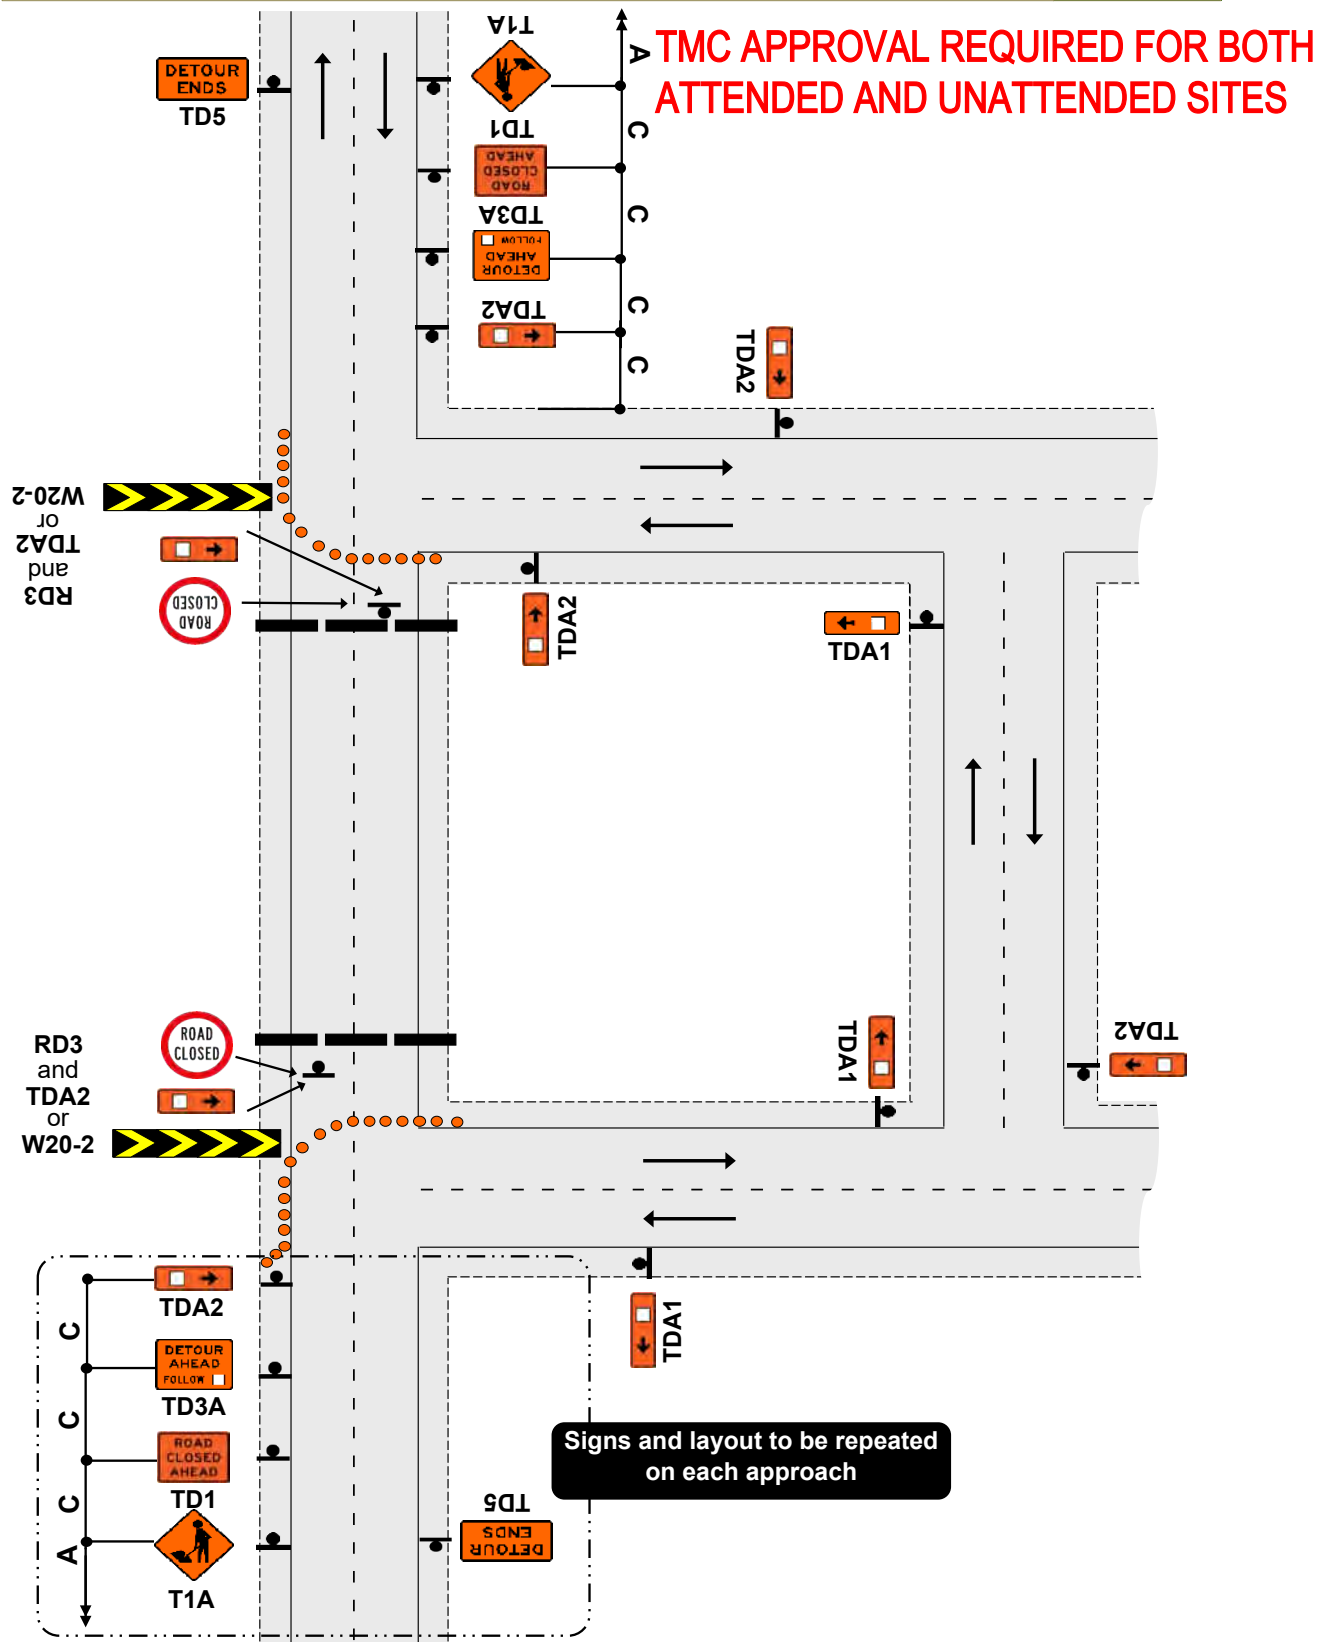

Notes

- Signpost all intersections to return diverted traffic back to normal/intended route:
 - Use appropriate sign to indicate detour ahead (eg TD3A)
 - Use appropriate route signs before each intersection and on long straights (eg TDA1)
 - Use TD5 signs to advise end of detour
- If detour to operate for more than 48 hours:
 - Use chevron sight board to direct traffic
 - Add destination signage as appropriate

APPROVED

CAR R1066208
 Jason Wildman
 STMS Number 307 43
 Hutt City Council

Wildman

14 November 2024

Static operations


TWO-WAY TWO-LANE ROAD

Cul De Sac - Closure

Access to maintained for Residents/Couriers/Emergency Services

ATMS08

Level 1

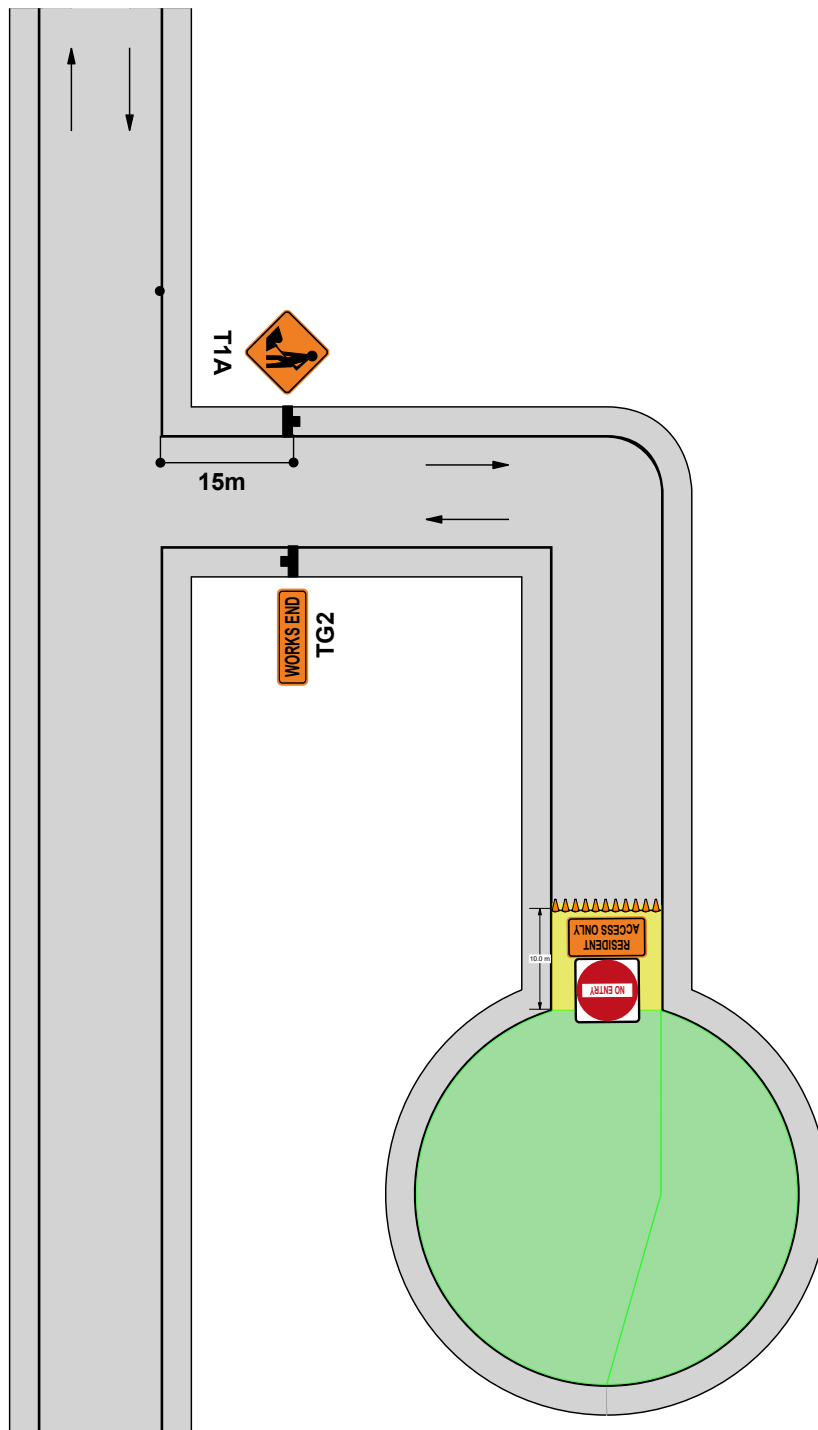

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council

Jason Wildman

14 November 2024

TWO-WAY TWO-LANE ROAD

Other hazard

Flooding, washout, slip, slippery surface






F2.26

Level 1

Notes

1. This diagram is for initial response only. Appropriate long term TTM must be installed as soon as practical

2. Use one of the following signs and/or supplementary plates:


T211		Flooding
T212		Washout
TR1L/R		Slips
TR2		Slippery Surface
TR4		Uneven Surface

3. If necessary, erect TG4 DRY YOUR BRAKES sign

4. Delineate hazard if hazard extends onto lane

5. Use TSLs if required by TSL decision matrix

6. The T144 X0km/h AHEAD sign is optional

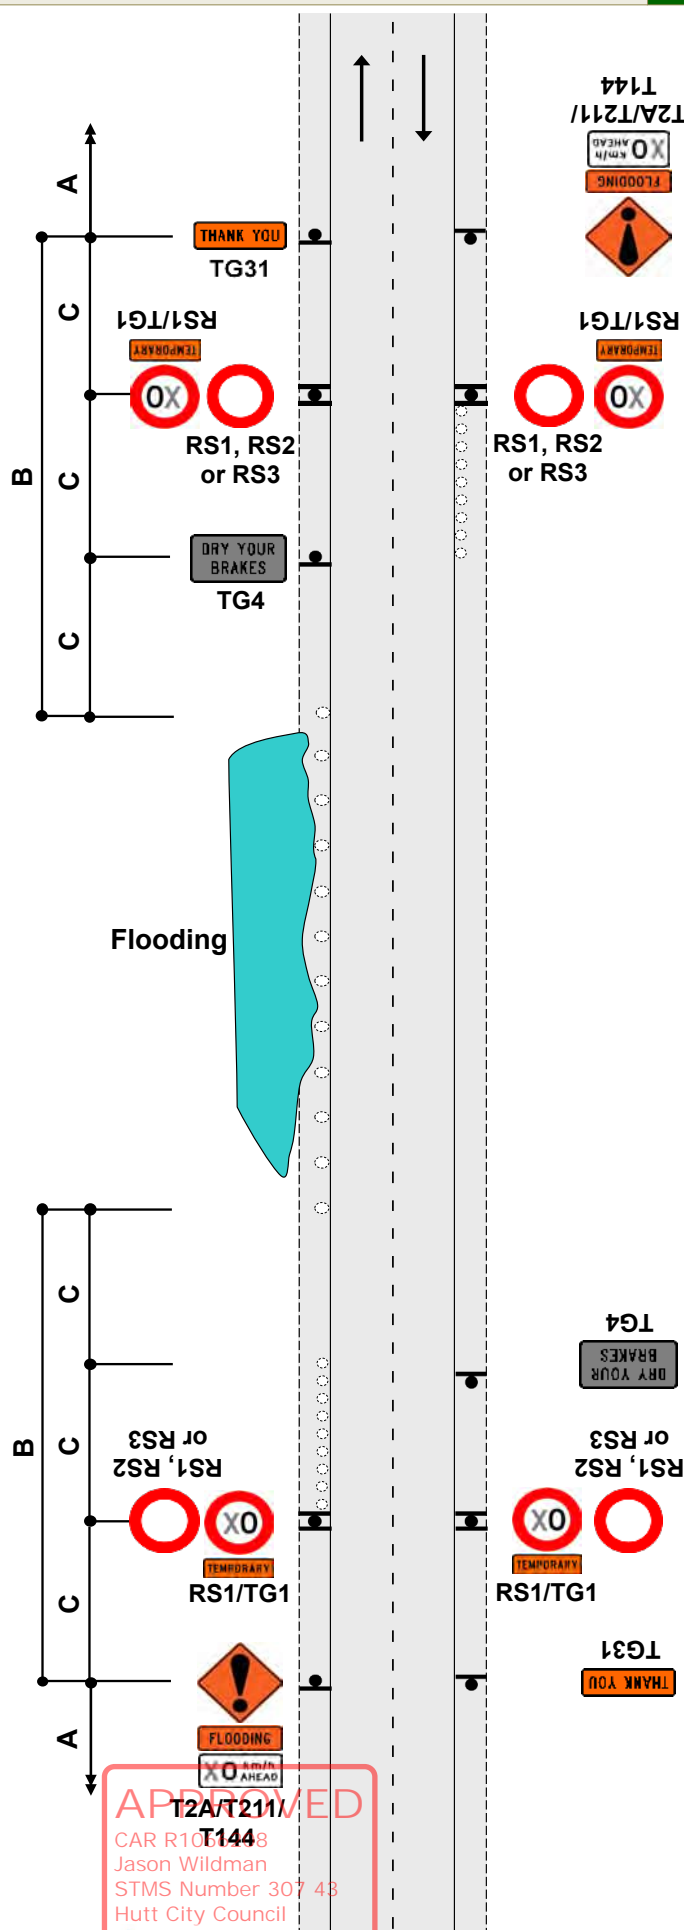

TWO-WAY TWO-LANE ROAD

Unattended worksites


New seal - unattended and/or unswept worksite

F2.27

Level 1



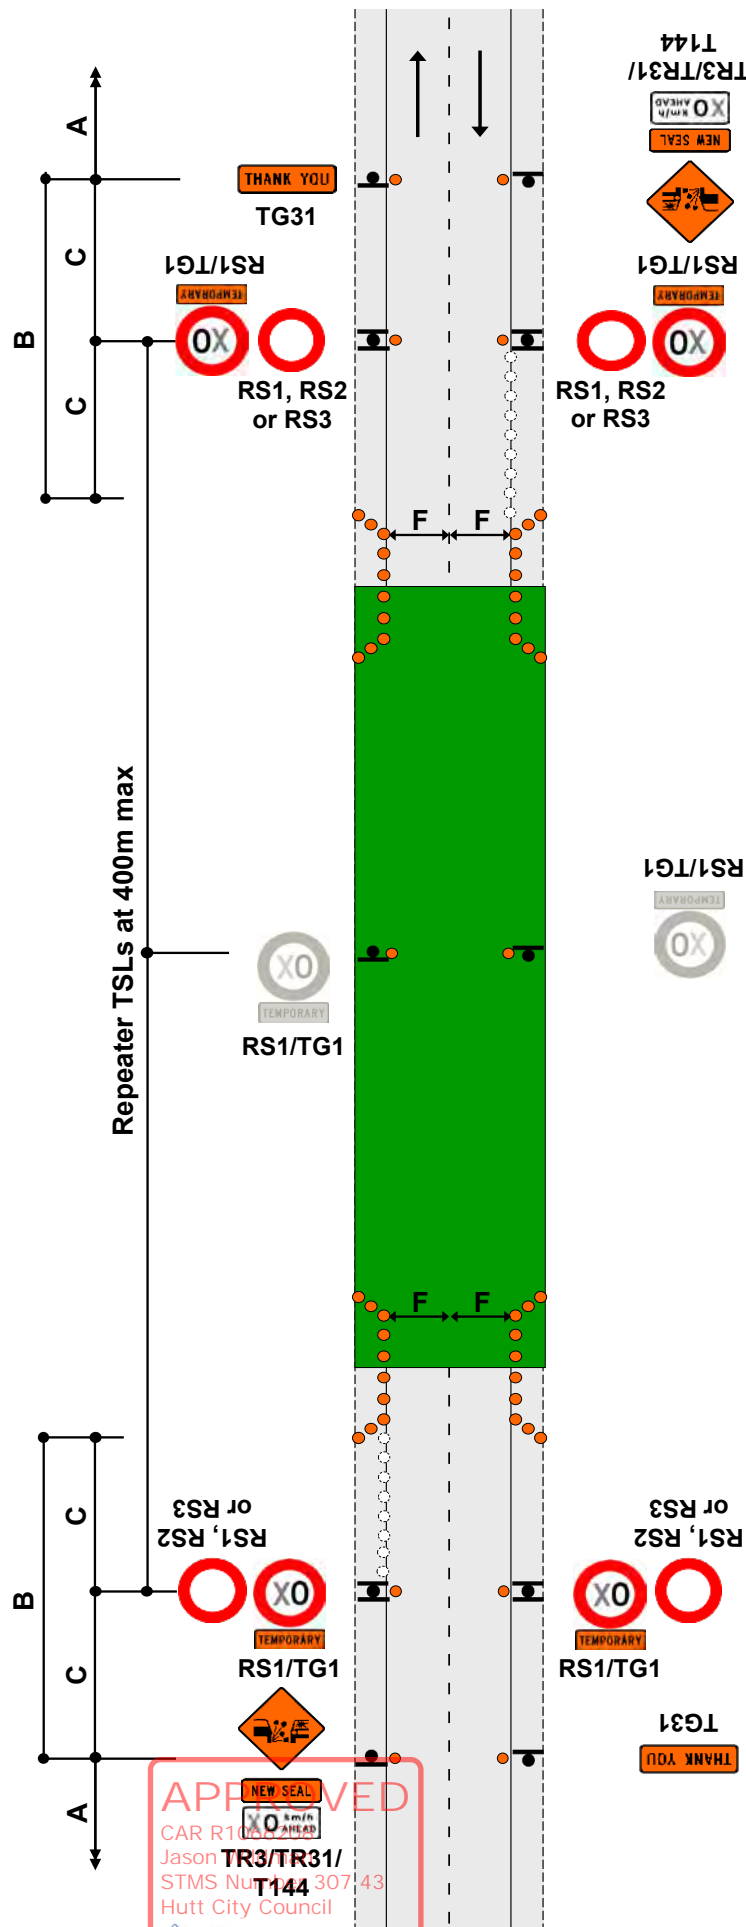


Notes

1. Use TSLs if required by TSL decision matrix
2. Worksites need positive traffic management to ensure all road users travel at the TSL
3. Use cones to form a threshold treatment at the start of the new seal. Minimum of 10 cones at 5m centres
4. Cones on the trafficked side of signs for sites to be left unattended overnight
5. TSLs to be repeated at not more than 400m intervals
6. The T144 X0km/h AHEAD sign is optional




Notes

1. This layout must not be used on an alignment with horizontal curves (corners) or when repairs are carried out on or near horizontal curves. See TMD F2.29
2. On long worksites, use 'Next X km' plates, repeat temporary speed limit signs at not more than 400m intervals
3. Signs for some alternative situations:

TR4		Uneven Surface
TR2		Slippery Surface
TR3		Gravel/Unsealed Surface
TR31		New Seal
TR32		Seal Repairs

4. Cones to be placed on left of carriageway for full length of hazard at 10m centres or at least 3 cones, whichever is the greater
5. Cones on the trafficked side of signs for sites to be left unattended overnight
6. Worksites need positive traffic management to ensure all road users travel at the TSL
7. Use TSLs if required by TSL decision matrix
8. The T144 X0km/h AHEAD sign is optional

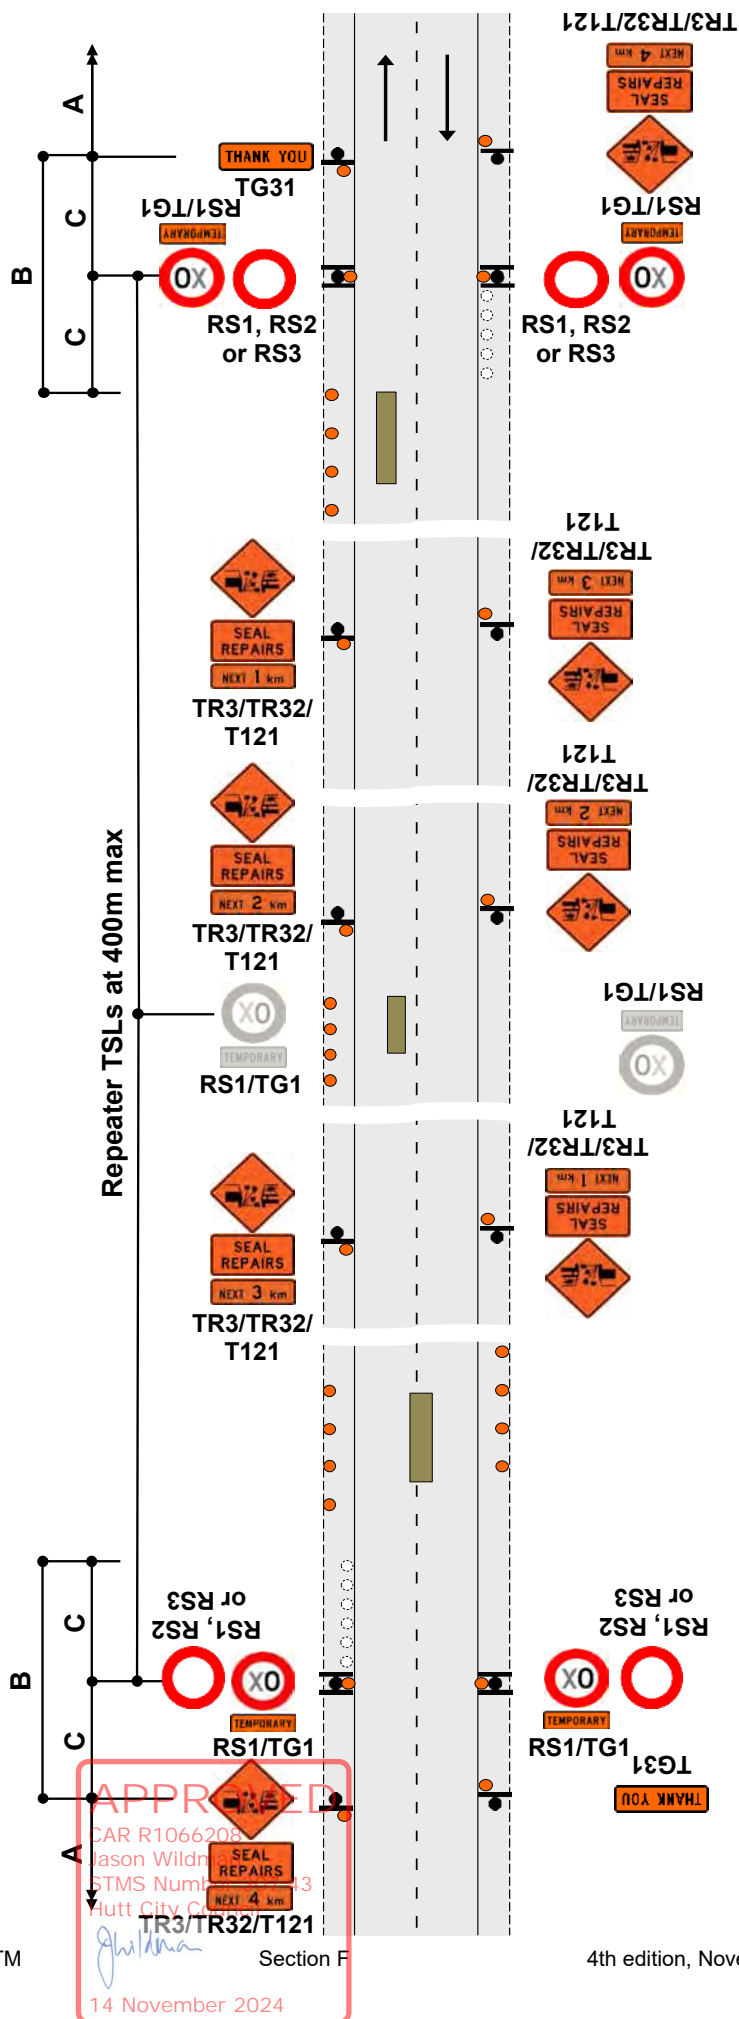

TWO-WAY TWO-LANE ROAD

Unattended worksites


Seal repairs on a curve

F2.29

Level 1

Notes

1. Cones on edge of seal - minimum 3 cones, maximum spacing 10m, next to each repair area
2. Cover any curve advisory speed sign that has a higher speed than the TSL
3. Use TSLs if required by TSL decision matrix
4. The T144 X0km/h AHEAD sign is optional

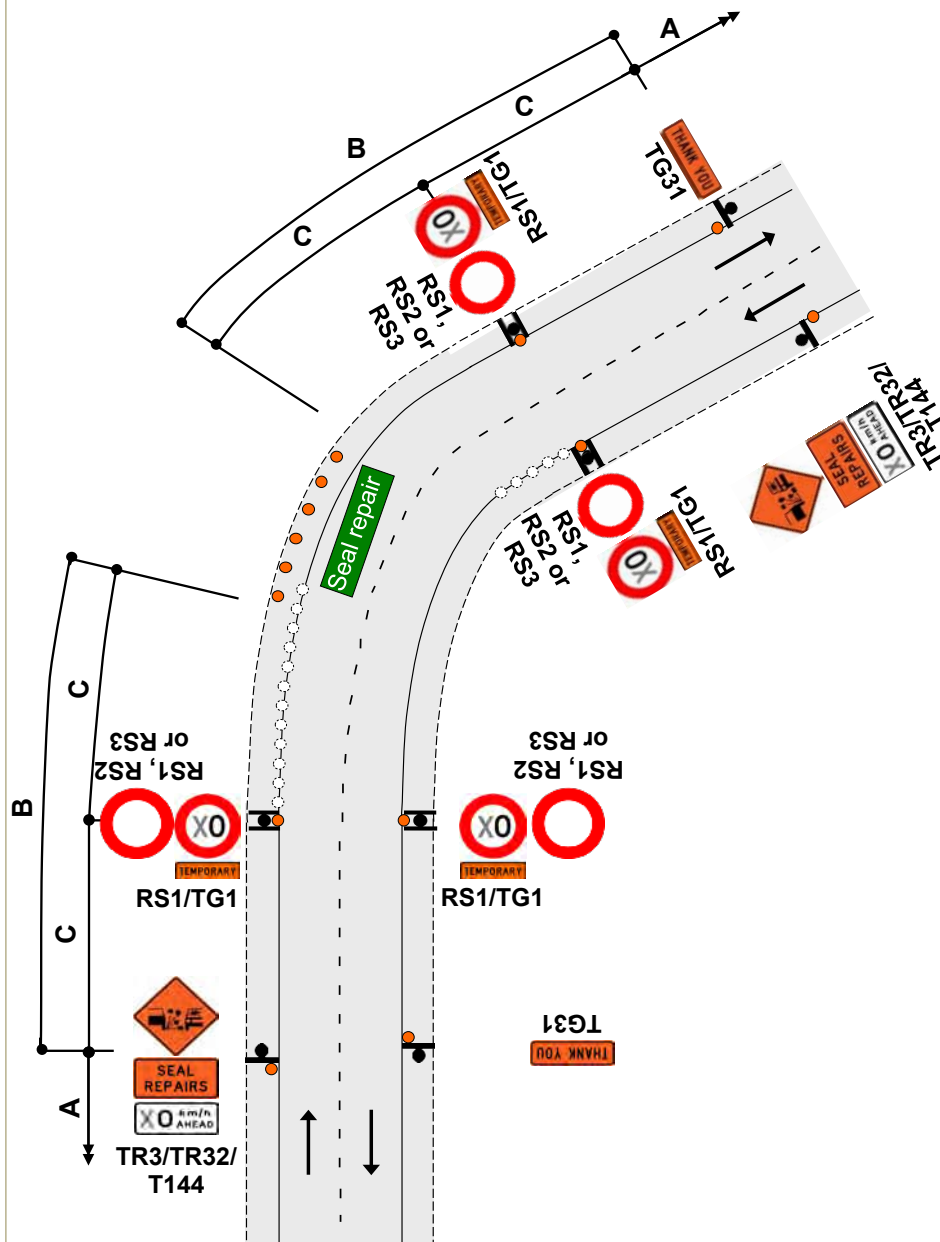

APPROVED

CAR R1066208
 Jason Wildman
 STMS Number 307 43
 Hutt City Council

Section F

14 November 2024

CC8 - Valve towards left of the lane

Mobile operations


TWO-WAY TWO-LANE ROAD

Personnel on the road - Valve towards left of the lane
50km/h or less

CC8
Level 1

Notes

1. The vehicle must be able to be driven with a Class 1 drivers license
2. There must be clear sight distance to the vehicle of at least 75m. This means that this operation cannot be completed within 75m of a corner or the brow of a hill
3. Worker to exit and enter the vehicle when there is a gap in traffic
4. The worker must not work within 10m of the vehicle (10m roll ahead)
5. The worker cannot be behind the vehicle unprotected in the live lane

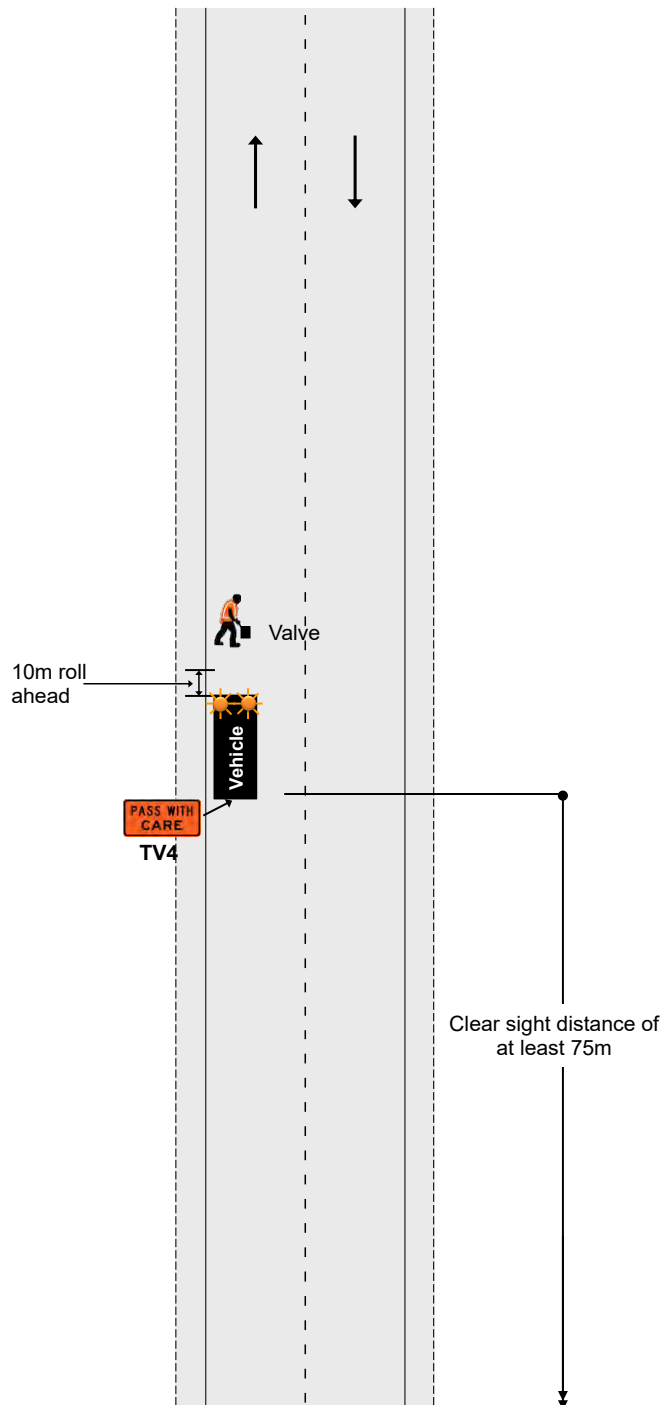

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43

14 November 2024

CC9 - Valve towards right of the lane

Mobile operations

TWO-WAY TWO-LANE ROAD


Personnel on the road - Valve towards right of the lane

50km/h or less

CC9
Level 1

Notes

1. The vehicle must be able to be driven with a Class 1 drivers license
2. There must be clear sight distance to the vehicle of at least 75m. This means that this operation cannot be completed within 75m of a corner or the brow of a hill
3. Worker to exit and enter the vehicle when there is a gap in traffic
4. The worker must not work within 10m of the vehicle (10m roll ahead)
5. The worker cannot be behind the vehicle unprotected in the live lane
6. TG2 WORKS END sign has been omitted for this mobile operation as end of works notification is achieved when road users can no longer see the flashing amber beacons

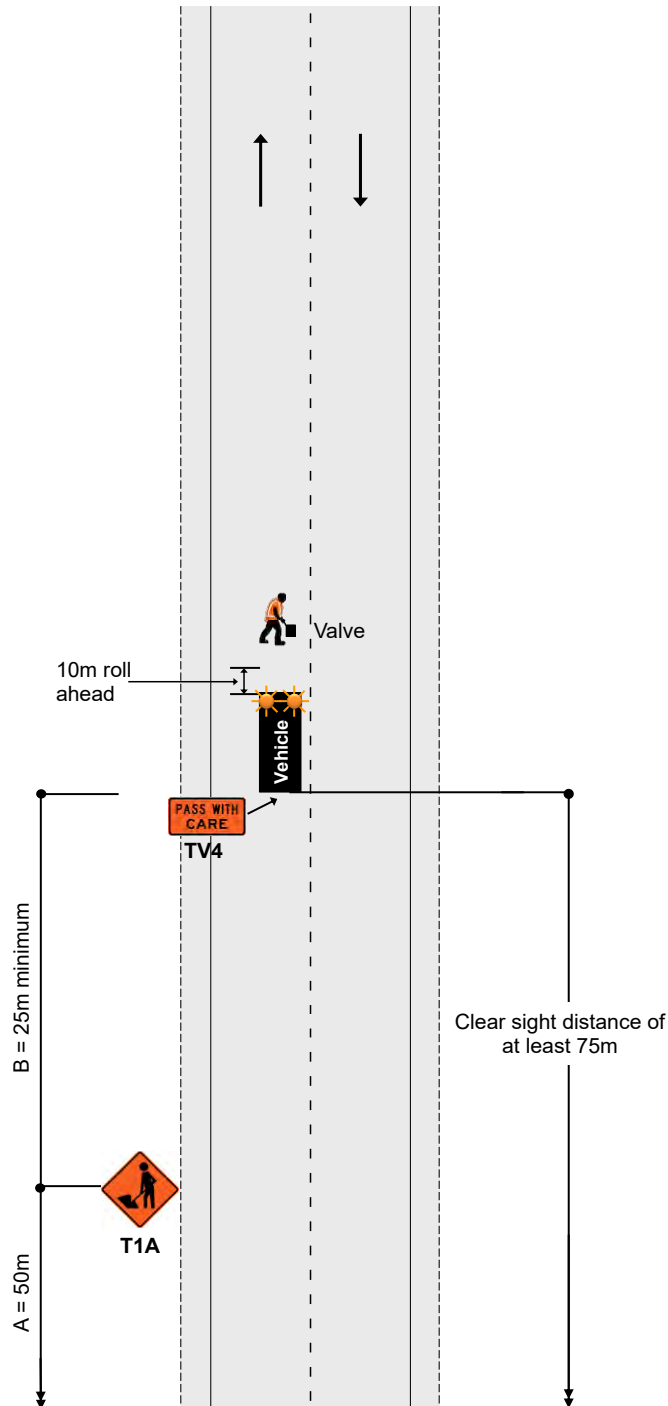

APPROVED

CAR R1066208

Jason Wildman

STMS Number 3072 43

14 November 2024

CC12 - Less than 75m CSD


Mobile operations

TWO-WAY TWO-LANE ROAD
Less than 75m CSD
50km/h or less

CC12
Level 1

Notes

1. Where a valve needs to be turned off where there is less than 75m clear sight distance in both directions (eg crest of a hill, on a corner or at a roundabout) then extend the shut off by turning off the nearest valve where 75m clear visibility can be achieved
2. If 50 houses or less are impacted by this extended shut off, then continue with the work activity
3. If more than 50 houses are impacted by this extended shut off, then get the TTM contractor to install TTM to enable the initial valve to be turned off/on safely

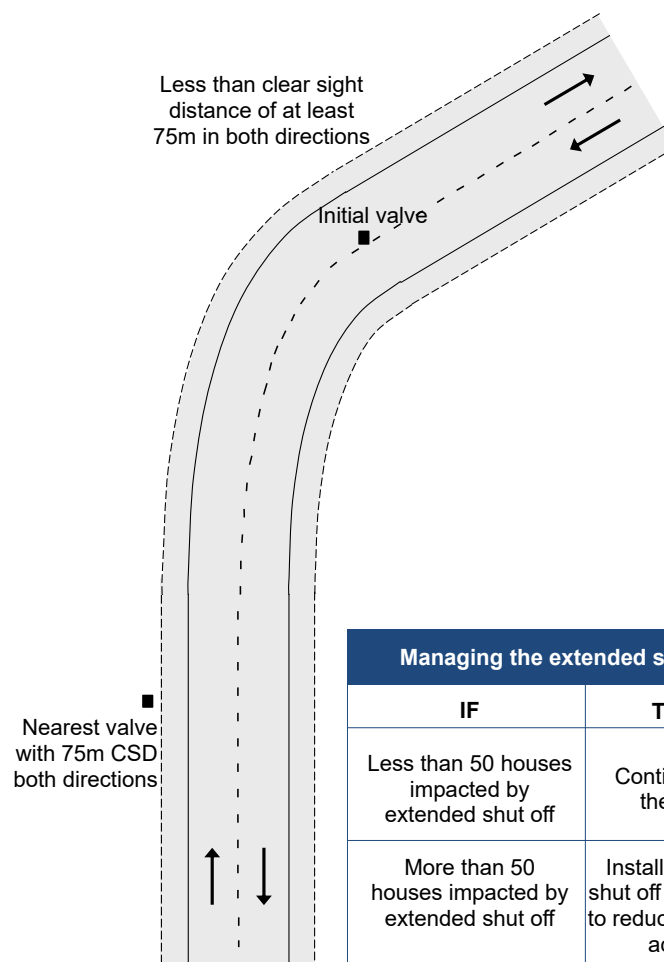

Managing the extended shut off

IF	THEN
Less than 50 houses impacted by extended shut off	Continue with the work
More than 50 houses impacted by extended shut off	Install TTM and shut off initial valve to reduce impact of activity

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43

14 November 2024


TWO-WAY TWO-LANE ROAD

Work vehicle is more than five (5) metres from the edgeline

Any speed

F4.1

Level 1

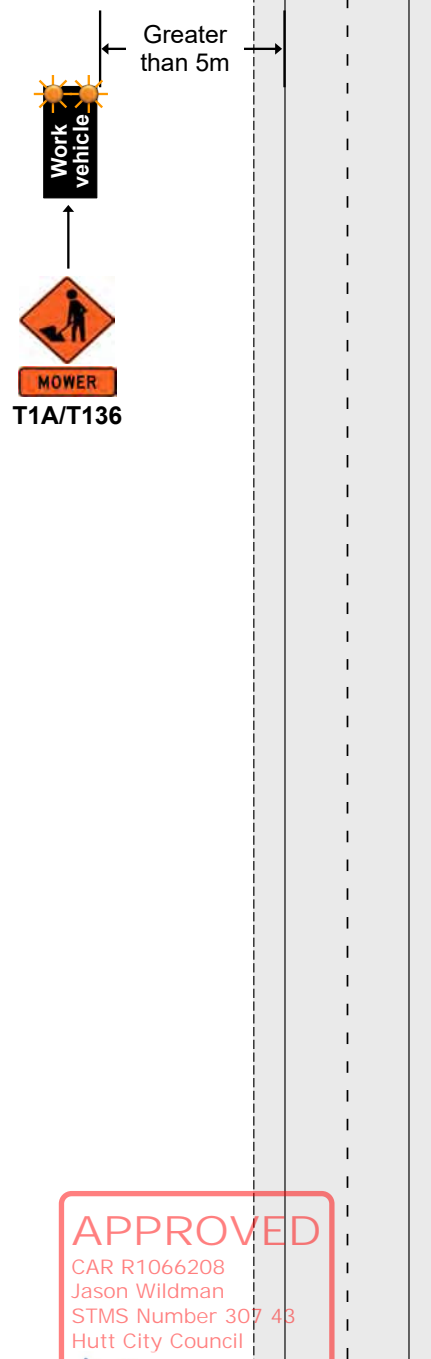

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council

Jason Wildman

14 November 2024

Mobile operations

TWO-WAY TWO-LANE ROAD


Work vehicle is within five (5) metres of the edgeline

CSD to work vehicle - not required under 65km/h, required over 65km/h

F4.2
Level 1

Notes

- 1.If permanent speed is under 65km/h, rear visibility to the work vehicle is not required
- 2.If permanent speed is over 65km/h, rear visibility to the work vehicle is required
- 3.A tail pilot vehicle equipped with T1A advance warning sign, appropriate supplementary plate and RD6R may replace the static signs if the permanent speed is under 65km/h (see TMD F4.3)

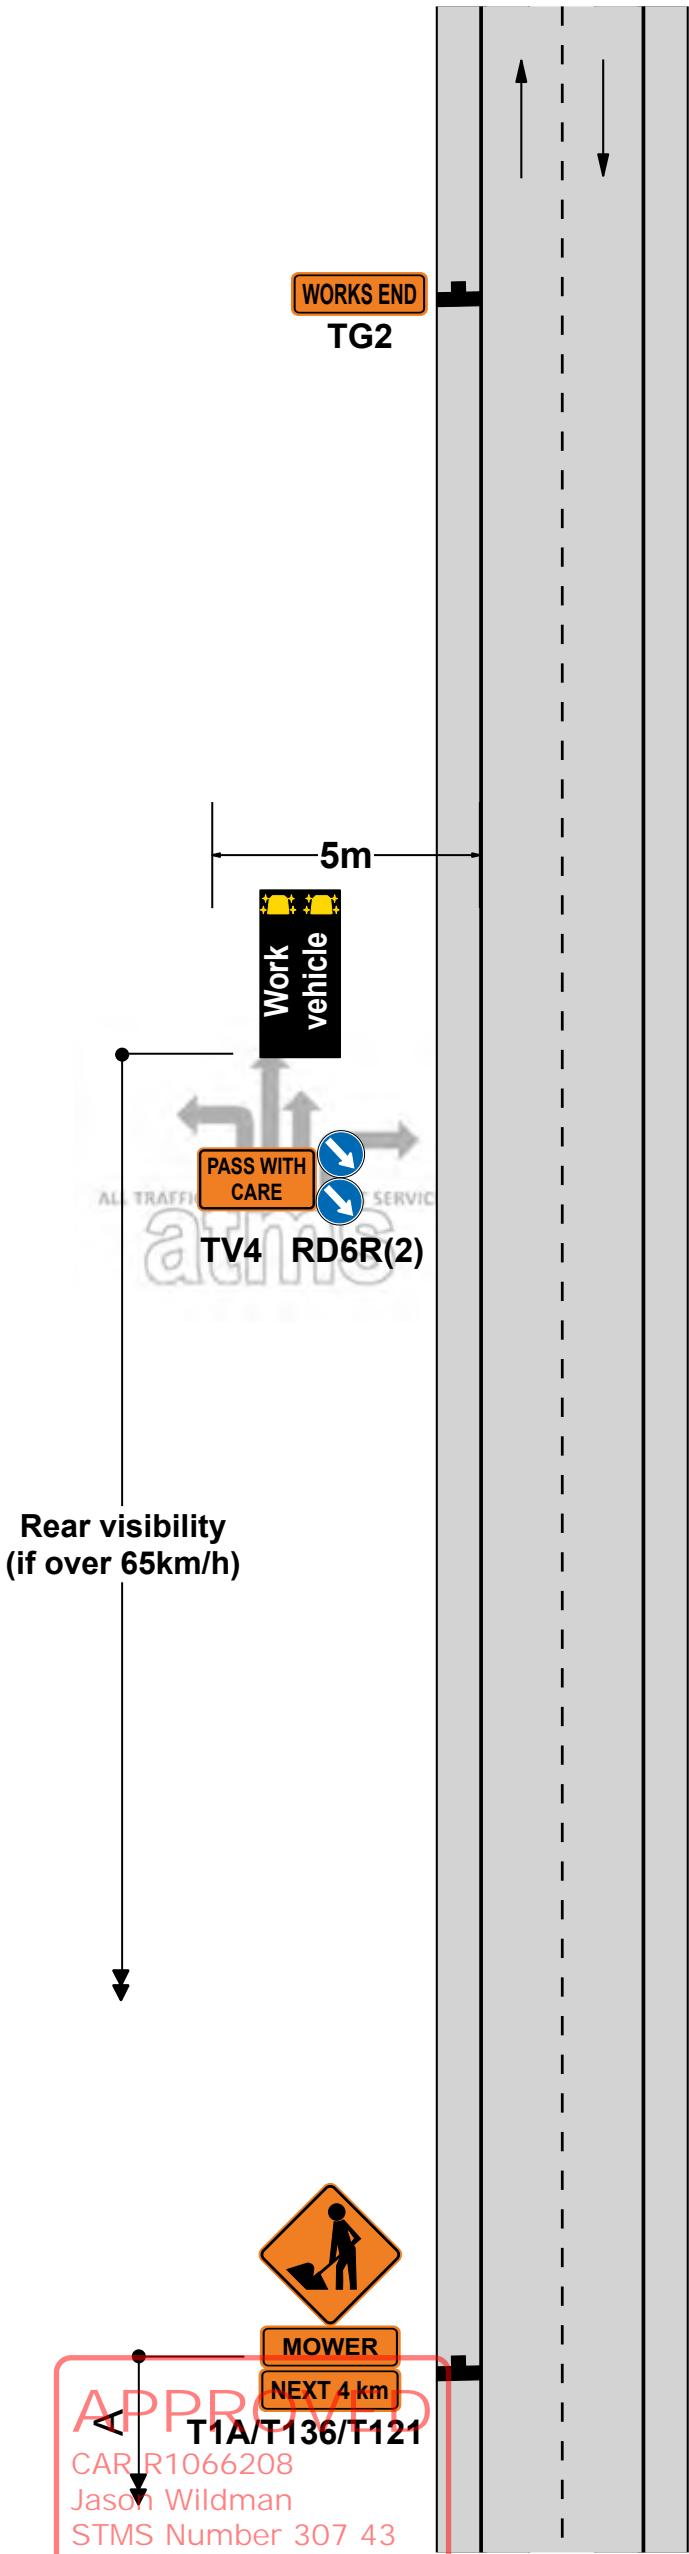


Mobile operations

TWO-WAY TWO-LANE ROAD
Work vehicle is within five (5) metres of the edgeline
Speed limit over 65km/h - the rear visibility is less than CSD

F4.3
Level 1

Notes

1.This TMD can replace
TMD F4.2 when
permanent speed is
under 65km/h. In these
situations, static signs
are not required

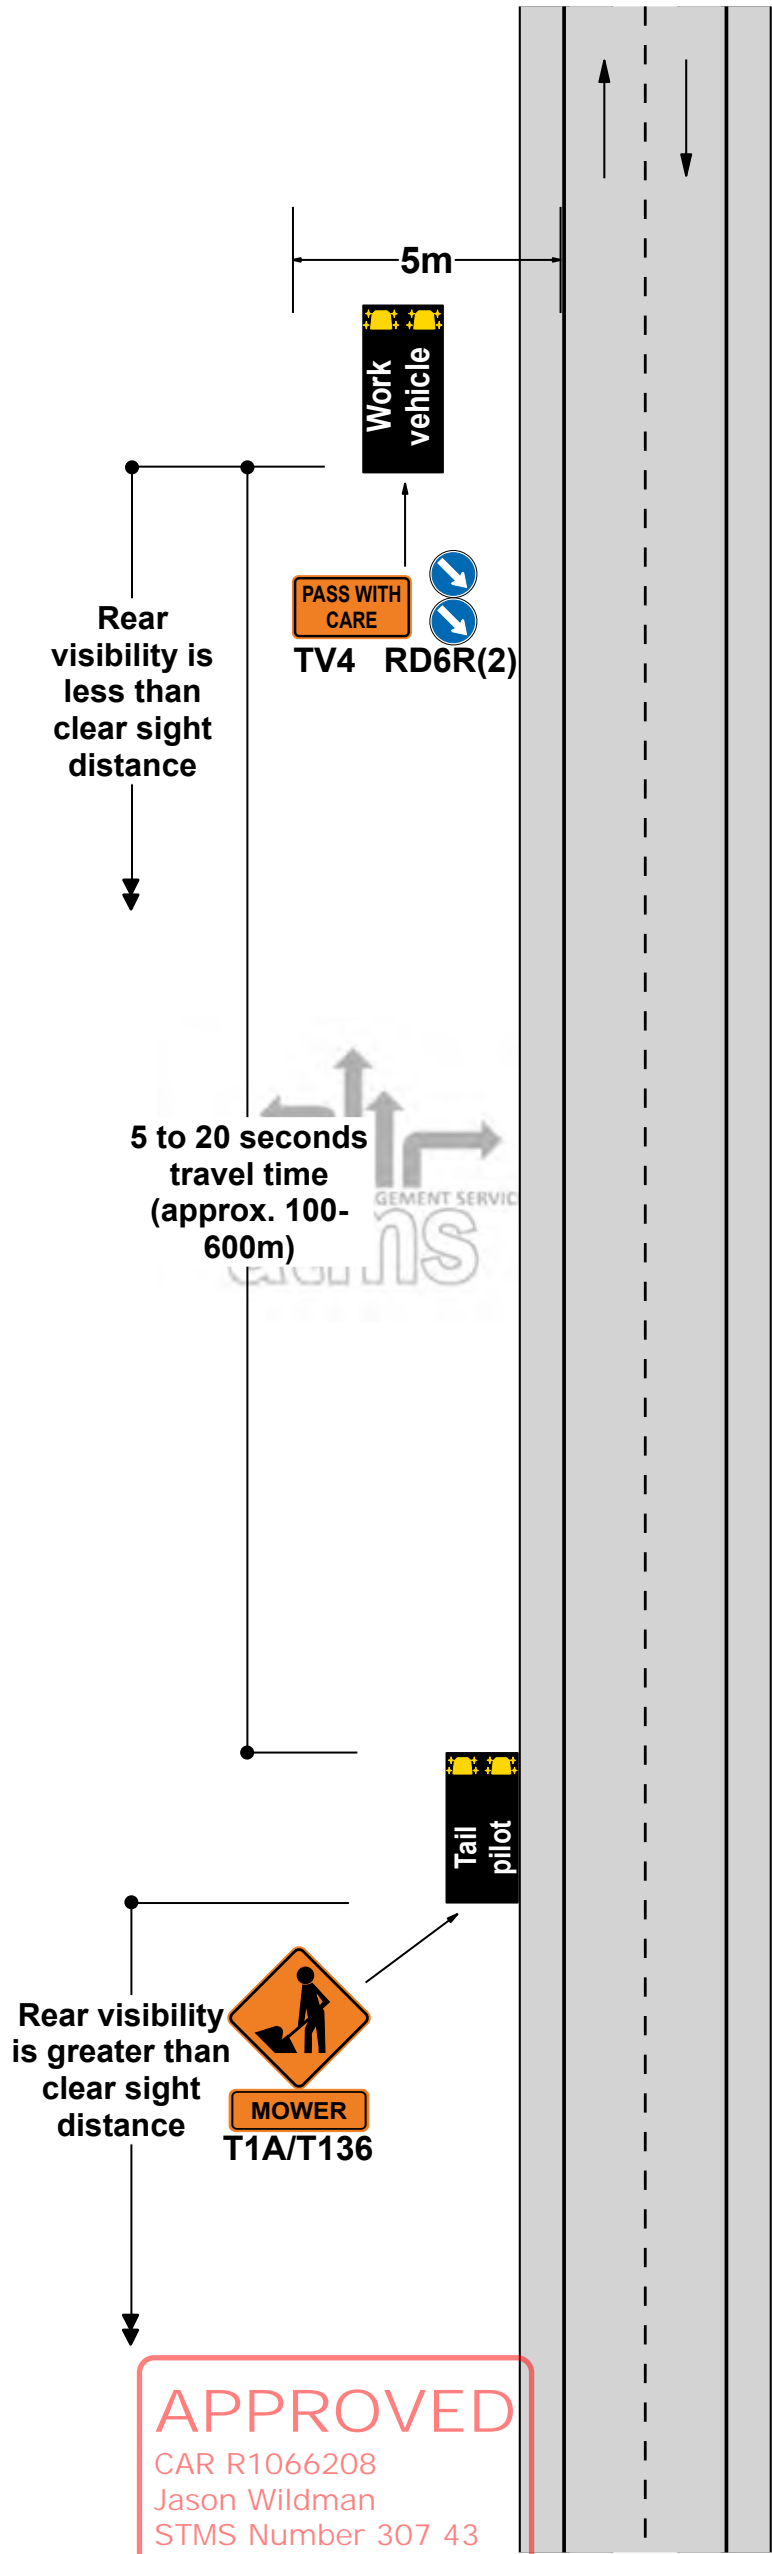

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council

14 November 2024

TWO-WAY TWO-LANE ROAD

Work vehicle is in a lane


Permanent speed under 65km/h

F4.4

Level 1

Notes

1. Advance warning sign X may be replaced by tail pilot equipped with T1A advance warning sign and appropriate supplementary plate
2. In this case, signs marked with Y do not need to be erected
3. If using static advance warning signs and the operation is on the lane, then static advance warning signs must also be placed on any intersecting roads

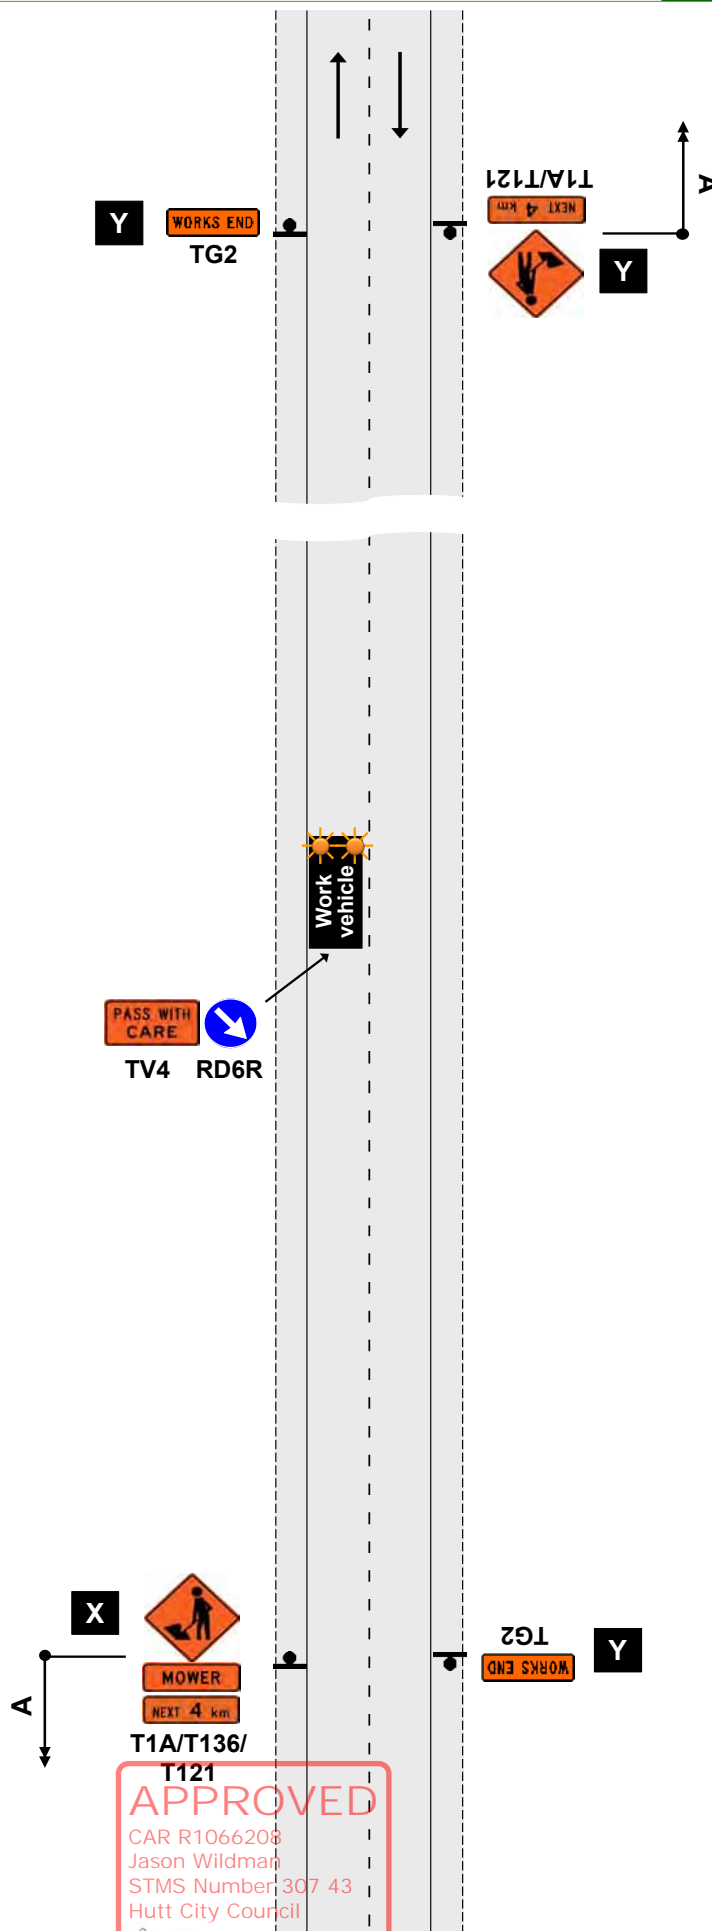


ATMS06

Level 1

Semi-static closure - work for up to 1 hour

Notes

1. Only use this TMD when activity can be completed within 1 hour (excluding set up and removal of worksite)
2. The T1A advance warning signs may be replaced by a tail pilot vehicle with a T1A sign, appropriate supplementary plate and a RD6R/L
3. If shadow vehicle is fitted with a TMA, the longitudinal safety zone (D) is not required
4. If using static advance warning signs and the operation is on the lane, then static advance warning signs must also be placed on any intersecting roads.
5. This site can be used on the opposite (left) lane also.

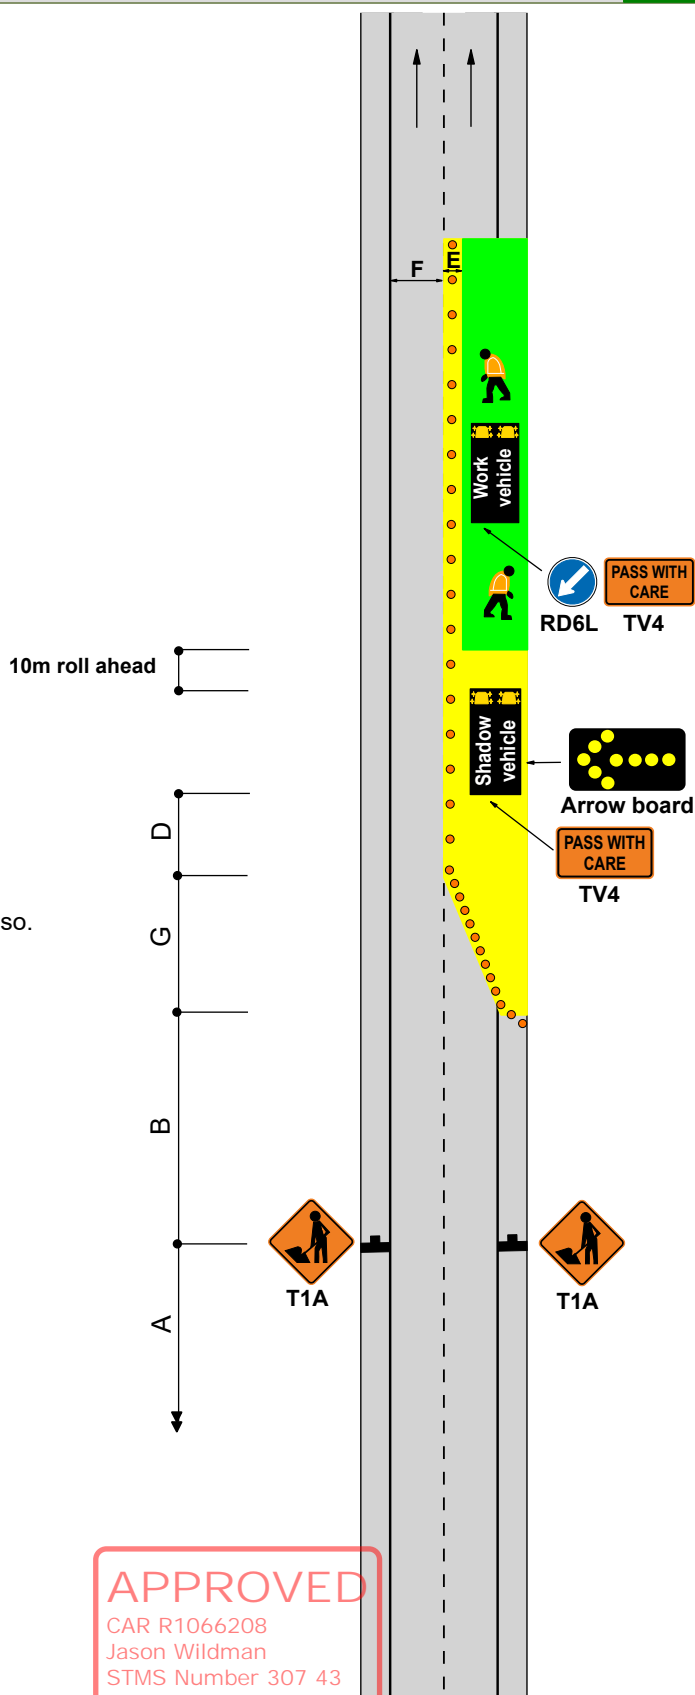


APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council

Gildman

14 November 2024

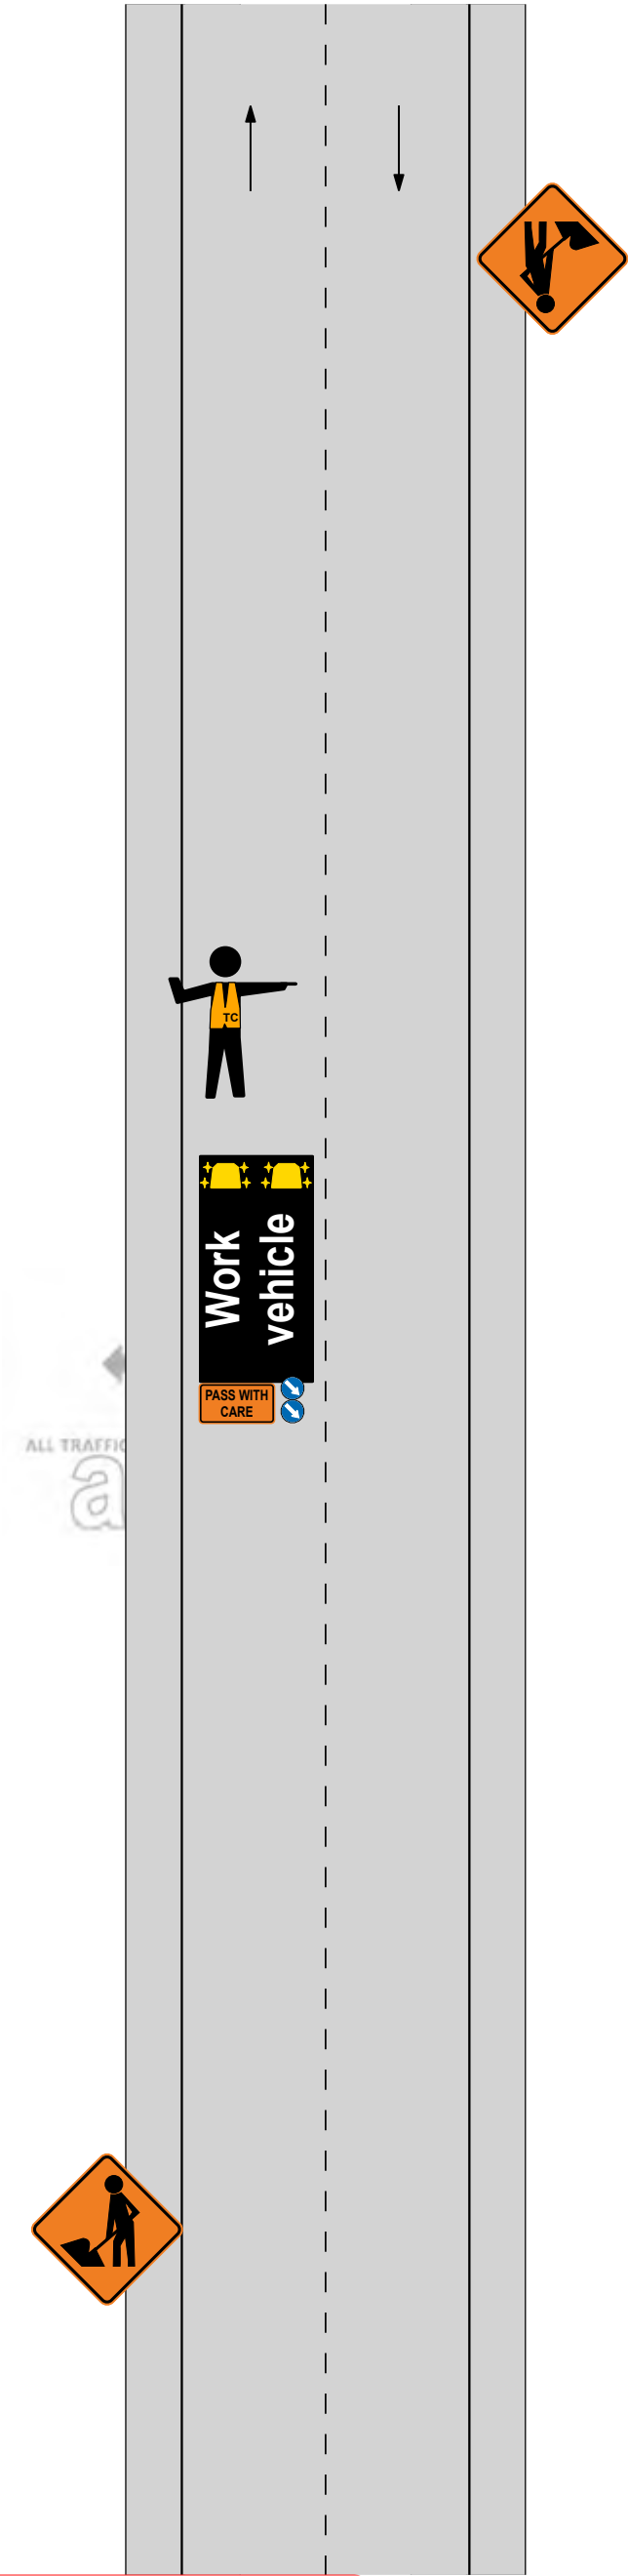

Closure: Level 1 Mobile Closure

Level: 1

TMP Ref: Mobile L1 - TTM Install/Removal

APPROVED

CAR R1066208

Jason Wildman

STMS Number 307 43

Hutt City Council

14 November 2024




Static operations

CYCLE LANE
Traffic crossing road centre
Diverted cycle lane - coned lane control

F2.9
Level 1

Notes

1. Minimum cycle lane width must be:
 - 1m - 50km/h or less
 - 1.5m - 60km/h or more
2. A minimum cycle lane width of 1.5m is required if the temporary cycle lane is uphill
3. *Calculation of taper length for lateral shift of less than 3.5m is:
 $W \times G$
3.5
W = Width of lateral shift
G = Taper length in metres from the level 1 layout distance table
4. To allow heavy vehicles to manoeuvre, cones in the channel must be offset by at least 10m where the direction changes. Refer C8.2.12
5. Use TSLs if required by TSL decision matrix
6. The T144 X0km/h AHEAD sign is optional

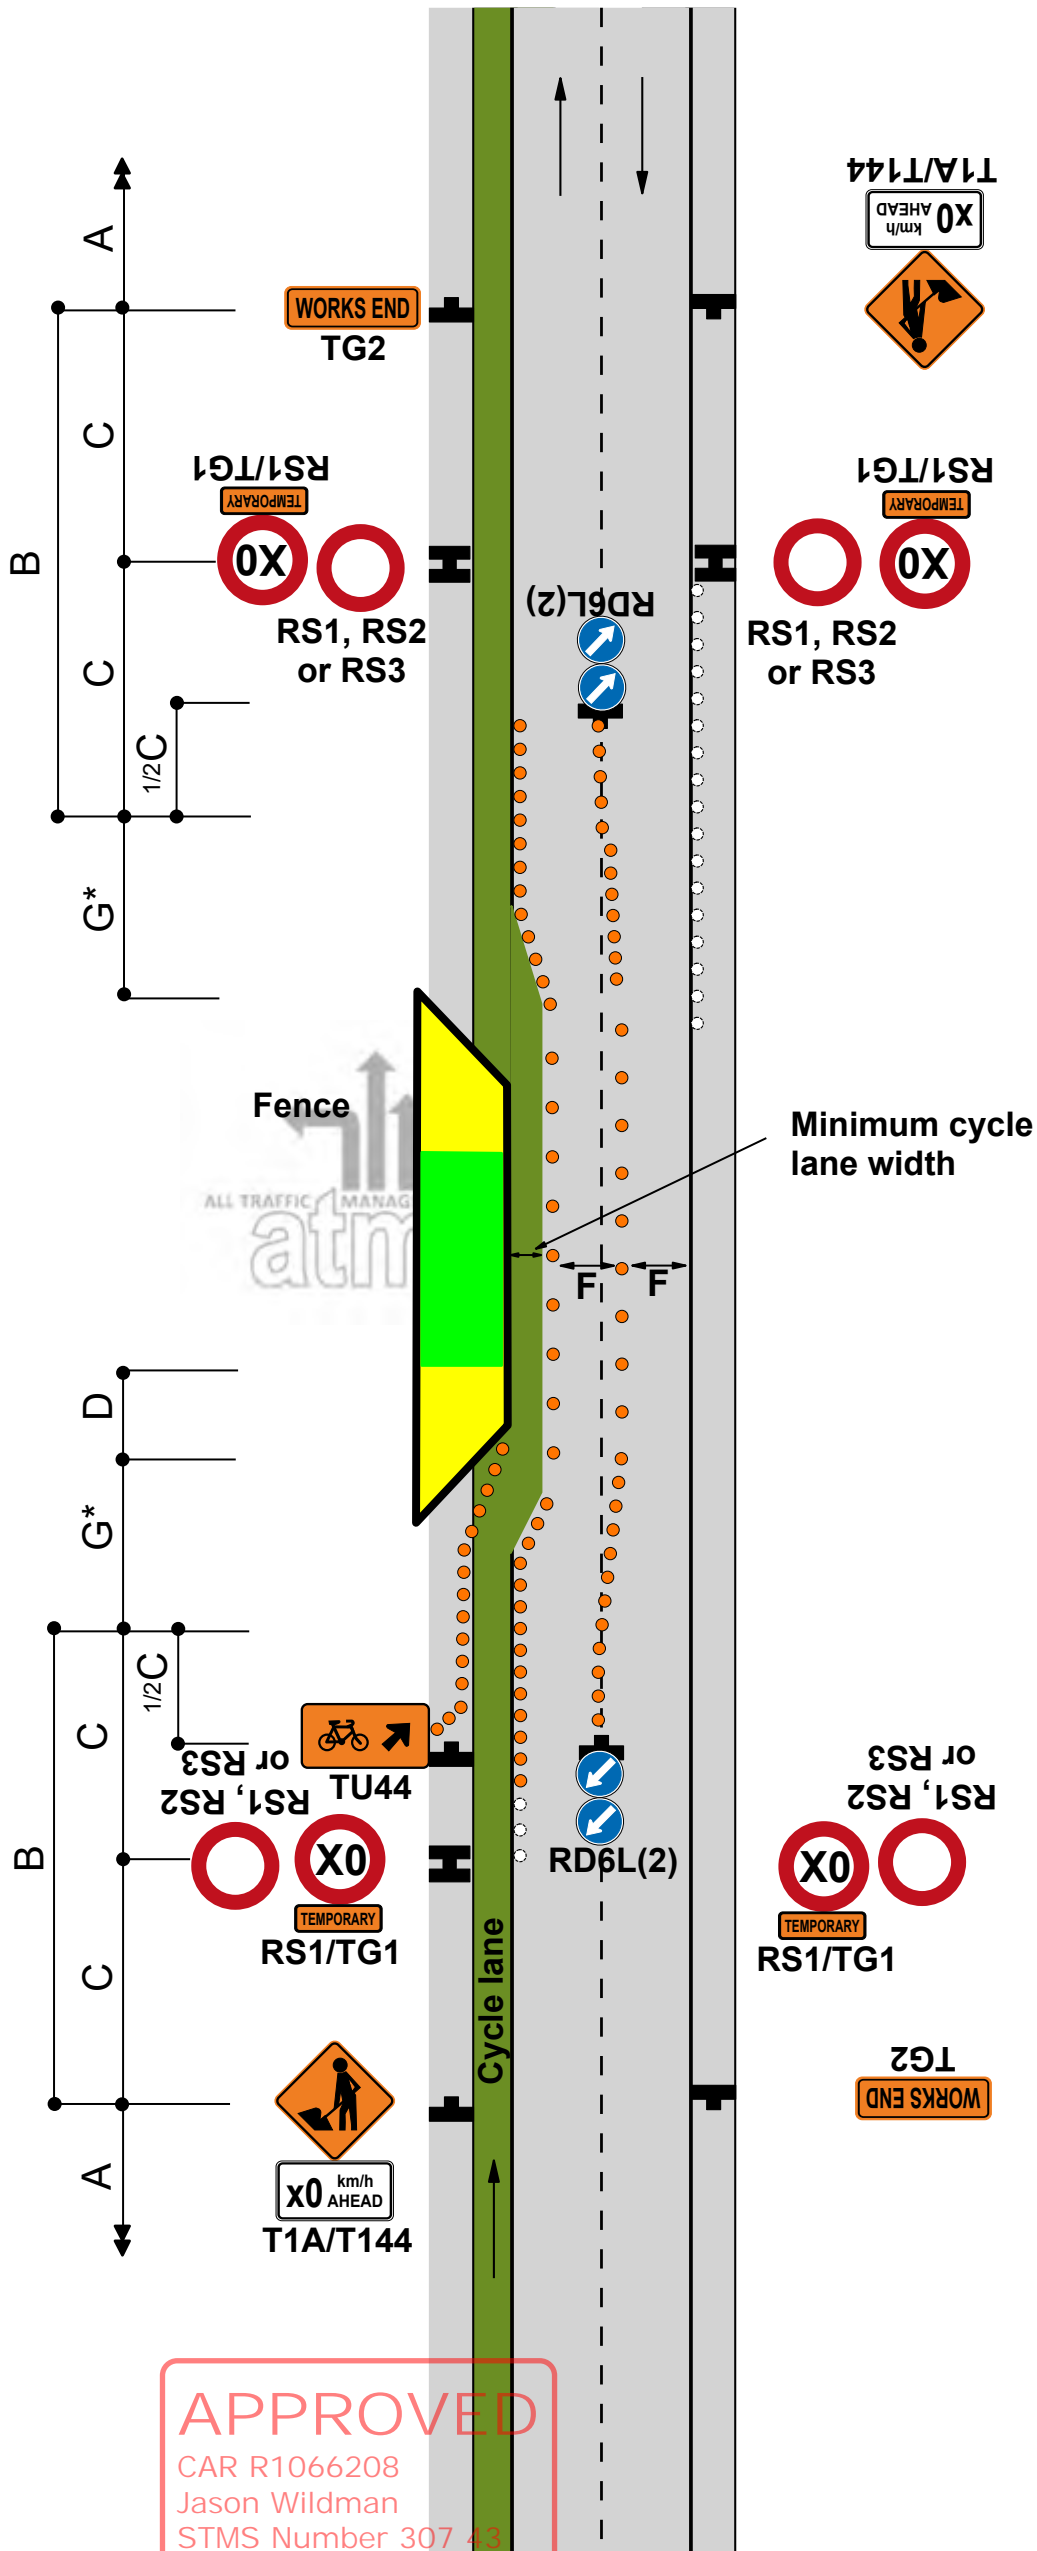

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council

14 November 2024

Static operations**CYCLE LANE**
Cycle lane closed
Portable e-STOP**ATMS03****Level 1****Notes**

1. Merge of cycle lane with live lane must be delineated with cones at 1.0m centres for at least 10m
2. The T144 30km/h AHEAD sign is optional on roads under 65km/h
3. Signs and layout shown in the box at the bottom of the diagram is to be repeated on each approach that requires cycle lane signage. ATMS01 or ATMS02 to be used on all non cycle lane approaches.
3. Provide details of make and model of portable traffic signals in the TMP
4. Use PN11 no stopping signs, if necessary as per the approved TMP

5. Install temporary RP61/RP62 signs.




7. Extend or place extra advance warning signs towards on-coming traffic beyond any expected traffic queues.

8. CONTINGENCY PLAN:
F2.14 or F2.22 to be implemented should issues arise with e-STOP/ adverse weather conditions or where stop go is unsuitable.
ex; Short term stoppages is defined as "stopping traffic for a short period of time within a static site, at inconsistent intervals to assist with the entry/exit of vehicles or small tasks required to be undertaken in the live lane".


9. In circumstances where for safety reasons, the use of stop/go operations is deemed more appropriate, a site specific safe work method statement must be prepared.

10. e-STOP can only be used on an attended site. e-STOPS must be manned at all times.

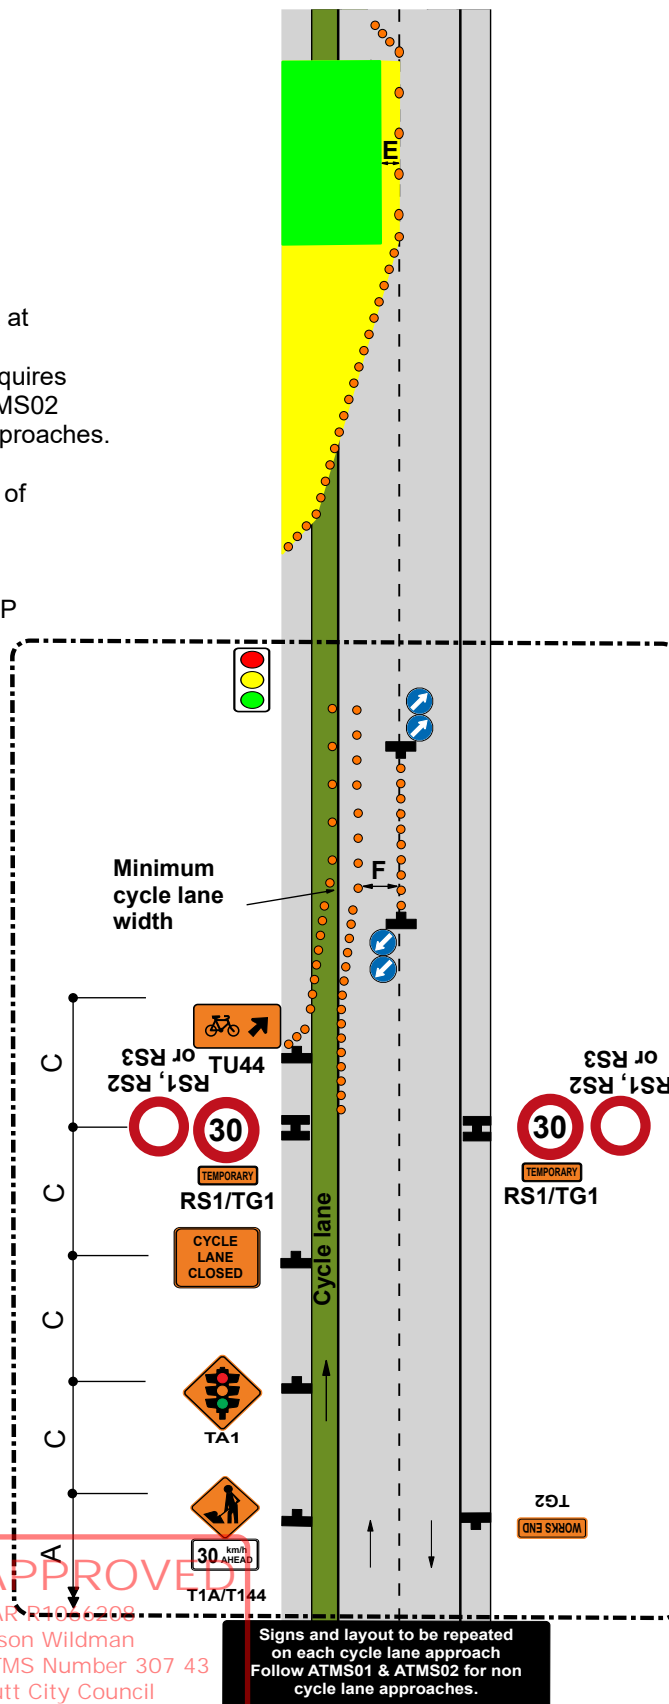

APPROVED
CAR R40-0208
Jason Wildman
STMS Number 307 43
Hutt City Council

14 November 2024

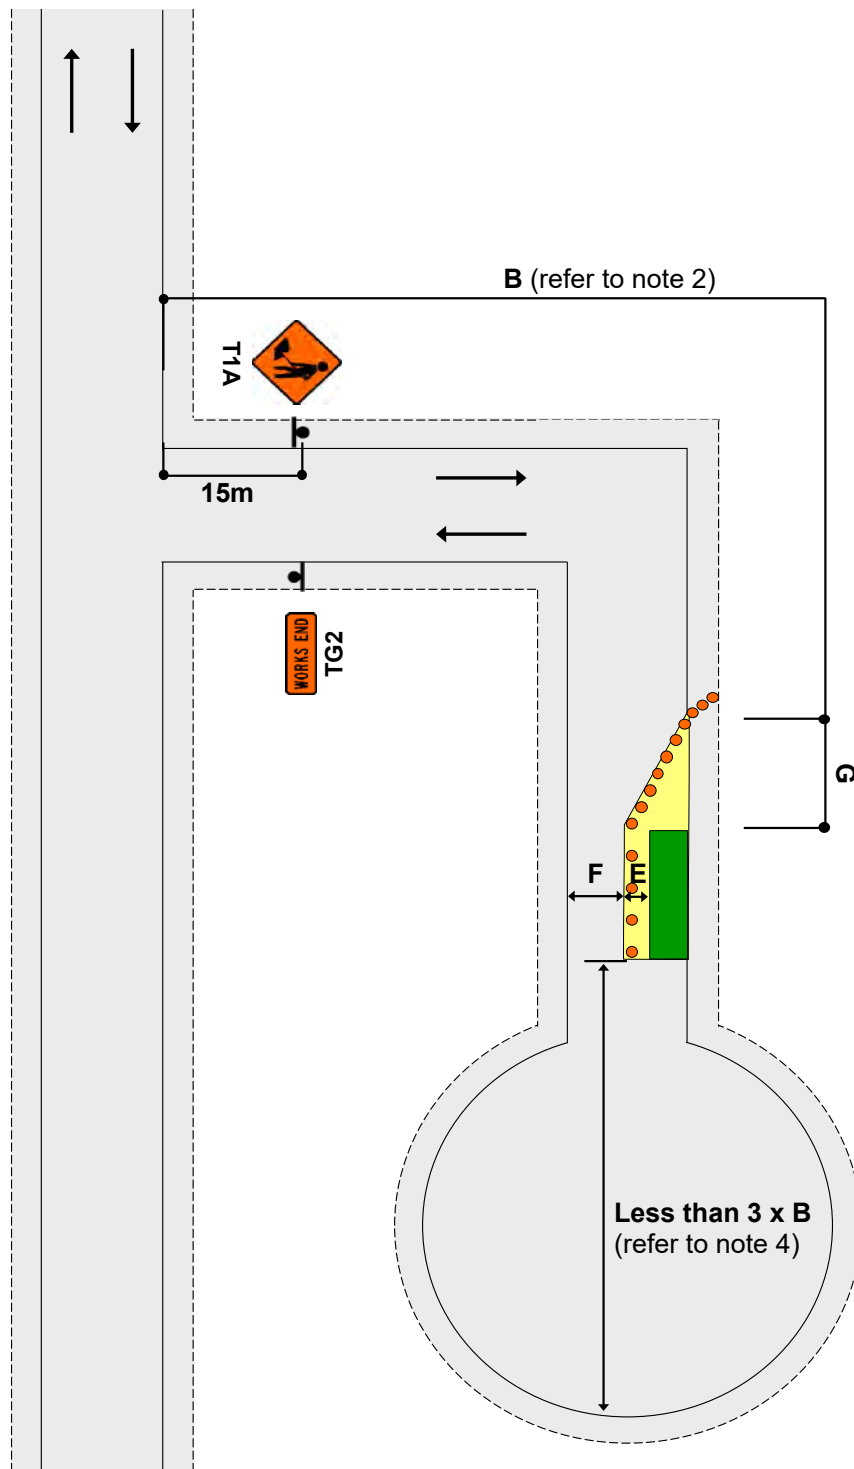


Notes

1. T1A sign to be placed at least 15m from the intersection
2. Where less than B, T1A/T135 and TG2 signs required on main road
3. Working space to be less than 100m
4. Signage is not required past the worksite where there is less than 3 x B from the end of the working space to the end of the road

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council

14 November 2024

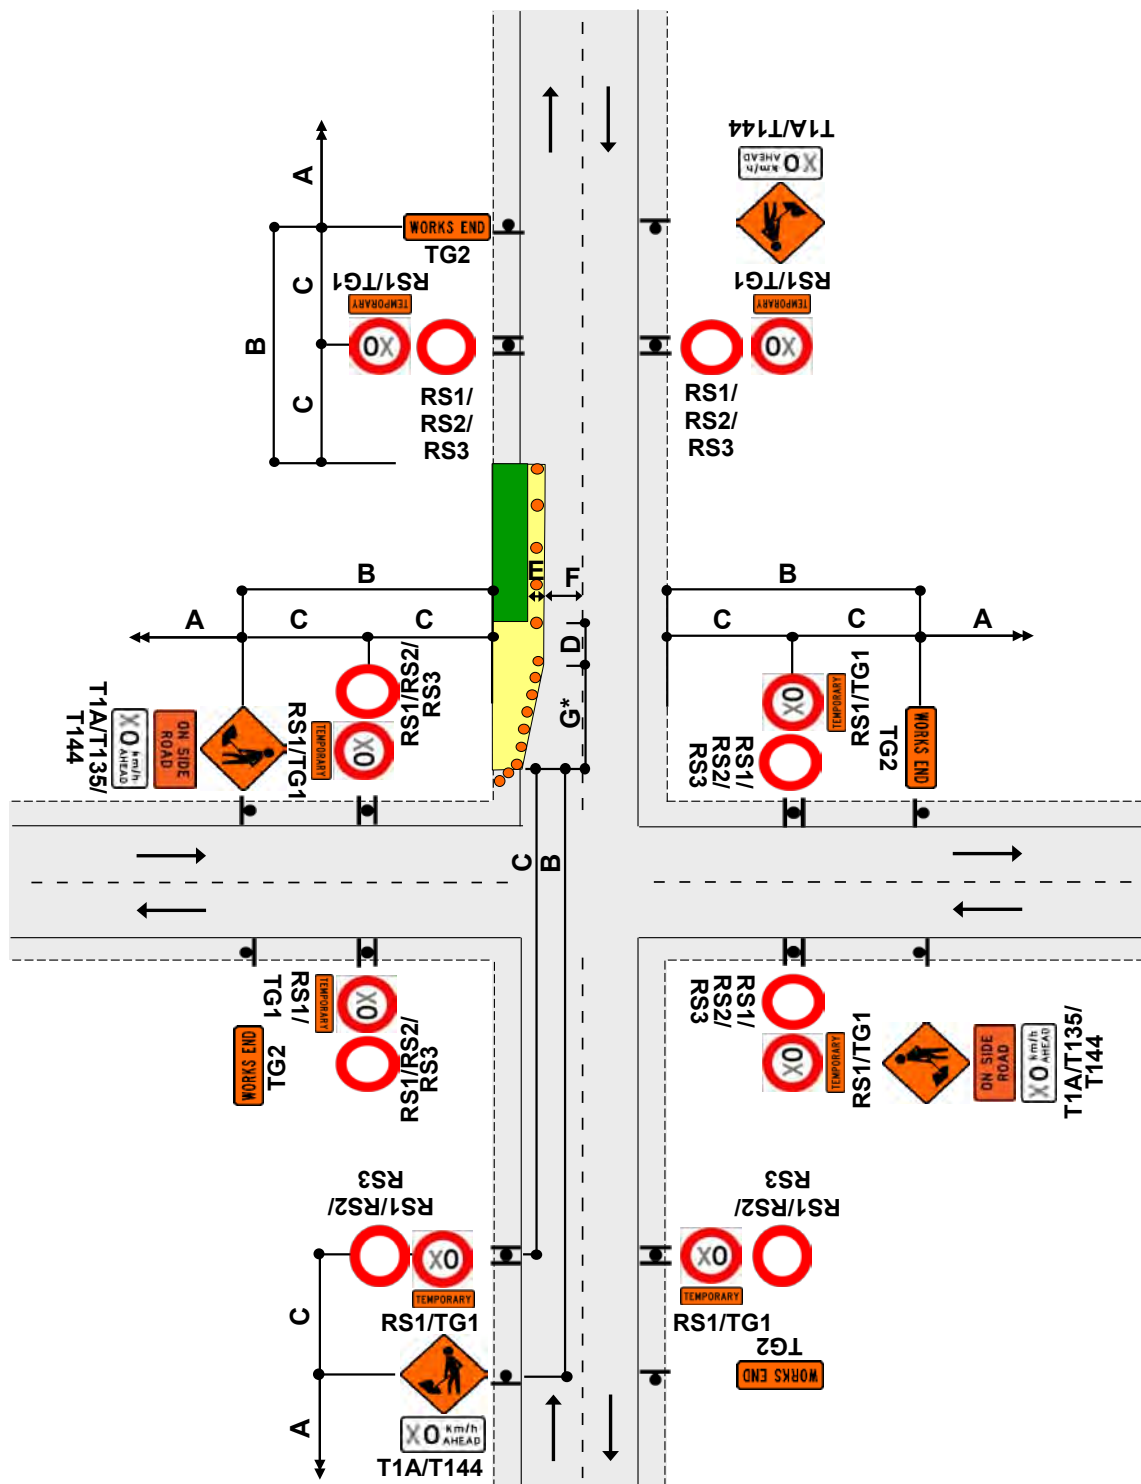


Notes

1. This diagram may be used at a T intersection by removing any one of the roads.
2. Taper length may be reduced by adding a RD6R sign
3. *Calculation of taper length for lateral shift of less than 3.5m is:

$$\frac{W \times G}{3.5}$$

W = Width of Shoulder G = Taper length in metres from the level 1 layout distance table

4. Use TSLs if required by TSL decision matrix
5. The T144 X0km/h AHEAD sign is optional



APPROVED


CAP R1066208

10/10/2024

STMS Number 307 43

Hutt City Council

14 November 2024

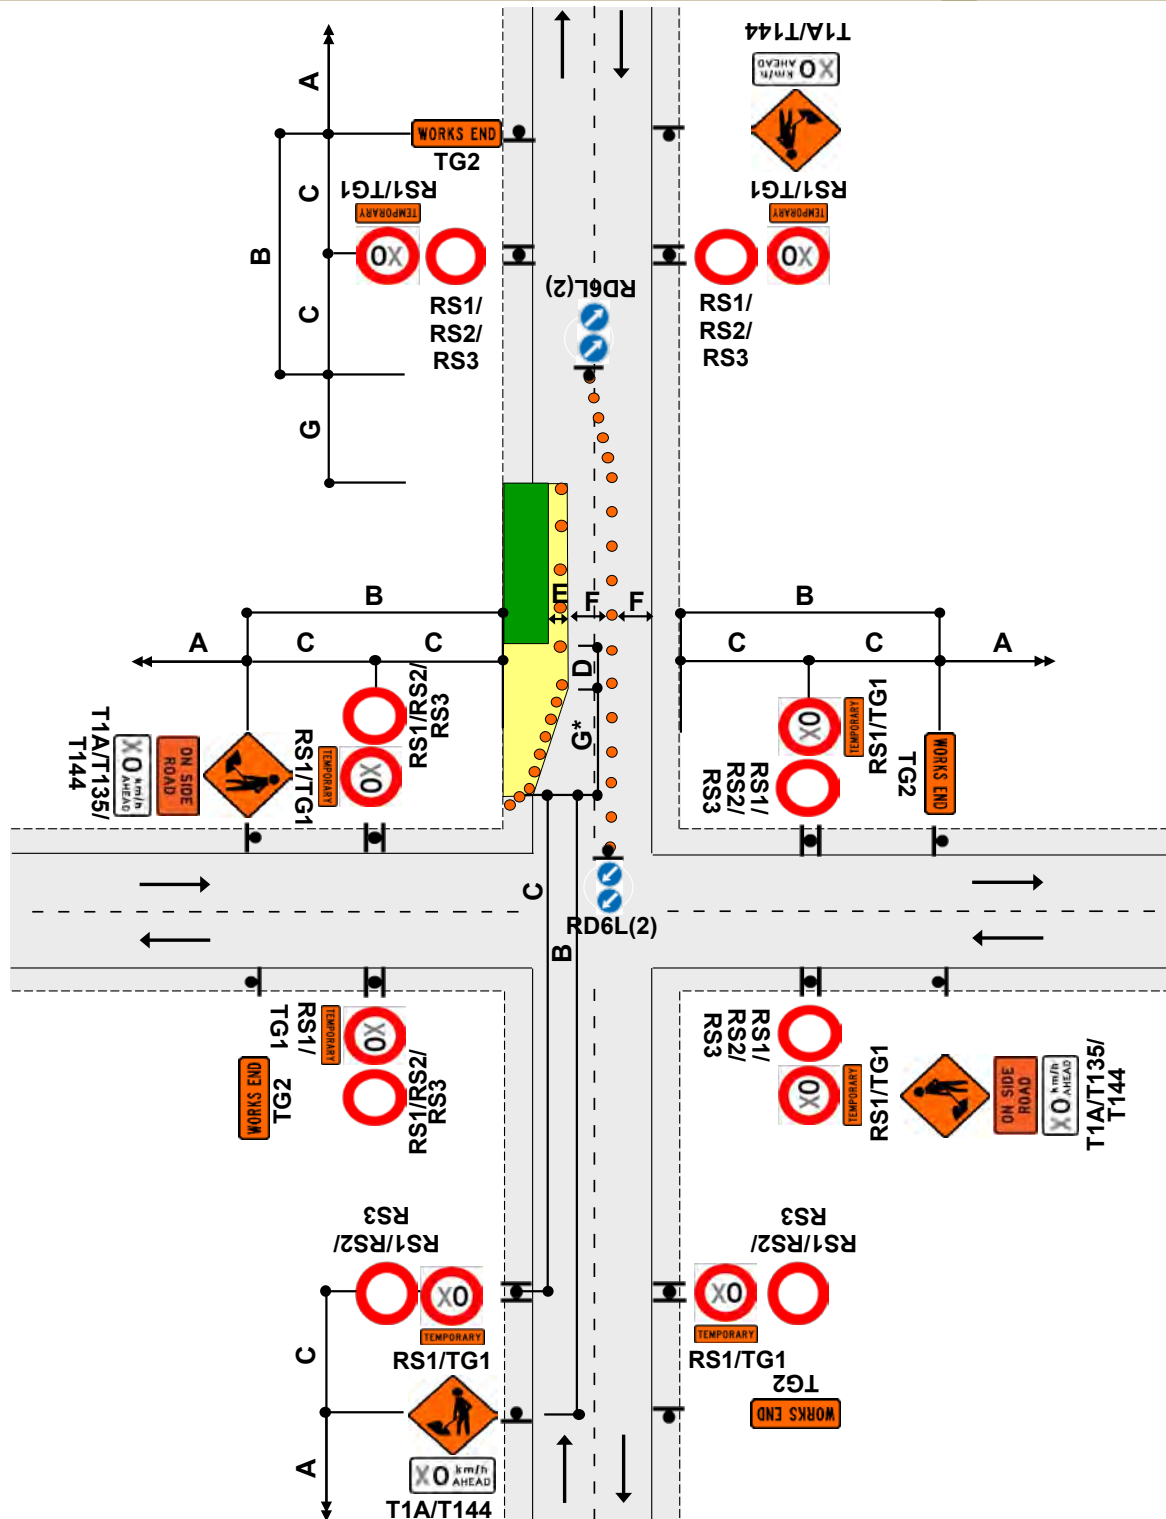


Notes


1. This diagram may be used at a T intersection by removing any one of the roads
2. Taper length may be reduced by adding a RD6R sign
3. *Calculation of taper length for lateral shift of less than 3.5m is:

$$\frac{W \times G}{3.5}$$

W = Width of Shoulder G = Taper length in metres from the level 1 layout distance table

4. Use TSLs if required by TSL decision matrix
5. The T144 X0km/h AHEAD sign is optional



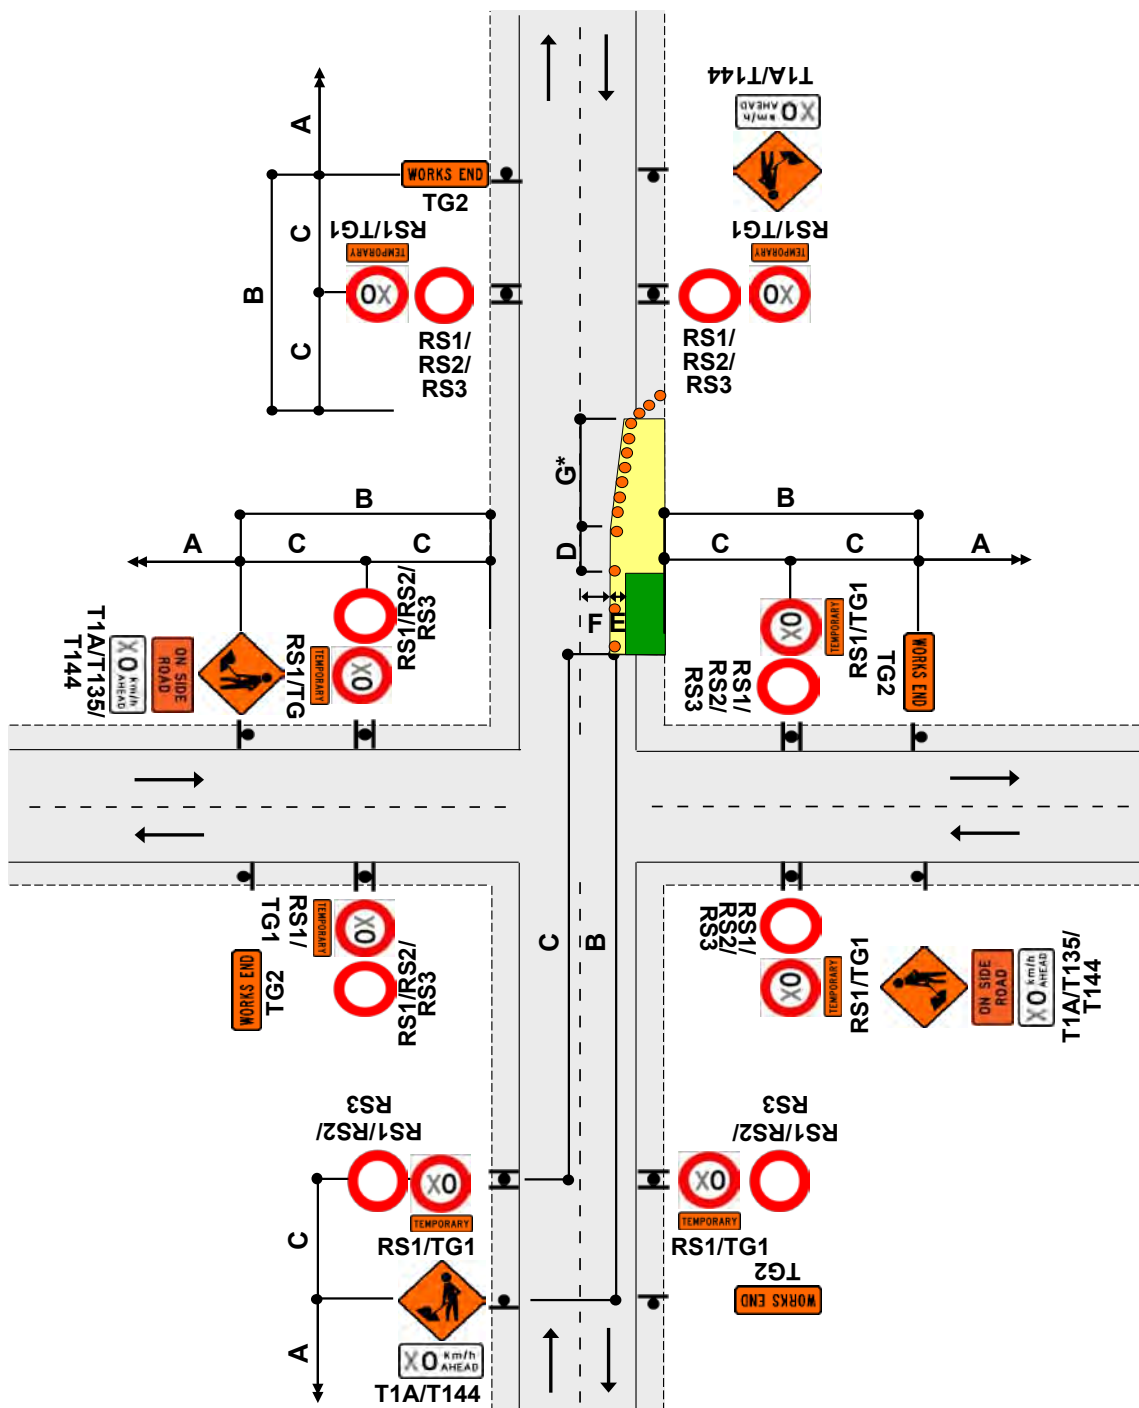


Notes

1. This diagram may be used at a T intersection by removing any one of the roads
2. Taper length may be reduced by adding a RD6R sign
3. *Calculation of taper length for lateral shift of less than 3.5m is:

$$\frac{W \times G}{3.5}$$

W = Width of Shoulder G = Taper length in metres from the level 1 layout distance table

4. Use TSLs if required by TSL decision matrix
5. The T144 X0km/h AHEAD sign is optional



APPROVED

CAR R1066208


Jason Wildman

STMS Number 307 43

Hutt City Council

8 CoPTTM

14 November 2024

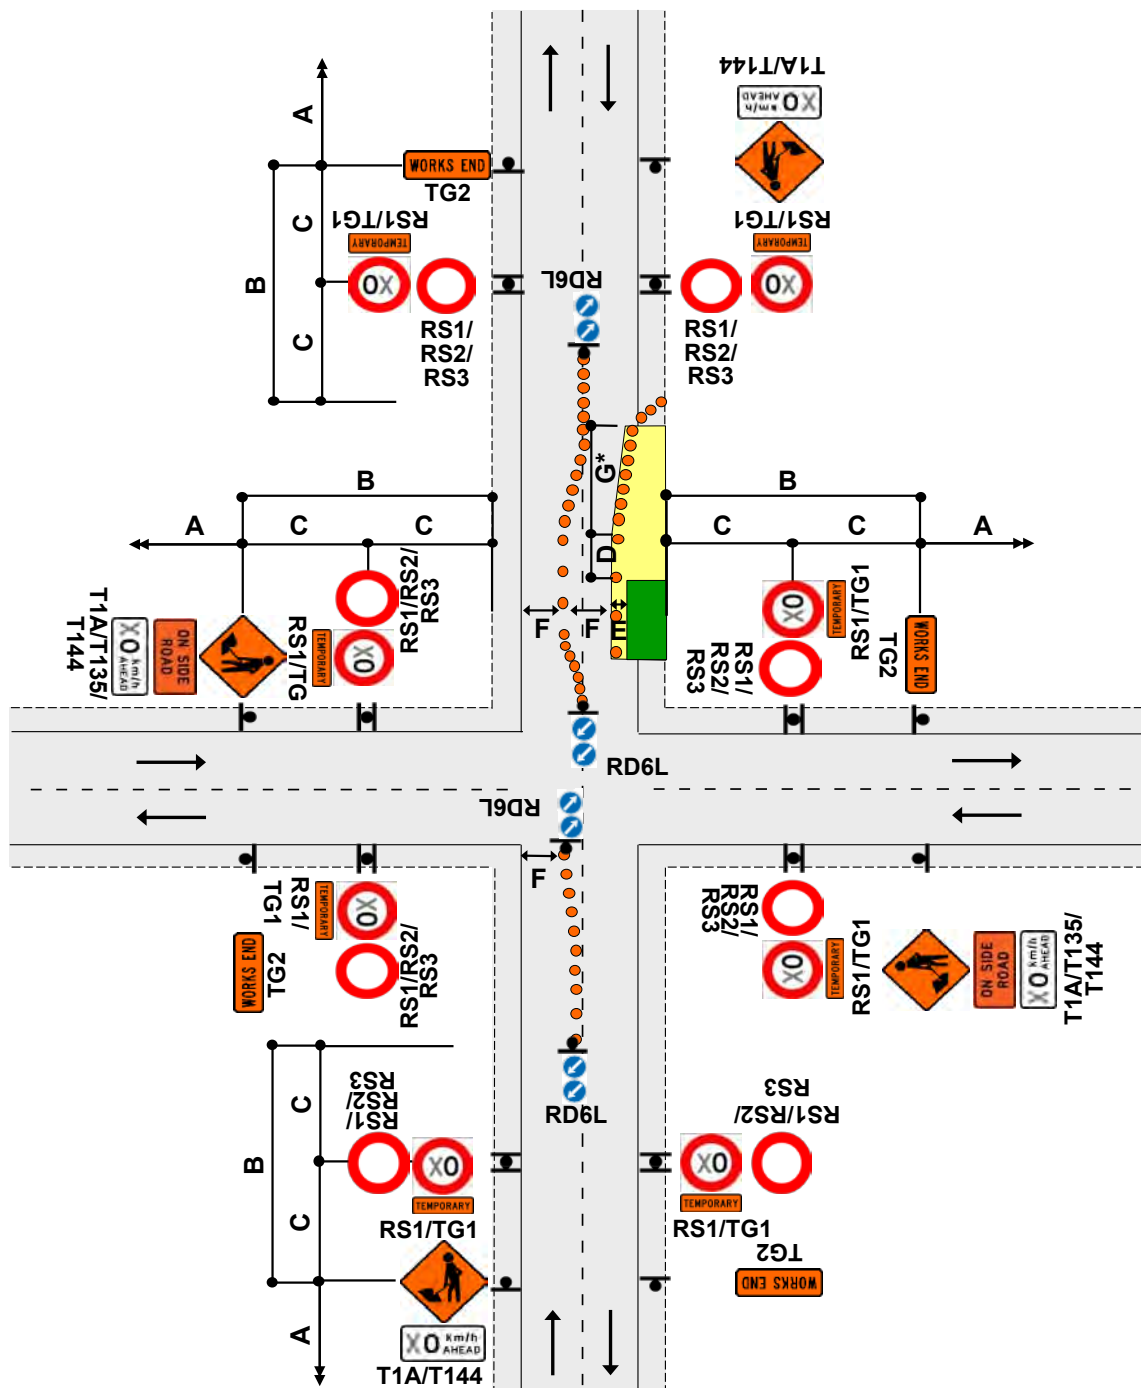

Notes

1. This diagram may be used at a T intersection by removing any one of the roads
2. *Calculation of taper length for lateral shift of less than 3.5m is:

 $W \times G$

3.5

W = Width of lane G = Taper length in metres from the level 1 layout distance table

3. Install shifting taper to move road users into the new alignment
4. Use TSLs if required by TSL decision matrix
5. The T144 X0km/h AHEAD sign is optional

matrix

CAR: R1066208

Jason Wildman

STMS Number 307 43


Hutt City Council

8 CoPTTM

John Doe

1. $\frac{1}{2}$ 2. $\frac{1}{3}$ 3. $\frac{1}{4}$ 4. $\frac{1}{5}$ 5. $\frac{1}{6}$ 6. $\frac{1}{7}$ 7. $\frac{1}{8}$ 8. $\frac{1}{9}$ 9. $\frac{1}{10}$ 10. $\frac{1}{11}$ 11. $\frac{1}{12}$ 12. $\frac{1}{13}$ 13. $\frac{1}{14}$ 14. $\frac{1}{15}$ 15. $\frac{1}{16}$ 16. $\frac{1}{17}$ 17. $\frac{1}{18}$ 18. $\frac{1}{19}$ 19. $\frac{1}{20}$ 20. $\frac{1}{21}$ 21. $\frac{1}{22}$ 22. $\frac{1}{23}$ 23. $\frac{1}{24}$ 24. $\frac{1}{25}$ 25. $\frac{1}{26}$ 26. $\frac{1}{27}$ 27. $\frac{1}{28}$ 28. $\frac{1}{29}$ 29. $\frac{1}{30}$ 30. $\frac{1}{31}$ 31. $\frac{1}{32}$ 32. $\frac{1}{33}$ 33. $\frac{1}{34}$ 34. $\frac{1}{35}$ 35. $\frac{1}{36}$ 36. $\frac{1}{37}$ 37. $\frac{1}{38}$ 38. $\frac{1}{39}$ 39. $\frac{1}{40}$ 40. $\frac{1}{41}$ 41. $\frac{1}{42}$ 42. $\frac{1}{43}$ 43. $\frac{1}{44}$ 44. $\frac{1}{45}$ 45. $\frac{1}{46}$ 46. $\frac{1}{47}$ 47. $\frac{1}{48}$ 48. $\frac{1}{49}$ 49. $\frac{1}{50}$ 50. $\frac{1}{51}$ 51. $\frac{1}{52}$ 52. $\frac{1}{53}$ 53. $\frac{1}{54}$ 54. $\frac{1}{55}$ 55. $\frac{1}{56}$ 56. $\frac{1}{57}$ 57. $\frac{1}{58}$ 58. $\frac{1}{59}$ 59. $\frac{1}{60}$ 60. $\frac{1}{61}$ 61. $\frac{1}{62}$ 62. $\frac{1}{63}$ 63. $\frac{1}{64}$ 64. $\frac{1}{65}$ 65. $\frac{1}{66}$ 66. $\frac{1}{67}$ 67. $\frac{1}{68}$ 68. $\frac{1}{69}$ 69. $\frac{1}{70}$ 70. $\frac{1}{71}$ 71. $\frac{1}{72}$ 72. $\frac{1}{73}$ 73. $\frac{1}{74}$ 74. $\frac{1}{75}$ 75. $\frac{1}{76}$ 76. $\frac{1}{77}$ 77. $\frac{1}{78}$ 78. $\frac{1}{79}$ 79. $\frac{1}{80}$ 80. $\frac{1}{81}$ 81. $\frac{1}{82}$ 82. $\frac{1}{83}$ 83. $\frac{1}{84}$ 84. $\frac{1}{85}$ 85. $\frac{1}{86}$ 86. $\frac{1}{87}$ 87. $\frac{1}{88}$ 88. $\frac{1}{89}$ 89. $\frac{1}{90}$ 90. $\frac{1}{91}$ 91. $\frac{1}{92}$ 92. $\frac{1}{93}$ 93. $\frac{1}{94}$ 94. $\frac{1}{95}$ 95. $\frac{1}{96}$ 96. $\frac{1}{97}$ 97. $\frac{1}{98}$ 98. $\frac{1}{99}$ 99. $\frac{1}{100}$ 100. $\frac{1}{101}$ 101. $\frac{1}{102}$ 102. $\frac{1}{103}$ 103. $\frac{1}{104}$ 104. $\frac{1}{105}$ 105. $\frac{1}{106}$ 106. $\frac{1}{107}$ 107. $\frac{1}{108}$ 108. $\frac{1}{109}$ 109. $\frac{1}{110}$ 110. $\frac{1}{111}$ 111. $\frac{1}{112}$ 112. $\frac{1}{113}$ 113. $\frac{1}{114}$ 114. $\frac{1}{115}$ 115. $\frac{1}{116}$ 116. $\frac{1}{117}$ 117. $\frac{1}{118}$ 118. $\frac{1}{119}$ 119. $\frac{1}{120}$ 120. $\frac{1}{121}$ 121. $\frac{1}{122}$ 122. $\frac{1}{123}$ 123. $\frac{1}{124}$ 124. $\frac{1}{125}$ 125. $\frac{1}{126}$ 126. $\frac{1}{127}$ 127. $\frac{1}{128}$ 128. $\frac{1}{129}$ 129. $\frac{1}{130}$ 130. $\frac{1}{131}$ 131. $\frac{1}{132}$ 132. $\frac{1}{133}$ 133. $\frac{1}{134}$ 134. $\frac{1}{135}$ 135. $\frac{1}{136}$ 136. $\frac{1}{137}$ 137. $\frac{1}{138}$ 138. $\frac{1}{139}$ 139. $\frac{1}{140}$ 140. $\frac{1}{141}$ 141. $\frac{1}{142}$ 142. $\frac{1}{143}$ 143. $\frac{1}{144}$ 144. $\frac{1}{145}$ 145. $\frac{1}{146}$ 146. $\frac{1}{147}$ 147. $\frac{1}{148}$ 148. $\frac{1}{149}$ 149. $\frac{1}{150}$ 150. $\frac{1}{151}$ 151. $\frac{1}{152}$ 152. $\frac{1}{153}$ 153. $\frac{1}{154}$ 154. $\frac{1}{155}$ 155. $\frac{1}{156}$ 156. $\frac{1}{157}$ 157. $\frac{1}{158}$ 158. $\frac{1}{159}$ 159. $\frac{1}{160}$ 160. $\frac{1}{161}$ 161. $\frac{1}{162}$ 162. $\frac{1}{163}$ 163. $\frac{1}{164}$ 164. $\frac{1}{165}$ 165. $\frac{1}{166}$ 166. $\frac{1}{167}$ 167. $\frac{1}{168}$ 168. $\frac{1}{169}$ 169. $\frac{1}{170}$ 170. $\frac{1}{171}$ 171. $\frac{1}{172}$ 172. $\frac{1}{173}$ 173. $\frac{1}{174}$ 174. $\frac{1}{175}$ 175. $\frac{1}{176}$ 176. $\frac{1}{177}$ 177. $\frac{1}{178}$ 178. $\frac{1}{179}$ 179. $\frac{1}{180}$ 180. $\frac{1}{181}$ 181. $\frac{1}{182}$ 182. $\frac{1}{183}$ 183. $\frac{1}{184}$ 184. $\frac{1}{185}$ 185. $\frac{1}{186}$ 186. $\frac{1}{187}$ 187. $\frac{1}{188}$ 188. $\frac{1}{189}$ 189. $\frac{1}{190}$ 190. $\frac{1}{191}$ 191. $\frac{1}{192}$ 192. $\frac{1}{193}$ 193. $\frac{1}{194}$ 194. $\frac{1}{195}$ 195. $\frac{1}{196}$ 196. $\frac{1}{197}$ 197. $\frac{1}{198}$ 198. $\frac{1}{199}$ 199. $\frac{1}{200}$ 200. $\frac{1}{201}$ 201. $\frac{1}{202}$ 202. $\frac{1}{203}$ 203. $\frac{1}{204}$ 204. $\frac{1}{205}$ 205. $\frac{1}{206}$ 206. $\frac{1}{207}$ 207. $\frac{1}{208}$ 208. $\frac{1}{209}$ 209. $\frac{1}{210}$ 210. $\frac{1}{211}$ 211. $\frac{1}{212}$ 212. $\frac{1}{213}$ 213. $\frac{1}{214}$ 214. $\frac{1}{215}$ 215. $\frac{1}{216}$ 216. $\frac{1}{217}$ 217. $\frac{1}{218}$ 218. $\frac{1}{219}$ 219. $\frac{1}{220}$ 220. $\frac{1}{221}$ 221. $\frac{1}{222}$ 222. $\frac{1}{223}$ 223. $\frac{1}{224}$ 224. $\frac{1}{225}$ 225. $\frac{1}{226}$ 226. $\frac{1}{227}$ 227. $\frac{1}{228}$ 228. $\frac{1}{229}$ 229. $\frac{1}{230}$ 230. $\frac{1}{231}$ 231. $\frac{1}{232}$ 232. $\frac{1}{233}$ 233. $\frac{1}{234}$ 234. $\frac{1}{235}$ 235. $\frac{1}{236}$ 236. $\frac{1}{237}$ 237. $\frac{1}{238}$ 238. $\frac{1}{239}$ 239. $\frac{1}{240}$ 240.

14 November 20.

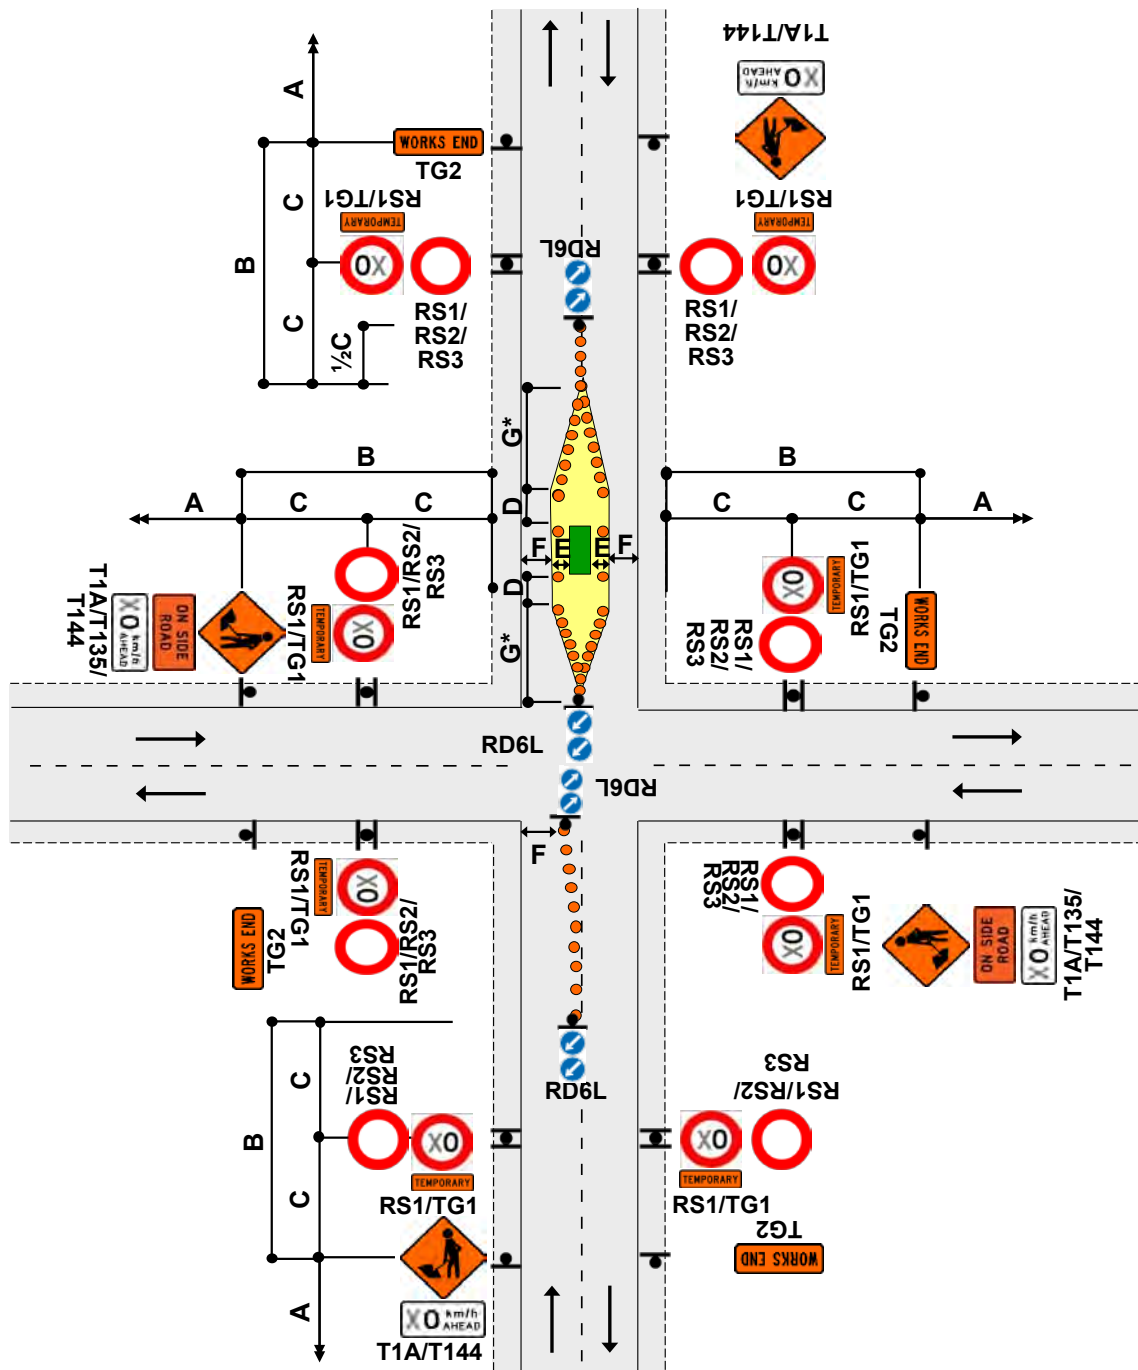

Notes

1. This diagram may be used at a T intersection by removing any one of the roads
2. *Calculation of taper length for lateral shift of less than 3.5m is:

$$\frac{W \times G}{3.5}$$

3.5

W = Width of lane G = Taper length in metres from the level 1 layout distance table

3. Install shifting taper to move road users into the new alignment
4. Use TSLs if required by TSL decision matrix
5. The T144 X0km/h AHEAD sign is optional

APPROVED

CAR R1066208
Jason Wildman
STMS Number 307 43
Hutt City Council
