Works Access Permit

Registration Number: **E1068566**

Utility Reference: 2025 Global Car Non-Excavation



1. Details of Proposed Work

Activity: Asset Inspections/Maintenance, Cabinets/Pedestals Access, Chambers Access, Drainage Works, Manhole Maintenance, Meter Maintenance, Survey, Other (Specify Detail)

Address: 838 Fergusson Drive, Upper Hutt Central, Upper Hutt, 5218

Location in road: Carriageway, Footpath, Berm, Nature Strip WAP valid period: 01 January 2025 to 31 December 2025

2. The Parties

Upper Hutt City Council being a body corporate in accordance with the Local Government Act 2002 ('the Corridor Manager;')

Wellington Water Alliance being an approved Utility Operator in accordance with submitting a request for access in accordance with that act;

Wellington Water Alliance being the agent of the Utility Operator submitting this request on behalf of the Utility Operator and in accordance with the Utility Operator's statutory rights ('the Applicant').

3. Attachments

Attachment 1 being the Schedule of Reasonable Conditions.

Attachment 2 being plan TMP showing the agreed service location.

4. Background

- (a) The Utility Operator wishes to carry out the works stated on CAR Number E1068566 and thereafter maintain the utility services established in the corridor;
- (b) The Corridor Manager is required to provide a written consent in accordance with its governing legislation and to provide a schedule of reasonable conditions, if required, by the utility legislation under which the request for access has been made; and
- (c) In accordance with the Code: Utilities' Access to the Transport Corridors and on behalf of the Corridor Manager, I give my written consent for access to the corridor at the agreed location and attach my schedule of reasonable conditions:
- (d) In the case of State highways this Works Access Permit serves as the approvals required under sections 51 and 78 of the Government Roading Powers Act.

Signed	Kello.		Date	25/11/2024					
Phil Gollin	gs acting pursua	ant to delegated au	thority.						
FOR Corri	FOR Corridor Manager APPROVAL USE ONLY								
Time Spe	nt Processing:								
	Approved Contractor	Route Plan Submitted	V	TMP Submitted	Stockpiling Arrangements				



CONDITIONS

General Conditions

- 1. The Utility Operator must:
 - (a) carry out all Work in Transport Corridors in accordance with the Code and KiwiRail's Specifications for Working in Railway Corridors;
 - (b) undertake all Works in compliance with the Acts of Parliament and mandated codes of practice that relate to their industry and the type of Work described within the plans and methodology submitted;
 - (c) install assets more or less in the location shown on the attached plans, and agree the exact location and position with the Road Corridor Manager before Work commences;
 - (d) locate any Utility Structures in the Road Corridor in the agreed position shown on the drawings and clear of the Carriageway, Road Corridor furniture and kerbs, drains, manholes, etc. Utility Structures agreed to be within the trafficable part of the Road are to be flush with the surface and designed to withstand full heavy Traffic loading (NZTA's HN-HO-72 Traffic Loading);
 - (e) provide a full description of the construction methodology, reinstatement, resurfacing and compaction and agree this with the Road Corridor Manager prior to Work commencing;
 - (f) make the Works available at all times for inspection by any person representing the Road Corridor Manager;
 - (g) if requested, pay the reasonable costs of the Road Corridor Manager in connection with the processing of this notice and for the monitoring and auditing of the Works; (See NZ Transport Agency Cost Structure under Clause 23)
 - (h) keep a full copy of the Works Access Permit/ Permit to Enter and Reasonable Conditions on the Work Site at all times during the Works;
 - (i) undertake remedial action on non-conforming Work within the timeframe set by the Road Corridor Manager, where reasonable and practicable;
 - (j) gain all the necessary consents, approvals and permits from the relevant statutory and regulatory authorities at its own cost;
 - (k) keep plans of the installed Work and make them available to the Railway Corridor Manager (in all cases) and Road Corridor Manager (on request);
 - (I) compensate the Road Corridor Manager for any damage or costs incurred to the Road Corridor due to the Work or for costs resulting from the removal of abandoned installations, Utility Structures, components and equipment that belong to the Utility Operator;
 - (m) repair all Road Corridor assets damaged as a result of the Works, should the Road Corridor Manager determine these are necessary prior to the end of the Warranty period;
 - (n) restore to their original condition any surface or Utility Structure that was damaged or removed as a result of the Works;
 - (o) control the surface water channels so as to cause minimal interference to existing flows;
 - (p) fully restore the surface water channels at the completion of the Works;
 - (q) notify the Road Corridor Manager of any maintenance Work it proposes to undertake within the two-year Warranty period;

- (r) have in place an approved TMP for Roads and Motorways at least two days prior to Work commencing on the Work Site;
- (s) provide the Road Corridor Manager with two Working Days' notice before commencement of Work on the Work Site;
- (t) ensure that the Work is carried out under the control of a warranted supervisor as required by the Code of Practice for Temporary Traffic Management and ensure that there are sufficient people on site specifically to control the flow of Traffic through the site in accordance with the TMP;
- (u) comply with instructions from an officer of the NZ Police Traffic Safety Branch or a duly authorised agent of the Road Corridor Manager in respect of Traffic management and safety;
- (v) complete Works in the Road Corridor in one continuous operation (suspension of Works over five continuous days requires the prior written permission of the Road Corridor Manager);
- (w) protect and maintain all Road Corridor signs, markers, signals, barriers and associated marking and replace them to the appropriate industry standard where they have been damaged by the Works;
- (x) complete and submit a Works Completion Notice form when the Works are complete; and
- (y) stop Work as necessary to meet the requirements of section 42 of the Heritage New Zealand Pouhere Taonga Act 2014.
- 2. Work must not take place on or near a State highway during and one day either side of a public holiday or public holiday weekend.
- 3. Where otherwise required due to Traffic volumes or specific residential or Central Business District requirements, the hours of Work must be as specified in the Local Conditions and Special Conditions.
- 4. The Warranty period starts from the date the Road Corridor Manager has given signed acceptance that the Work is complete or otherwise as provided in Section 4.7.1.7 of the Code.
- 5. Unless the Works stated in the WAP have started on the Work Site, the agreement relating to the Works will only remain valid for six months from the date of approval on the Works Access Permit.
- 6. The Road Corridor Manager must manage all applications relating to Road Corridor access in accordance with the timeframes and processes in the Code.
- 7. The Corridor Manager may:
 - (a) assess the suitability of any action proposed by the Utility Operator during the Warranty period and impose Reasonable Conditions that will maintain the integrity of the Road assets;
 - (b) arrange for remedial Work to be done and recover the costs incurred from the Utility Operator, if the Utility Operator fails to take action within the agreed timeframe; and
 - (c) instruct the Utility Operator to stop Work and leave the Work Site (having made the site safe) if the Works are not complying with the relevant Reasonable Conditions including any plans, relevant conditions or specifications contained in the Code, or permission requirements.

- 8. In granting this WAP, no vested right is created.
- 9. This WAP is not transferable without the written permission of the Road Corridor Manager.

Local Conditions

- 10. These conditions supplement the requirements of THE NATIONAL CODE OF PRACTICE FOR UTILITY OPERATORS ACCESS TO TRANSPORT CORRIDORS and THE HUTT VALLEY LOCAL CONDITIONS.
- 11. Cement stabilised basecourse to be used in trench.
- 12. As work is in CBD boundary, the TMP must be sent to Roading Inspector for approval before any physical work can begin.
- 13. Active traffic control is required at all times that work is taking place.
- 14. All temporary traffic signs and cones must be up before any physical work can begin.
- 15. When site is unattended over night all reasonable precautions must be made to ensure there is no hinderance to public vehicular, pedestrian, or cycle traffic.
- 16. Compliant compaction results must be loaded to CAR with Work Completion Notice.
- 17. Photos of trench reinstatement must be loaded to CAR with Work Completion Notice.

Special Conditions

- 18. Finished height of pad must be level with surrounding surfaces.
- 19. No debris from excavation to be left on site.
- 20. No stockpiling of material within road corridor unless authorised by Corridor Manager.
- 21. Cement stabilised basecourse to be used in trench directly in front of vehicle crossing.
- Full width of footpath to be reinstated.
- 23. Full reinstatement of vehicle crossing up to property boundary is required..
- Letter drop informing all residents within the work site, including 20 meters before and after site and directly opposite site, of the nature of the work to be carried out. Contact details for complaints and any other relevant information contractor deems necessary.

 Letter drop to be done minimum 24 hours prior the commencement of work.

25. Brown out Period 2024

No work shall be carried out within the Central Business District (CBD) and retail zones between Monday 2 December 2024 and Friday 3 January 2025.

CBD zone map - https://www.upperhutt.govt.nz/Services/Roads-and-parking/Approval-to-work-on-the-road-footpath-or-berm#section-2

No work on the Corridor network outside the CBD and retail zones between Monday 22 December 2024 and Friday 3 January 2025.

Letter drop informing all residents within the work site, including 20 meters before and after site and directly opposite site, of the nature of the work to be carried out. Contact details for complaints and any other relevant information contractor deems necessary.

Letter drop to be done minimum 5 working days prior the commencement of work.

27. Access to private properties within the site must be maintained during the works.

CAR UHCC Full Scope of Works Utility

Utility

Company	Wellington Water
Contract Manager	Bob Wilson
Phone	027 3355 334
Email	Bob.Wilson@wellingtonwater.co.nz

Contractor

Company	Wellington Water alliance
Contract Manager	Bob Wilson
Phone	027 3355 334
Email	Bob.Wilson@wellingtonwater.co.nz

Type of Work					Minor Non-	х
(Tick)					Excavation	
Location Road (Tick)	Carriageway	х	Footpath	х	Berm	х

Work Location

Physical Address	Various Locations / Streets within Upper Hutt City Region

Work Programme

Start Date	01/01/2025	Completion Date	31/12/2025
Duration of Work	24/7	Day / Night	365

Hours of work

Start Time	Finish Time	

Description of Activity

Non excavation works not needing site specific:

• All work carried out may involve having 1 to 2man onsite including sub-contractors.

ALL ROAD CLOSURES MUST HAVE RCA / TMC APPROVAL

All Night Works must have Noise Control Approval before the work can start. 6:00pm – 7:30am Mon-Sat, All time Sunday & Public Holidays

Note: All project works, or other work not covered under the Generic Tmp / Tmd will need site specific.

Weekend or afterhour works:

All weekend (Sat-Sun) or afterhours (6pm – 7am) work requires a child CAR to be raised in advance.

Confirmation is required from RCA to see if Generic covers main arterial roads or suburban shopping areas, Site Specific TMP maybe required.

Only approved contractors listed on Tmp are covered under Global Car.
ALL CONTRACTORS ARE TO NOTIFY THE RCA PRIOR TO CARRY OUT THEIR WORK ACTIVITY.

This work will cover inspections / maintenance / locates that can be completed on the same day.

- Locating council assets.
- Investigate any leaks to determine what may be required to carry out any repairs.
- Poor water quality needing to flush hydrants.
- Operation of hydrants and valves on the same day.
- Hydrant painting carried out annually.
- Flow meter testing, need to access chamber to carry out test.
- Leak detection surveys carried out by approved contractors AD Riley and Detection Services to locate leaks.
- Utility asset mark outs.
- 3 Water asset mark outs.
- Meter reading check if any issues with meters and carry out final readings.
- CCTV inspections.
- Checking condition of Wastewater / Stormwater assets.
- Smoke / Dye testing on Wastewater / Stormwater assets to identify inflow sources, defects and cross connections, this work can take between 2 4 hours and will cover set locations in each suburb.
- Installation and maintenance of monitoring equipment into manholes to measure flow and overflows from the Wastewater network.
- Lifting manhole covers to check assets running clear.
- Clearing Wastewater / Stormwater blockages.
- Regular hydrant flushing takes approx. 15 mins until run clear cleaning the lines.
- Regular fortnightly / monthly flushing for the 3 waters that can be completed within 3 to 6 hours.
- Culvert / intake clearing removing debris / trash that may impede the flow of water.
- Annual pit cleaning to prevent blockages and potential overflows, duration will take no longer than 1.5 hours between 1am to 5.30am.

No work will be carried out on main arterial roads between 6am to 9am.

Crews and Sub contractors must adhere to the following:

- Ensure proper traffic and pedestrian management is in place.
- Set up correct Tmd to suit the work site.
- Safety induction is carried out as per RCP process.
- Ensure safety is always adhere to.
- Ensure all efforts are made to minimise disruption to residents, business, and pedestrians.
- Make sure relevant documents are onsite.
- Provide photos showing a wide street view of location.
- Photos of Work carried out.
- Clear notes of what work was carried out.
- Site is packed up and left clean and tidy.
- No car will need to be logged in Submitica when carrying out inspection work on same day.

Work Vehicles onsite at various stages of work but not limited to:

Standard work crew:

1 to 2 service vehicles equipped with beacons onsite along with any small plant and equipment to carry out inspections. Crews to set up own Tmd.

Service crews are equipped to set up the following Tmd's only.

Traffic management will be required if you do not carry correct signage.

CC1	F2.1
CC2	F2.2
CC3	F2.5
CC4	F2.6
CC5	F2.7
CC7	J2.16A
CC8	F4.10
CC9	ATMS07
CC12	

Sub-contractors are to follow the Tmd criteria above, or if you do not have correct signage to set up own Tmd. Any Tmd not listed above will require external traffic management.

Extended crew when needed:

- Traffic management vehicles if unable to set up own traffic.
- Hydro Vac Truck / Digger / Jet Flusher maybe utilised.

Site Specific TMP required depending on the work activities and impact. Works include:

- Entry to access Three Water Assets located at a major intersection, or within a live lane that will impact traffic flow.
- All works within State Highways.
- All works within KiwiRail property, prior approval is required.
- All works that impact bus stops, including relocation, will need a site TMP.
- All works that impact a school during school hours.
- Road closures.

This also includes works that may have an impact on traffic and project work taking more than 1 day.

- ANY STATE HIGHWAY WORKS WILL BE AT THE DISCRETION OF WAKA KOTAHI TMC.
- All Works approved by Waka Kotahi TMC Must then be notified to the traffic OPERATIONS CENTRE (TOC) PRIOR TO COMMENCEMENT AND POST WORK.
- WORKS ARE TO BE PLACED ON THE WEEKLY ROAD WORKS REPORT.

ALL COMPLETED WORKS MUST COMPLY TO WAP CONDITIONS AND ARE TO BE REINSTATED ACCORDING TO WTA STANDARDS.

Quantities of proposed Work (use meters, items, hours and minutes to indicate);

Length of trenching	Number of Cabinets/pedestals effected	
Length of Horizontal/Vertical Drilling	Number of Structures effected (fully explain in	
	description of work)	

Number of holes	Number of assets removed	
Number of Chamber/s effected	Duration of Road / Lane Closure (circle)	
	Hours / Days	
Number of Poles/Posts/Piles effected	Duration of Footpath diversion (circle)	
	Hours / Days	
Number of Car parks/bus stop/taxi stands	Duration of property access restricted (circle)	
affected for more than two hours	Hours / Days	

Health and Safety Policy Wellington Water



Our Purpose

Creating excellence in regional water services for healthy communities

Our Vision

Our people, suppliers and affected parties go home healthy and safe

- · Health and safety is our top priority
- We look after ourselves; everyone takes personal responsibility for their own health and safety
- We look out for each other, suppliers and the public; we make sure everyone is safe
- Wellington Water takes a methodical approach to health and safety; we continuously review our systems to ensure they are up-to-date and ensure that health and safety is foremost in infrastructure planning and design
- We're committed to health and safety at all times; nobody walks past an unsafe activity or work site we make it

Our Commitments

Leadership

- We make sure our people work in a safe environment
- We make sure our work sites are safe for suppliers, neighbours and the general public
- We empower our people to manage health and safety in all situations and to stop unsafe acts as they happen; we make sure there's a safe working environment before work continues
- We proactively identify and manage hazards and ensure safe behaviour
- We support the safe and early return to work of any of our people who are injured or sick, and support and follow up on anyone who is injured on a Wellington Water site
- We recognise staff and suppliers who practice excellence in health and safety

Systems

- We make sure our people have the training, skills and resources to work safely
- We ensure infrastructure managed by Wellington Water is designed, constructed, operated and maintained safely, and will remain safe for our people, suppliers and the community
- We accurately record, investigate and report incidents and learn from them
- We monitor our health and safety performance and that of our suppliers as a basis for continuous improvement and identifying new and safer ways of working

Working with others

- Our suppliers are required to commit to our vision of our people and suppliers going home healthy and safe
- We make sure all suppliers working on behalf of Wellington Water have high quality health and safety systems in
- · We comply with and exceed all relevant legislation, regulations, codes of practice and industry standards
- We interpret health and safety broadly and work with all stakeholders to achieve our health and safety vision



People at the heart of everything we do

Living safely is how we go about every aspect of our lives; all day, every day. It is more than work, it is about integrating our work, home and interests, our desire to get the best out of life, and to be the best we can. It is recognising our strengths and weaknesses, and making positive choices that benefit our wellbeing and way of life, including those of others in the communities in which we live and work.

We will:

- · Demonstrate our commitment through active and visible leadership
- Abide by a simple safety management system that encourages health and safety ownership by each and every individual
- · Incorporate health and safety into the way we design, plan and do our work
- Work collaboratively with our subcontractors to meet the required health and safety standards
- . Enhance our health and safety skills and behaviours through training and development
- · Foster a culture of reporting, learning and sharing
- · Be empowered to maintain a safe and healthy workplace
- · Promote a positive health and wellbeing mindset
- · Meet or exceed relevant standards and legal requirements
- · Set measurable objectives and targets to ensure continual improvement

C W Bruyn Managing Director





ROAD SPACE BOOKING

Address:					
Contractor:					
Dates & Times (attended):	From:			То:	
Dates & Times (unattended):	From:			То:	
Generic TMP used:					
Diagram (s) used:					
CAR#					
Work A	ctivity an	nd Razson	s TTM to re	amain ir	n nlace:
WOIRA	ctivity an	iu iteasoii	5 1 1141 (0 16	ziiiaiii ii	i piace.
Contractor Name:					
Contractors Signature:					
TMC Approval:					

Please attach photos of site active site set up (these photos are to include both ends of the site (inclusive of any side roads), pedestrian/cycle management and the working area.





TRAFFIC MANAGEMENT PLAN (TMP) - FULL FORM

Use this form for complex activities. Refer to the NZ Transport Agency's Traffic control devices manual, part 8 Code of practice for temporary traffic management (CoPTTM), section E, appendix A for a guide on how to complete each field.

Organisations /TMP			Principal (Client): Wellington Water				
reference	Contractor (TTM): As per attached list			RCA: Upper Hutt City Council			
	Road names and Suburb		House no./RPs		Road	0	
Location details and road			From and to		level	Speed Limit	
characteristics	Various within the Upper Hutt City Region			Various		30/40/50/60 /70/80km/h	
	AADT Various		Peak flows				
			Start			End	
Traffic details (main route)			AM	5:30am		9:00am	
			PM 4:00pm			7:00pm	

Description of work activity

1Non excavation works not needing site specific:

All work carried out may involve having 1 to 2man onsite including sub-contractors.

ALL ROAD CLOSURES MUST HAVE RCA / TMC APPROVAL

All Night Works must have Noise Control Approval before the work can start. 6:00pm – 7:30am Mon-Sat, All time Sunday & Public Holidays

Note: All project works, or other work not covered under the Generic Tmp / Tmd will need site specific.

Weekend or afterhour works:

All weekend (Sat-Sun) or afterhours (6pm – 7am) work requires a child CAR to be raised in advance.

Confirmation is required from RCA to see if Generic covers main arterial roads or suburban shopping areas, Site Specific TMP maybe required.

Only approved contractors listed on Tmp are covered under Global Car.
ALL CONTRACTORS ARE TO NOTIFY THE RCA PRIOR TO CARRY OUT THEIR WORK ACTIVITY.

This work will cover inspections / maintenance / locates that can be completed on the same day.

- Locating council assets.
- Investigate any leaks to determine what may be required to carry out any repairs.
- Poor water quality needing to flush hydrants.
- Operation of hydrants and valves on the same day.
- Hydrant painting carried out annually.
- Flow meter testing, need to access chamber to carry out test.
- Leak detection surveys carried out by approved contractors AD Riley and Detection Services to locate leaks.
- Utility asset mark outs.

CAR E 1008500





- 3 Water asset mark outs.
- Meter reading check if any issues with meters and carry out final readings.
- CCTV inspections.
- Checking condition of Wastewater / Stormwater assets.
- Smoke / Dye testing on Wastewater / Stormwater assets to identify inflow sources, defects and cross connections, this work can take between 2 – 4 hours and will cover set locations in each suburb.
- Installation and maintenance of monitoring equipment into manholes to measure flow and overflows from the Wastewater network.
- Lifting manhole covers to check assets running clear.
- Clearing Wastewater / Stormwater blockages.
- Regular hydrant flushing takes approx. 15 mins until run clear cleaning the lines.
- Regular fortnightly / monthly flushing for the 3 waters that can be completed within 3 to 6 hours.
- Culvert / intake clearing removing debris / trash that may impede the flow of water.
- Annual pit cleaning to prevent blockages and potential overflows, duration will take no longer than
 1.5 hours between 1am to 5.30am.

No work will be carried out on main arterial roads between 6am to 9am.

Crews and Sub contractors must adhere to the following:

- Ensure proper traffic and pedestrian management is in place.
- Set up correct Tmd to suit the work site.
- Safety induction is carried out as per RCP process.
- Ensure safety is always adhere to.
- Ensure all efforts are made to minimise disruption to residents, business, and pedestrians.
- Make sure relevant documents are onsite.
- Provide photos showing a wide street view of location.
- Photos of Work carried out.
- Clear notes of what work was carried out.
- Site is packed up and left clean and tidy.

Vehicles onsite at various stages of work but not limited to:

Standard work crew:

1 to 2 service vehicles equipped with beacons onsite along with any small plant and equipment to carry out inspections. Crews to set up own TMD.

Service crews are equipped to set up the following Tmd's only.

Traffic management will be required if you do not carry correct signage.

CC1	F2.1
CC2	F2.2
CC3	F2.5
CC4	F2.6
CC5	F2.7
CC7	J2.16A
CC8	F4.10
CC9	ATMS07
CC12	

Sub-contractors are to follow the TMD criteria above or f you do not have correct signage to set up own TMD.

Any TMD not listed above will require external traffic management.

Phil Gollings





Extended crew when needed:

- Traffic management vehicles if unable to set up own traffic.
- Hydro Vac Truck / Digger / Jet Flusher maybe utilised.

WHEN ARE SITE SPECIFIC TMP'S NEEDED:

Retrospective Site Specific TMP required depending on the work activities and impact. Works include:

- Entry to access Three Water Assets located at a major intersection, or within a live lane that will impact traffic flow.
- Burst water main / water leaks in the carriageway / intersections that will impact traffic.
- Hydrant / valve replacements in the carriageway that will impact traffic.
- Water / wastewater lateral replacements that involve trenching across the carriageway.
- All works within State Highways.
- All works within KiwiRail property, prior approval is required.
- All works that impact bus stops, including relocation, will need a site TMP.
- All works that impact a school during school hours.
- Road closures.
- This also includes works that may have an impact on traffic and project work taking more than 1 day.
- ANY STATE HIGHWAY WORKS WILL BE AT THE DISCRETION OF WAKA KOTAHI TMC.
- All WORKS APPROVED BY WAKA KOTAHI.
- TMC MUST THEN BE NOTIFIED TO THE TRAFFIC OPERATIONS CENTRE (TOC) PRIOR TO COMMENCEMENT AND POST WORK.
- WORKS ARE TO BE PLACED ON THE WEEKLY ROAD WORKS REPORT

ALL COMPLETED WORKS MUST COMPLY TO WAP CONDITIONS AND ARE TO BE REINSTATED ACCORDING TO NZTA STANDARDS

APPROVED
CAR E1068566
Phil Gollings





Planned work program	mme						
Start date	01/01/2025	Time	See Below	End date	31/12/2025	Time	See Below
Consider significant			F	Residential Ro	pads		
tages, for example:	lı lı	nstallati	ion: 7:00am -	- 7:30am or w	henever site is installed.		
 road closures 		Site Active: 7:30am – 17:30pm					
detours		Site Removal: 17:30pm – 18:00pm					
 no activity periods. 	NIG	HTWO	RKS ARE NO	T PERMITTE	D IN RESIDENTIAL AREAS	S	
				Main Road	1		
		Installa	tion: 9:00am	-9:30am or w	henever site is installed		
			Site Ac	tive: 9:30am	– 15:30pm		
			Site Rem	oval: 15:30pi	m – 16:00pm		
	Ins	stallatio	n: 19:00pm -	- 19:30pm or	whenever site is installed	'	
			Site Ac	tive: 19:30pn	n – 5:00am		
			Site Re	moval: 5:00aı	n – 5:30am		
	1,0						
	Works near schools No work to be completed between school drop off & pick up times: Between 8.30am – 9.30am & 2.30pm – 3.30pm						
	TI	nis TMP	is to cover 1	day attende	d non - excavation works.		
	Road Space Booking I Location/Addres		nclude:				
	Dates/Times ofTMP & Diagram		LEX DEST	GEN	KENT SER	VII	
	Reasons for work	Reasons for works/TTM remaining in place, longer than 1 day					
	Photos of the ac side roads), ped				include both ends of the sit working area.	e (inclusiv	e of any
	A site specific TMP is requ	uired for	/when:		(Co		
	A road	d closure			l road closure)		
	Bus la Roads	ne only s of Sign	closed (Petor	ne Esplanade) r attached list,			
	Plans F2.16 and F2.4 mus	st be ap	proved by TM	C.			
	Any changes to the appro-	ved TMI	must be doo	cumented on the	ne Onsite Record.		

APPROVED

CAR E1068566 Phil Gollings

Section P, appendix A. Traffic management plans
Page 4





Parking Restrictions:

Parking restrictions will be installed where required 12-24hrs prior to works commencing. Parking restriction signage is to show actual work times and dates.

INFORMATION ONLY: – vehicles may require towing.

Upper Hutt City Council to be contacted 04 527 2169

All related towing fees will be directed to the contractor. Towing authority is not approved as part of the TMP process.

Kerb Side Collection:

Kerb side collection occurs Monday to Friday. Refer to the attached kerb side collection schedule. Works to halt when kerb side collection vehicle is working in the area or onsite personnel to assist with the collection.

- A risk assessment is to be applied prior to selecting/installing TMDs.
- Checking-process-for-GTMPs checklist form (attached) is to be completed prior to using the GTMP.

APPROVED CAR E1068566

Phil Gollings





Type of road	On shoulder or roadside – no time limit	On live lane – up to 5 minutes	Over 5 minutes	
Low volume (less than 500vpd) category A or B road environment		a practising STMS of any category, and in the interim until the warrants		
Category A	Spotter optional – can be one person activity	Spotter required – minimum two person activity		
	Onsite control must be by either practising TMO or Inspector (and phased out):	oractising STMS of any category, in the interim until the warrants are		
	Road level	Onsite control		
	Level 1 road	TC, TC-Inspector or STMS		
	Level 2 road	L2/3 STMS, STMS-NP, or TC- Inspector	Inspection not	
Category B	Spotter optional – can be one person activity	Spotter required – minimum two person activity	permitted.	
	Onsite control must be by either a a practising TMO or an Inspector are phased out:	Must use a mobile, semi- static, or static closure.		
	Road level	Onsite control	Ciosure.	
	Level 1 road	TC, TC-Inspector or STMS		
	Level 2 road (shoulder, roadside or on the lane with speed 60km/h or less)	L2/3 STMS, STMS-NP or TC- Inspector		
	Level 2 road (on the lane with speed 70km/h or more)	L2/3 STMS or STMS-NP		
Category C	Spotter optional – can be one person activity: Onsite control must be by either a practising STMS (C) or an Inspector (and in the interim until the warrants are phased out, a L2/3 STMS, STMS-NP, or TC-Inspector).	Inspection not permitted. Must use a mobile, semi-static, or static closure.		

WAKA KOTAHI

TTM NOTICE: IMPLEMENTATION OF STAGE 1 OF TRAINING & COMPETENCY MODEL // 93

APPROVED CAR E1068566

Phil Gollings

Section P, appendix A. Traffic management plans
Page 6





General rules (apply to all the above)

Inspectors must move to avoid traffic. They must not expect traffic to move or slow down to avoid them.

There must be CSD to the inspector when on the live lane.

On busy roads where traffic volumes and speed affect access to the live lane, peak periods should be avoided or a higher level of TTM considered.

Crossing a level LV, 1 or 2 road does not constitute being on a live lane but crossing a level 3 road does, unless a pedestrian crossing facility is being used.

Advance warning in the form of an inspection vehicle fitted with one and preferably two amber flashing beacons and a rear-mounted sign indicating the type of activity taking place must be positioned in advance of the inspection site.

A vehicle is not required on a level LV or level 1 road with a permanent speed of less than 65km/h If the Inspector remains on a footpath.

On roads with a permanent speed of less than 65km/h an amber flashing beacon is not required on the vehicle if the inspector or non-invasive works is on an unsealed shoulder (or further away from the carriageway - Including a footpath).

A spotter is not required for inspections and non-invasive works on level LV roads.

Unless otherwise approved by the RCA, all inspections on the live lane of level 1 and level 2 roads require a spotter. The RCA may provide a list of level 1 roads, times and/or activities suitable for inspection by a single inspector (eg where no level LV roads have been declared by the RCA)

Where an unaccompanied inspector is not able to maintain adequate attention (eg due to work tasks or poor visibility), a spotter will be required or another type of traffic management operation used.

Alternative dates if activity delayed

N/A – works will be carried out within the times/dates as listed.

Road aspects affected (delete either Yes or No to show which aspects are affected)					
Pedestrians affected?	Potentially	Potentially Property access affected? Potentially Traffic lanes affected? Potentially			
Cyclists affected?	Potentially	Restricted parking affected?	Potentially	Delays or queuing likely?	Potentially

Proposed traffic management methods

APPROVED CAR E1068566 Phil Gollings

Section E appendix A: Traffic management plans Page 7

Edition 4, April 2020





- STMS to contact Metlink (0800 801 700) for any works including installing a TSL on a bus route or impacting bus stops 30mins prior to installation.
- STMS to contact WTOC (0800 869 286) for any works affecting or close to traffic signals 30 mins prior to installation.

Once on site, the TMP will be implemented as follows:

- Identify public safety and site safety hazards and how they will be addressed and place on the hazard document for 'toolbox' briefing
- STMS to check the TMP is appropriate to the worksite.
- All vehicles are to have correct signage and flashing beacons. They also need to have continuous and appropriate communication with the STMS and each other on an agreed channel at all times
- Work vehicles required on site will be parked within the site or parked legally nearby.
- Mobile Operations or inspection activities may be required to turn on/off water valves.

Installation

(includes parking of plant and materials storage)

Layout Procedure

Installation of the site will be done under a level 1 mobile closure with appropriate work vehicles and crew.

- 1. A site drive through will be conducted first to confirm layout, conditions and environment are all appropriate for works to proceed.
- 2. Vehicle positioning will be as far to the left as practical and the installation vehicle will be stationary at the installation of each sign, with activity occurring only on the non-traffic side of the vehicle.
- 3. Advanced warning signage will be installed first on the left, followed by progressive signage installation in a 'loop' fashion around the site area.
- 4. Once ALL signage for the site has been installed delineation and direction signage will be installed in the following order;
 - a. Longitudinal Delineation (Along the lane)
 - b. Tapers & RD6 signage

Once all delineation is installed and prior to personnel, vehicle, plant and machinery populating the worksite, a drive through check must be performed by the STMS to ensure the site has been set up as per the selected TMDs, this should include the checking of worksite layout distances.

APPROVED
CAR E1068566
Phil Gollings

Section E appendix A Traffic management plans

ection E, appendix A? Tra Page 8





AGENCY	and/or RCA contract reference				
	An STMS or delegated TMO must be onsite at all times.				
	TM-W/STMS to assist pedestrians/cyclists/driveways and any resident/business driveways.				
	For Stop/Stop and Stop/Go setups, cyclists will be sent prior to any vehicles.				
	STMS/TMO will complete 2 hourly site checks and document on the onsite record.				
	Where Mobility Parking are affected alternative to be provided (same side of road, as close as possible), TM personnel to assist and guide users as required				
	Works near Signals:				
	Any affected signal loops must be notified to WTOC during the pre-installation call to allow them to adjust signal management.				
	Works near Pedestrian Crossings:				
Attended (day)	TM-W's to guide pedestrians through/around the closure.				
	Works near a Bus Stop:				
	Bus stop integrated into MTC Stop Point				
	MTC's on stop/go are to stop each bus and assist with loading & unloading of passengers as required.				
	Bus stop signage is to direct pedestrians towards the stop point				
	Bus stop relocated away from site				
	Bus stop signage is be placed to show patrons where the relocation is.				
	TM personnel to assist and guide bus patrons as required				
	Temporary bus stop signage is to be used				
	Parking restrictions are to be in place at the relocated bus stop				
	Works near a School:				
	No work to be completed between school drop off & pick up times:				
	Between 8.30am – 9.30am & 2.30pm – 3.30pm				
	An STMS or delegated TMO must be onsite at all times. TM WOTAG.				
	TM-W/STMS to assist pedestrians/cyclists/driveways and any resident/business driveways. The Charlest and Charlest an				
	For Stop/Stop and Stop/Go setups, cyclists will be sent prior to any vehicles. CTMS/TMO will appreciate 2 hours its about and decrease to the applications and decrease to the applications.				
	STMS/TMO will complete 2 hourly site checks and document on the onsite record. Additional lighting may be required for unplied.				
	 Additional lighting may be required/supplied. Noise will be kept to a minimum where possible. 				
	· · ·				
	 Where Mobility Parking are affected alternative to be provided (same side of road, as close as possible), TM personnel to assist and guide users as required 				
	Works near Signals:				
Attended (night)	 Any affected signal loops must be notified to WTOC during the pre-installation call to allow them to adjust signal management. 				
	Works near Pedestrian Crossings:				
	TM-W's to guide pedestrians through/around the closure.				
	Works near a Bus Stop:				
	Bus stop integrated into MTC Stop Point				
	MTC's on stop/go are to stop each bus and assist with loading & unloading of passengers as required.				
	Bus stop signage is to direct pedestrians towards the stop point				
	Bus stop relocated away from site				
	Bus stop signage is be placed to show patrons where the relocation is.				
	TM personnel to assist and guide bus patrons as required				
	Temporary bus stop signage is to be used				
Unottonded (des)	Parking restrictions are to be in place at the relocated bus stop An unottonded site is not required for non-execution works.				
Unattended (day)	An unattended site is not required for non-excavation works.				





Unattended (night)	An unattended site is not required for non-excavation works.
Detour route	A detour route is not required or approved in the TMP



APPROVED
CAR E1068566

Phil Gollings





	Does detour route go into another RCA's roading network? No				
	If Yes, has confirmation of acceptance been requested from that RCA? No				
	Note: Confirmation of acceptance from affected RCA must be submitted prior to occupying the site.				
	STMS to contact Metlink (0800 801 700) upon site removal				
	STMS to contact WTOC (0800 869 286) upon site removal.				
	Work plant / vehicles to be removed from site before closure is removed				
	Removal of the site will be done under a level 1 mobile closure with appropriate work vehicles and crew.				
Removal	Workspace delineation to be removed first (by either removing to the kerb for later collection or directly onto a stationary working vehicle)				
	Centreline delineation may now be removed using the same method as installation				
	Once all delineation is removed – sign removal may commence in a clockwise 'loop' fashion (leaving advanced warning signage in place till last)				
	A full site check being conducted prior to site departure.				
	The STMS will carry out the final check before leaving the site.				

Proposed TSL	Proposed TSLs (see TSL decision matrix for guidance)				
	TSL details as required Approval of Temporary Speed Limits (TSL) are in terms of Section 7 of Land Transport Rule: Setting of Speed Limits 2022. (List speed, length and location)	Times (From and to)	Dates (Start and finish)	Diagram ref. no.s (Layout drawings or traffic management diagrams)	
Attended day/night	A temporary maximum speed limit is hereby fixed for motor vehicles travelling over the length of situated between (house no./RP) and (house no./RP) on (street or road name) STMS to document on the Onsite Record daily.	7am – 6pm Or 9am – 4pm Or 7pm – 5:30am	01/01/2025 - 31/12/2025	F2.11, F2.12, F2.13, ATMS02, F2.14, ATMS04, F2.22, F2.15, F2.16, F2.17, F2.18, F2.19, F2.20, F2.21, F2.30, F2.31, F2.8, F2.9, ATMS03, J2.19a, J2.20a, J2.20b, J2.20c, J2.20d, J2.20e,	
Unattended day/night	A temporary maximum speed limit is hereby fixed for motor vehicles travelling over the length of situated between (house no./RP) and (street or road name)	N/A	N/A	N/A	
TSL duration	Will the TSL be required for longer than 12 months? If yes, attach the completed checklist from section I-18: 6 Processes for TSLs to this TMP.	Guidance on TMP I	Monitoring	No	

Positive traffic management measures

APPROVED CAR E1068566 Phil Gollings


Section P, appendix A. Traffic management plans
Page 11





- Side friction delineation installed from TSL to the start of the taper.
- Additional cones may be placed on centerlines, edgelines or shoulders to increase site safety and reduce vehicle speed.
- Use of paddles and TSL
- Cone offset delineation where cones are placed either side of the lane(s), the cones on one side are placed longitudinally
 offset from the other by half a cone spacing.

Reduced cone spacing (2.5m) can be utilised to increase impact

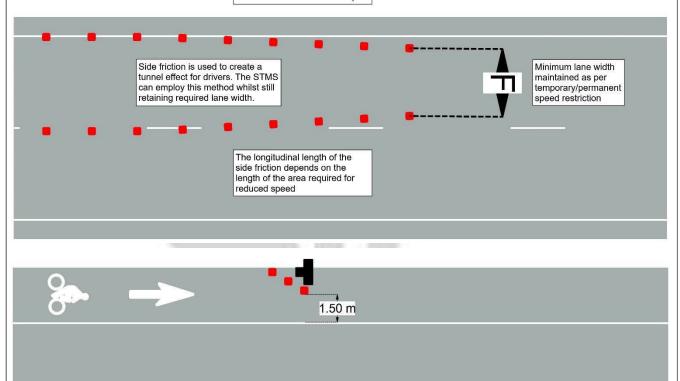

1.50 m

APPROVED
CAR E1068566
Phil Gollings



Contingency plans

Generic contingencies for:

- major incidents
- incidents
- pre planed detours.

Remove any options which do not apply to your job

Major Incident

A major incident is described as:

- Fatality or notifiable injury real or potential
- Significant property damage, or
- Emergency services (police, fire, etc) require access or control of the site.

Actions

The STMS must immediately conduct the following:

- stop all activity and traffic movement
- secure the site to prevent (further) injury or damage
- contact the appropriate emergency authorities
- render first aid if competent and able to do so
- notify the RCA representative and / or the engineer
- under the guidance of the officer in charge of the site, reduce effects of TTM on the road or remove the activity if safe to do so
- re-establish TTM and traffic movements when advised by emergency authorities that it is safe to do so
- Comply with any obligation to notify WorkSafe.

Incident

An incident is described as:

- excessive delays real or potential
- minor or non-inquiry accident that has the potential to affect traffic flow
- structural failure of the road.

Actions

The STMS must immediately conduct the following:

- stop all activity and traffic movement if required
- secure the site to prevent the prospect of injury or further damage
- notify the RCA representative and / or the engineer
- STMS to implement a plan to safely remove TTM and to establish normal traffic flow if safe to do so
- re-establish TTM and traffic movements when it is safe to do so and when traffic volumes have reduced.

Detour

If because of the on-site activity it will not be possible to remove or reduce the effects of TTM once it is established a detour route must be designed. This is likely for:

- excessive delays when using an alternating flow design for TTM
- · redirecting one direction of flow and / or
- total road closure and redirection of traffic until such time that traffic volumes reduce and tailbacks have been cleared.

The risks in the type of work being undertaken, the risks inherent in the detour, the probable duration of closure and availability and suitability of detour routes need to be considered.

The detour and route must be designed including:

- pre- approval form the RCA's whose roads will be used or affected by the detour route
- ensure that TTM equipment for the detour signs etc are on site and pre-installed.

Actions

When it is necessary to implement the pre-planned detour the STMS must immediately undertake the following:

- Notify the RCA and / or the engineer when the detour is to be established
- Drive through the detour in both directions to check that it is stable and safe
- Remove the detour as soon as it practicable and safe to do so and the traffic volumes have reduced and tailbacks have cleared
- Notify the RCA and / or the engineer when the detour has been disestablished and normal traffic flows have resumed.

CAR E1068566 Phil Gollings





	Note also the requirements for no interference at an accident scene:					
	In the event of an accident involving serious harm the STMS must ensure that nothing, including TTM equipment, is removed or disturbed and any wreckage article or thing must not be disturbed or interfered with, except to:					
	save a life of, prevent harm to or relieve the suffering of any person, or					
	make the site safe or to minimise the risk of a further accident; or					
	maintain the access of the general public to an essential service or utility, or					
	 prevent serious damage to or serious loss of property, or 					
	follow the direction of a constable acting in his or her duties or act with the permission of an inspector.					
Other contingencies to be identified by	This will be determined on a case-by-case basis. Where achievable works will stop until emergency or delays have been cleared.					
the applicant (i.e. steel plates to quickly cover	Should signals or e-STOPs fail – Manual Traffic Control is to be installed immediately (refer to F2.14 & F2.22).					
excavations)						

Authorisations					
Parking restriction(s)	Will controlled street parking be affected?		Yes (potentially)	Has approval been granted?	N/A
alteration authority	Where Mobility Parking are aff assist and guide users as requ		o be provided (s	ame side of road, as close as possible), TM	A personnel to
Authorisation to work at permanent	Will portable traffic signals be used or permanent traffic signals be changed?		Yes (potentially)	Has approval been granted?	No
traffic signal sites	WTOC to be notified 30 mins p	prior to site installa	tion and upon re	moval.	
Road closure authorisation(s)	Will full carriageway closure continue for more than 5 minutes (or other RCA stipulated time)?		No	Has approval been granted?	No
	N/A				
Bus stop relocation(s) –	Will bus stop(s) be obstructe activity?	ed by the	Yes (potentially)	Has approval been granted?	No
closure(s)	Pre-approval required before works commence. Metlink will be notified 30 mins prior to installation and upon removal.				
Authorisation to use portable traffic signals	Make, model and description/number	'			
	NZTA compliant?	Yes			

EED			
Is an EED applicable?	EED is not required	EED attached?	EED is not required

Delay calculations/trial plan to determine potential extent of delays

APPROVED
CAR E1068566

Phil Gollings

Section E, appendix A. Traffic management plans





e-STOP & Stop Go Closures:

Delays of up to 5 minutes can be expected due to the nature of the TTM implemented. The STMS is to take measures to ensure delays remain under 5 minutes at all times, and queues do not extend past the advance warning signage.

If delays are occurring or excessive queueing is apparent, the STMS is to implement one of the following contingency plans;

- 1) Traffic Metering
 - Send only a specific amount of vehicles per side instead of clearing the entire queue
- 2) Pause works and open site
 - Make the site safe, remove plant and vehicles from the carriageway and open the tapers
- 3) Prioritise high flow route
 - Send vehicles from the approach with the highest flow first. Hold side street traffic for slightly longer if required.
- 4) Install additional signage
 - Install T2A/T234 "Warning Hidden Queue" signage up to 2xB from the initial advance warning signage for additional advance warning

STMS will continuously monitor for delays - TMC will be notified of any excessive delays.

Public notification plan

A letter drop to residents and businesses is to be completed 5 working days prior to works commencing.

WTOC notification for any works which are in close proximity to traffic signals and/or for a communications plan on permanent VMS within Upper Hutt City region.

Public notification plan attached? No

On-site monitoring plan		
Attended	An STMS or delegated TMO will be on site at all times.	
(day and/or night)	2 Hourly Site Checks to be documented on the on-site record.	
(day anaror mgm)	STMS/TM-W to monitor and assist pedestrians, cyclists and driveways when needed.	
Unattended (day and/or night)	An unattended site is not required for non-excavation works.	

Method for recording daily site TTM activity (eg CoPTTM on-site record)

- Hazard ID sheet
- CoPTTM on-site record.
- Checking process for Generic TMPs form to be completed prior to set up of a worksite when using this TMP.

Site safety measures

- · All visitors/contractors to be inducted and hazard ID completed
- · PPE gear to be worn by all on site
- Toolbox meeting to be held prior to work commencing.
- Arm bars to be installed around the work area.
- STMS/TC to monitor and assist pedestrians, cyclists and driveway access at all times when required.
- Pedestrian ramps to be installed when required.

Temporary safety barrier system	Will a temporary safety barrier system be used at this worksite?	No	designed	the temporary safety barrier by an installation designer a ently reviewed as being fit for	nd	N/A
	Statement from temporary safety t	parrier instal	lation desig	ner attached	N/A	

CAR E1068566 Phil Gollings





Other information

LEVEL 1 LAYOUT DISTANCES TABLE

Permanent speed limit or RCA- designated operating speed (km/h)		≤50	60	70	80	90	100
Tra	ffic signs				(I)		
Α	Sign visibility distance (m)	50	60	70	80	90	100
В	Warning distance (m)	50 or 30*	80	105	120	135	150
C	Sign spacing (m)	25 or 15*	40	50	60	70	75
Saf	ety zones	landario de la constitución de l					
D	Longitudinal (m)	10 or 5*	15	30	45	55	60
E	Lateral (m)	1	1	1	1	1	1
Tap	pers			1	Vi		
G	Taper length (m)#	30	50	70	80	90	100
K	Distance between tapers (m)	40	50	70	80	90	100
Del	Ineation devices						
Cor	ne spacing in taper (m)	2.5	2.5	5	5	5	5
Cone spacing: Working space (m)		5	5	10	10	10	10

- Larger minimum distances apply on all state highways and also on all multi-lane roads. The smaller minimum distances may be applied on other roads to accommodate road environment constraints.
- * On non-state highways with speeds 50km/h or less, a 10m taper (with cones at 1m centres) may be used when there are road environment constraints (eg intersections and commercial accesses).

On all roads where shoulder width is less than 2.5m and the activity does not affect the live lane, a 10m shoulder taper is permitted (with at least 5 cones at no greater than 2.5m centres).

A taper of 30m (with cones at 2.5m centres) must be used where manual traffic control (stop/go), portable traffic signals or priority give way are employed.

Lan	e widths								
Spe	ed (km/h)	30	40	50	60	70	80	90	100
F	Lane width (m)	2.75	2.75	3.0	3.0	3.25	3.25	3.5	3.5

Except for delineation device spacings, which are maximum values, the distances specified in the above tables are minimum values.

Attached Diagrams

APPROVED
CAR E1068566

Phil Gollings

25 November 2024

Section E, appendix A. Traffic management plans
Page 16





Pedestrian Management

- 1. ATMS05 Pedestrian Escort (1st Choice)
- 2. F2.1 Pedestrian Diversion (berm) (2nd Choice)
- 3. F2.2 Pedestrian Diversion (berm) (3rd Choice)
- 4. F2.3 Pedestrian Diversion (carriageway) (4th Choice)
- 5. F2.4 Footpath Closed (5th Choice) Requires TMC approval

Works on berm/shoulders/Lane Width Reduction

- 6. CC1 Works on berm or footpath
- 7. CC2 Traffic not crossing road centre
- 8. CC3 Works on berm or footpath vehicle parked on berm
- 9. CC4 Footpath diverted onto shoulder or parking lane
- 10. CC5 Footpath
- 11. CC7 Valve in Shoulder or berm
- 12. F2.5 Works on berm
- 13. F2.6 Works on parking lane
- 14. F2.7 Shoulder Closure
- 15. F2.11 Lane Width Reduction
- 16. F2.12 Lane Width Reduction (median)

Inspection Activities

- 17. F4.10 Inspection Activity
- 18. ATMS07 Inspection Activity Centre of Road

Lane Closures/Diversions/e-STOP/MTC/Traffic Lights/Centre Of Road

- 19. F2.13 Two Lane Diversion
- 20. ATMS02 -2 Way e-STOP
- 21. F2.14 2 Way MTC
- 22. ATMS04 e-STOP with MTC
- 23. F2.22 3-4 Way MTC
- 24. F2.15 Stop Stop
- 25. F2.16 Priority Give Way Requires TMC approval
- 26. F2.17 Traffic Lights
- 27. F2.18 Works in centre of road
- 28. F2.19 Intersection
- 29. F2.20 Intersection
- 30. F2.21 Works in middle of intersection
- 31. F2.30 Left Lane Closure (1 way, 2 lane)
- 32. F2.31 Right Lane Closure (1 way, 2 lane)

Mobile Operations/Semi Statics

- 33. CC8 Valve towards left of lane
- 34. CC9 Valve towards right of lane
- 35. CC12 Two way Two Lane Road
- 36. F4.1 Mobile Operation 5m from edgeline
- 37. F4.2 Mobile Operation within 5m of edgeline
- 38. F4.3 Mobile Operation with pilot
- 39. F4.4 Mobile Operation work vehicle in lane
- 40. ATMS06 Semi Static (right or left lane)
- 41. Mobile Closure L1 Install & Removal

APPROVED

CAR E1068566 Phil Gollings

Section E, appendix A. Traffic management plans

VAGENCE

Page 17





Cycle Lanes

- 42. F2.8 Cycle Lane Diversion
- 43. F2.9 Cycle Lane Diversion
- 44. ATMS03 Cycle Lane e-STOP

Section J diagrams

- 45. J2.16a
- 46. J2.19a
- 47. J2.20a
- 48. J2.20b
- 49. J2.20c
- 50. J2.20d
- 51. J2.20e

APPROVED
CAR E1068566
Phil Gollings

Section E, appendix A. Traffic management plans
Page 18





Contact details						
	Company / Council	Name	24/7 contact number	CoPTTM ID	Qualificatio n	Expiry date
Principle	Wellington Water	Bob Wilson	027 3355 334	-	-	-
ТМС	Upper Hutt City Council	Phil Gollings	021 495 822	148577	STMS (A) NP	07/11/25
Engineers' representative	Wellington Water	Bob Wilson	027 3355 334	-	-	-
Service Delivery Manager	Wellington Water	Steve Watt	021 507 440	-	-	-
	Action Civil	Dave Murtagh	027 442 2971			
	Agricontracts Hutt Ltd (CAS)	Jaden Munn	027 319 4575	-	-	-
	Aidan Kelly Contracting (AKC)	Cory Hikuroa	021 455 361	-	-	-
	ATMS	David Quintela	027 213 5654	-	-	-
	Alliance Services Ltd	Chris Barlow	021 640 282	-	-	-
	Anzel Limited	Darryl Tatana	021 281 1102	-	-	-
	Arthur D Riley & Co Ltd	Chris Parkinson	04 472 7614	-	-	-
	Brian Perry Civil	Blair Mould	027 229 3270	-	-	-
	Stantec	AJ Weir (Alice)	027 331 9930	-	-	-
		Andrea	021 222 8756			
	011 0 111	Brett Eaton	021 861 772			
	City Care Ltd	Mark Thompson	027 542 6244	-	-	-
	Constructions Contracts Limited	David Howard	021 243 6656	-	-	-
	Cubic Metre	Andrew McWhirter	021 345 79			
	Daniel Renshaw Drainage Contractor Ltd	Daniel Renshaw	027 450 8799	-	-	-
Contractor	Davies Waste Solutions	Jan Godfrey	04 528 9909	-	-	-
Interim	Dawson Waste Services Ltd	Dave Phillipson	022 657 2402	-	-	-
Contacts	Detection Services	Ross Beckett	04 915 0530	-	-	-
	DMK Contracting	Deon Kumm	027 202 5142	-	-	-
	Downer New Zealand	Sam Farnworth	021 896 603	-	-	-
	Drain Doctor NZ Ltd	Ian Pauley	027 484 8887	-	-	-
	E Carson & Sons	Eddie Carson	027 442 4343	-	-	-
	E N Ramsbottom Ltd	Michelle Hoffman	027 471 6246	-	-	-
	Fulton Hogan	Duncan Mundell	027 4786 203	-	-	-
	G & C Diggers	Mark Dennes	022 350 7550	-	-	-
	G P Friel Ltd	Dave Philipson	022 657 2402	-	-	_
	Greenstone Contracting Ltd	David Williams	04 566 0890	-	-	-
	Groundworks Ltd	Hamish Rees	027 765 6139	-	-	-
	Horokiwi Paving Limited	Peter Green	027 443 2206	-	-	-
	Hydrotech Limited	David Neru	09 600 0888	-	-	-
	Inline Drainage Limited	Patrick Carson	027 <mark>2</mark> 94 0952	-	-	-
	Intergroup Ltd	Alex Phelan	/ E 021 927 801	-	-	-

CAR E1068566 Phil Gollings

Section E, appendix A. Traffic management plans
Page 19





Ives Plumbing Ltd	Daniel Barnett	021 758 621	-	-	-	
JB's Environmental Ltd	John Matangi	021 750 920	-	-	-	
Jet Black Asphalts Ltd	Neville Playford	027 208 9309	-	-	-	
Juno Civil	Jim Juno	021 227 7001	-	-	-	
Laser Plumbing Wellington East	Simon Walker	027 449 1180	-	-	-	



APPROVED
CAR E1068566

Phil Gollings





- - - - - - -
- - - -
- - - -
<u>-</u> -
_
-
-
-
-
-
-
-
-
-
-
-
-
-
-
-
-
-
-
-
-

APPROVED

CAR E1068566 Phil Gollings





AGENCY	all all	u/or KCA contract fer	erence			
	ATMS	Vena Lam Sam	021 767 165	39930	Cat A,B,C	29/05/27
	Wellington Traffic Control	Martyn Sauaiga	027 348 9478	72781	Cat A,B (P) Cat C (NP)	19/08/25
	Hanging Around Traffic Management	Sam Redhill	021 505 900	-	-	-
TTM Interim	Men At Work - Traffic Management	Kurt Puryer-Smith	027 274 2369	-	-	-
Contacts	Men At Work - Traffic Management	Todd Lynch	027 282 0998	-	-	-
	SAP Contractors	Glenn Churches	027 272 1666	-	-	-
	Stapp Contracting Traffic Management	Shane Pihema	027 249 9882	-	1	-
	Traffic Management NZ Ltd	Steven Morgan	027 491 9494	-	-	-
	Leading Traffic	Chantelle Mereriana Ngaia	027 2555 5002	-	-	-
	Leading Traffic	Ben Teika	027 555 0997	-	-	-
	Trafficflow	Steven Huriwaka	021 944 037	-	-	-
	WTOC		0800 869 286	-	-	-
Others as required	Metlink Contac	t Centre	0800 801 700	-	-	-

APPROVED
CAR E1068566

Phil Gollings





TMP preparation							
Preparation	Pania Werahiko	07/11/2024	P.Werahiko	149481	STMS (A) NP -R STMS (B) NP -R	-	11/01/2026
					. ,		25/01/2026

This TMP meets CoPTTM requirements				f diagrams atta	ched	51		
TMP returned for								
correction (if required)	Name	Date	Signature	ID no.	Qualification	Expiry date		
Engineer/TMC to co	Engineer/TMC to complete following section when approval or acceptance required							
Temporary safety barrier system	The attached temporary road safety barri as being fit for purpose	er design has be	en independer	ntly reviewed	Not required			
TMD A								
TMP Approved	Name	Date	Signature	ID no.	Qualification	Expiry date		
Acceptance by	- A	III						
TMC (only required if TMP approved by engineer)	Name	Date	Signature	ID no.	Qualification	Expiry date		

Qualifier for engineer or TMC approval

Approval of this TMP authorises the use of any regulatory signs included in the TMP or attached traffic management diagrams.

This TMP is approved on the following basis:

- 1. To the best of the approving engineer's/TMC's judgment this TMP conforms to the requirements of CoPTTM.
- 2. This plan is approved on the basis that the activity, the location and the road environment have been correctly represented by the applicant. Any inaccuracy in the portrayal of this information is the responsibility of the applicant.
- 3. The TMP provides so far as is reasonably practicable, a safe and fit for purpose TTM system.
- 4. The STMS for the activity is reminded that it is the STMS's duty to postpone, cancel or modify operations due to the adverse traffic, weather or other conditions that affect the safety of this site.

Notification to TMC prior to occupying worksite/Notification completed									
Type of notification to TMC required		Notification completed	Date Time						

APPROVED
CAR E1068566
Phil Gollings

Traffic control devices manual part 8 CoPTTM

Section P, appendix A. Traffic management plans Page 23 Edition 4, April 2020

ROAD SPACE BOOKING

Address:					
Contractor:					
Dates & Times (attended):	From:			То:	
Dates & Times (unattended):	From:			То:	
Generic TMP used:					
Diagram (s) used:					
CAR#					
Work Ac	ctivity a	nd Reasor	ns TTM to re	main in	place:
	I				
Contractor Name:					
Contractors Signature:					
TMC Approval:					

Please attach photos of site active site set up (these photos are to include both ends of the site (inclusive of any side roads), pedestrian/cycle management and the working area.



APPROVED
CAR E1068566
Phil Gollings
Upper Hutt City Council

TEMPORARY SPEED LIMIT (TSL) INSTRUCTIONS Appendix B Select the appropriate road condition description for each of the four factors, and in the right hand circle list the **DECISION MATRIX** chosen TSL for that road condition. Transfer lowest TSL to the bottom circle. **WORKSHEET** Possible **EXCELLENT POOR AVERAGE BELOW AVERAGE Temporary** Speed Limit Minimum Lane Width 3.25m 3.00m 2.75m 3.5m Pavement / Surface Condition The shoulder and lane is clear of The road is close to normal condition Defects and / or loose material on the There are major defects and / or loose or greasy material and the except for a few minor defects lane (eg unattended reseals) significant loose material on the lane (eg recently milled surface, large traveled way is smooth (eg small pot holes or a few pieces of **50km/h** for protection of a new seal stones, steel plates) loose aggregate) 70km/h where new seal has been swept but not marked Visibility and Alignment There is greater than 140m visibility There is less than 140m visibility to the There is less than 60m visibility to the first There is less than 30m visibility to the first first cone in taper, to the first cone in taper, cone in taper, cone in taper, vehicles are deflected by 20 degrees or the worksite has not imposed a vehicles are deflected by 20-45 degrees vehicles are deflected by more than 45 less from the original direction of travel from the original direction of travel change in alignment degrees from the original direction of travel Deflected by less than 20° Deflected by 20° to 45° Deflected more than 45° Site Clutter Low site clutter, clear vehicle lanes. Some site clutter either plant or Considerable site clutter requires Has numerous driver distractions including cycle lanes and footpaths materials, vehicle lanes, cycle lanes additional management to guide construction traffic. and footpaths are lightly trafficked vehicles though the site. Cycle lanes or footpaths are closed. 30km/h for portable traffic signals, MTC Some queues of road users operations or where traffic has to traverse the actual active working space (either in a delineated single lane or where traffic is not separated from the working space) Is the lowest speed 80km/h or less and at Yes **Use this Temporary Speed Limit** least 10km/h below the permanent speed? **No Temporary Speed Limit Required** No

ON-SITE RECORD MOBILE OPERATIONS (On-site record must be completed and retained with the applied TMP for 12 months) Today's date										
STMS in charge of TTM										
Name		NZTA warrant	TTM ID Number	NZTA warrant expiry date	STMS signature	Time				
In charge STMS pre-sta	rt check									
	High-visibility garments are fit for purpose, in an acceptable condition and worn correctly?	Vehicle Xenon (or LED)/Beacons are fit for purpose?	LAS/RD6/AWVMS/VMS/ Horizontal arrow boards are fit for purpose?	purpose	Two-way radios available, operating OK and batteries are fully charged	Correct signs for work operation are fitted to all vehicles and are fit for purpose				
Time the check was completed:		In charge STMS signature:								

Operation record (To be completed for all ins	pection worksites/runs, mobile runs, semi-static site	es)		
Af	Work Activity Timing			
Affected Road name(s)	Worksite start point	Worksite end point	Start	End
	APPROVE CAR E1068566	D		
	Phil Gollings Upper Hutt City Cour	ncil	_	

TMP or generic plan reference

Checks (mu	ıst be completed and d	ocumented at least ev	very 30 minutes)				
Mobile closure	re						
Time	Distances between vehicles maintained	Lateral positioning of vehicles maintained	LAS/RD6/AWVMS/VMS/Horizontal arrowboards continue to operate correctly	Road clear and available for planned work?	Static equipment maintained?	Safety zones maintained?	Working space adequate and maintained?
		and or improvements	s to the approved TTM/TMP				
Time of comm	nent Detail						
			APPR(
			Phil Gollings Upper Hutt C				

Traffic control devices manual part 8 CoPTTM

TMP or generic plan reference

ON-SITE REC	CORD must be retained with TMP for 12 month	S.			Toda	y's date		
Location details	Road names(s):	House number/RPs	Su Su		Subu	ırb:		
Working sp	ace							
Person responsible for working space	Name		Signature					
Where the STN	MS/TC is responsible for both the working	g space and TTM they s	ign above and	d in the	appr	opriate TTM b	ox below	
TTM								
STMS in charge of TTM								
	Name	TTM ID Number	Warrant expir	y date	Signa	ture		Time
Worksite handover accepted by								
replacement STMS	Name Tick to confirm handover briefing	ID Number	Warrant expir	y date	Signature			Time
311/13	completed							
Delegation								
Worksite control								
accepted by TC/STMS-NP	Name	ID Number	Warrant expir	Warrant expiry date Signature				Time
	Tick to confirm briefing completed			_	_			
Temporary								
Street/road na	ame (RPs or street numbers):	TSL action	Date:	Time	:	TSL speed:	Length of	TSL (m):
		TSL installed TSL remains in place						
From:	To:	TSL removed						
	ame (RPs or street numbers):	TSL action	Date:	Time	,	TSL speed:	Length of	TSI (m)
Street/road rie	into (N 3 of 3treet numbers).	TSL installed	Date.	TITIC		TOE Speed.	Lengthon	TOL (III).
		TSL remains in place						
From:	To:	TSL removed						
Street/road na	ame (RPs or street numbers):	TSL action	Date:	Time	:	TSL speed:	Length of	TSL (m):
	, , , , , , , , , , , , , , , , , , ,	TSL installed				·		. ,
		TSL remains in place						
From:	To:	TSL removed						
Street/road na	ame (RPs or street numbers):	TSL action	Date:	Time	:	TSL speed:	Length of	TSL (m):
		TSL installed						·
		TSL remains in place						
From:	To:	TSL removed	h					
		APPROVER						

CAR E1068566 Phil Gollings Upper Hutt City Council


						_		
TMP	or	ann	oric	n	an	roto	ron	00
IIIVII	() (CIII.		CH I			7.7

WOLKSILE IIIOIIII								
TTM to be monitore	ed and 2 hourly in							
Items to be inspec	cted	TTM set-up	2 hourly check	TTM removal				
High-visibility garm	ent worn by all?							
Signs positioned as per TMP?								
Conflicting signs co	overed?							
Correct delineation	as per TMP?							
Lane widths approp	oriate?							
Appropriate positive	e TTM used?							
Footpath standards	s met?							
Cycle lane standard	ds met?							
Traffic flows OK?								
Adequate property	access?							
Barrier deflection at (Refer to Barrier de								
Add others as requ	ired							
Time inspection c	ompleted:							
Signature:								
Comments:								
Time	Adjustment m	nade and reas	on for change					
			APPF	ROVED	}			
			CAR E1068					


Upper Hutt City Council

<u> </u>	ss for generic TMPs								
	milar company record, must be com	npleted prior	to set u	up of a v	vorksite v	vhere a generi	c TMP is u	ısed.	
Location details									
Road name(s)			House numbe	r/RP(s)			,	Suburb	
Road name(s)			House numbe	r/RP(s)				Suburb	
Generic TMP reference no.	ТІ	MD no(s).						ne checking p nll the TMDs	process must to be used
Category	Points to consider		Υ	N C	Comment	:/Mitigation			
Road level	Is this at the correct road level?	?							
	Are the following catered for in TMP?	the generic							
	Intersections								
Shape	Vertical Curves (hills)								
	Horizontal Curves (corners)	Horizontal Curves (corners)							
	Sufficient advance warning								
	Check that there is:								
	sufficient length to place the direction and protection								
Direction and protection	sufficient road width to place planned direction and protection minimum lane width is 2.75r								
	adequate sight distance on								
	sufficient room to accommo required positive traffic cont								
Drangered anged	Is a TSL required?								
Proposed speed restrictions	Refer to the TSL decision matr CoPTTM (section E Appendix I								
Plant and equipment	Will your plant and equipment f designated working space?	fit within the							
Dana and anfah	Are all workers able to carry ou within the designated working s								
Personal safety	If not are they covered by the rinspections?	If not are they covered by the rules for							
	Is diagram(s) detailed in the ge	neric TMP?							
Layout diagrams Does the diagram(s) match the written section of the TMP?		written							
RCA notification	Has the RCA been notified?								
Completed by:									
STMS/TC in charge of									
worksite	Name		Sign	ature		Date	Qua	alification	ID number
(All names to be entered before site set-up)		APP	RO'	VEC					
site set-up)	Name	CAR E106	58 <mark>5%ig</mark> n	ature		Date	Qua	alification	ID number

Upper Hutt City Council

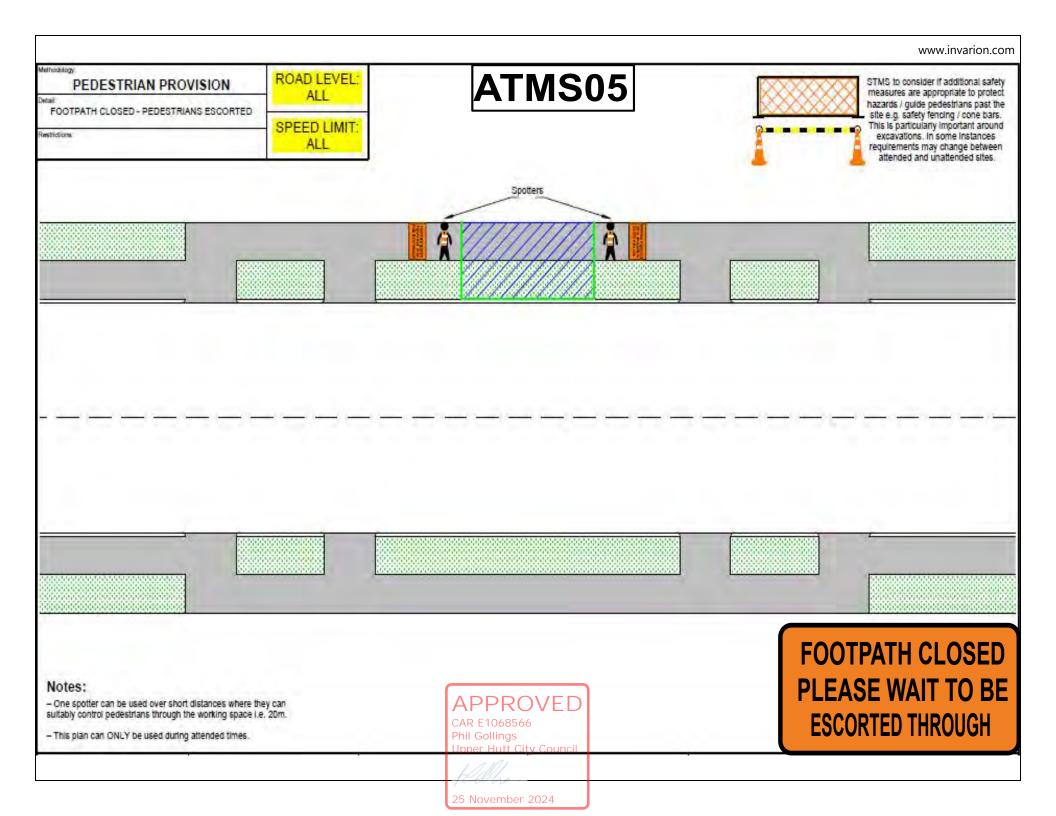


1. CC1 Work on berm or footpath - light vehicle parked in carriageway

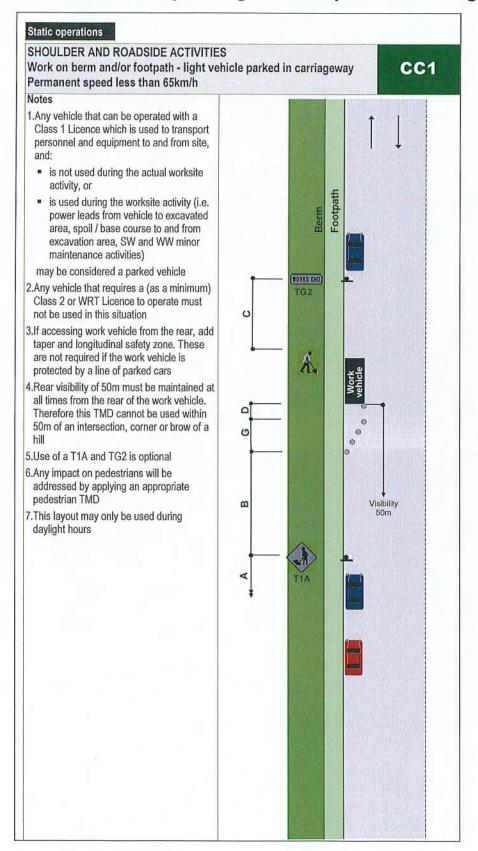




2. CC2 Traffic not crossing road centre - heavy vehicle parked in carriageway

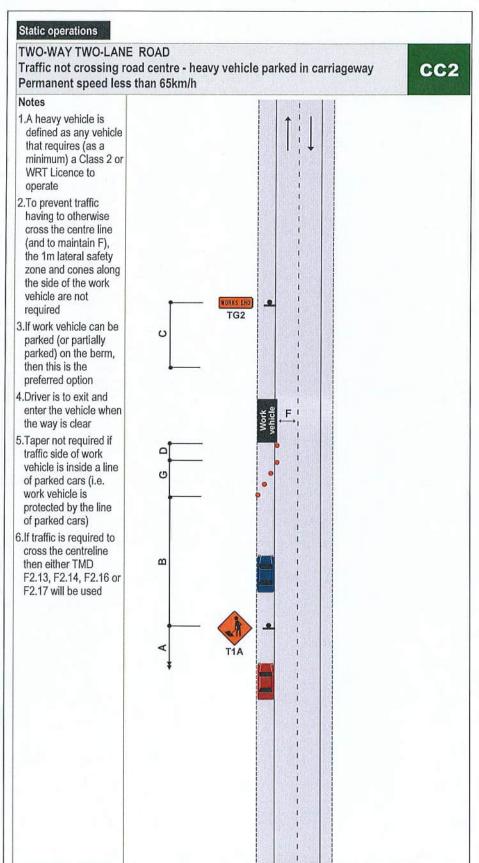




CC3 Work on berm and/or footpath - work vehicle parked on berm

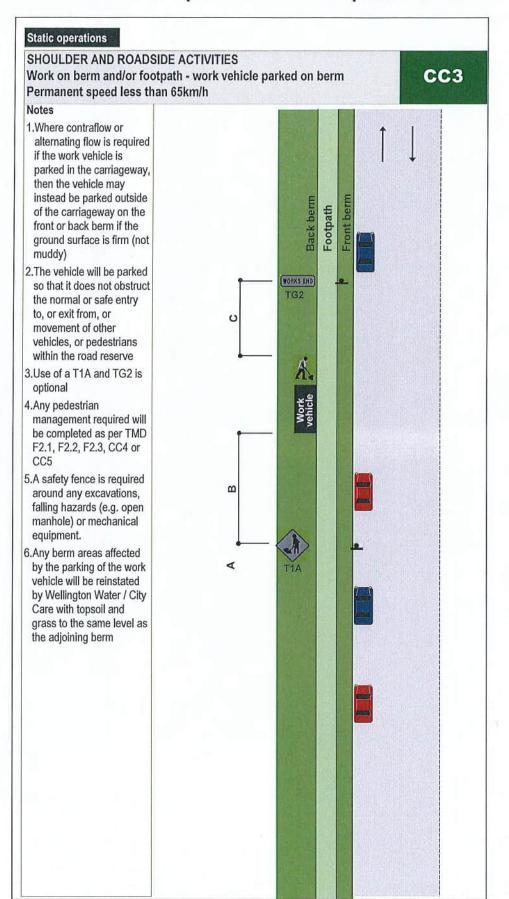




3. CC4 Footpath diverted onto shoulder or parking lane

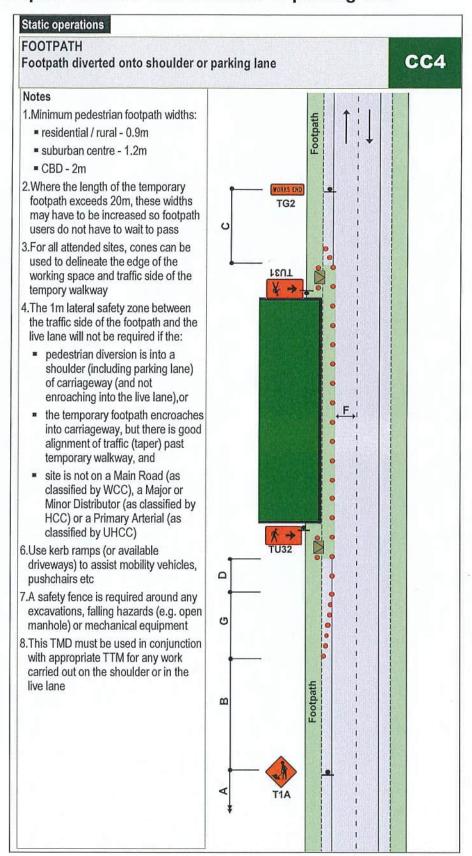



CC5 Footpath controller guiding pedestrians past the working space

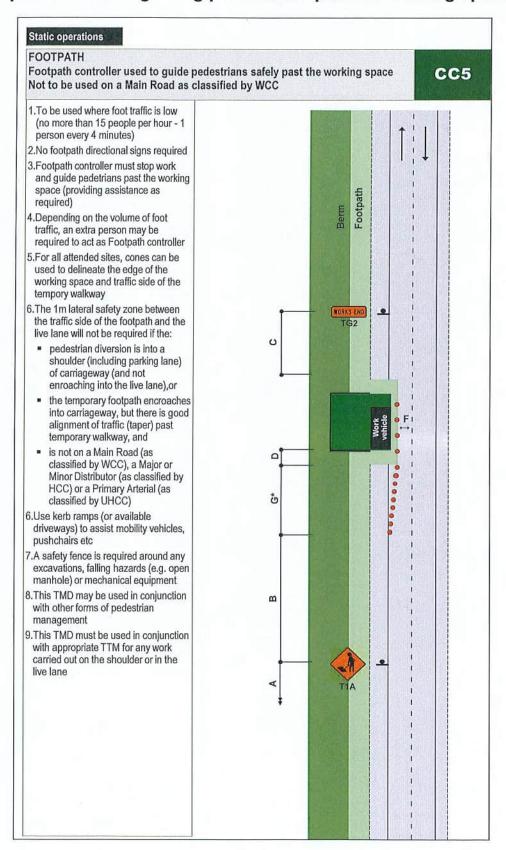




FOOTPATH

Footpath diverted onto berm behind working space First preference

F2.1 Level 1

Notes


- **1.**Minimum pedestrian footpath widths:
 - Residential/Rural/Suburban Centre - 1.2m
 - CBD 2m
- 2. Where the length of the temporary footpath exceeds 20m, these widths may have to be increased so footpath users do not have to wait to pass
- **3.**Temporary footpath surfaces must be suitable for footpath users
- 4.Use safety fence to enclose the working space, or at attended worksites, cones connected with cone bars can be used to enclose the working space but only for a short period of time Note: Cone bars are not recommended where heavy equipment (eg a digger) is being used. A safety fence is preferred in these cases
- **5.**This TMD must be used in conjunction with appropriate TTM for any work carried out on the shoulder or in the live lane



Footpath diverted onto berm between working space and carriageway Second preference F2.2 Level 1

Notes

- **1.**Minimum pedestrian footpath widths:
 - Residential/Rural/Suburban Centre - 1.2m
 - CBD 2m
- 2. Where the length of the temporary footpath exceeds 20m, these widths may have to be increased so footpath users do not have to wait to pass
- 3. Temporary footpath surfaces must be suitable for footpath users
- 4.Use safety fence to enclose the working space, or at attended worksites, cones connected with cone bars can be used to enclose the working space but only for a short period of time Note: Cone bars are not recommended where heavy equipment (eg a digger) is being used. A safety fence is preferred in these cases
- 5.Use barrier or safety fence to delineate the traffic side of the footpath, or at attended worksites cones connected with cone bars can be used to delineate the traffic side of the footpath for a short period of time (not for use on state highways)
- **6.**There must be a lateral safety zone between the traffic side of the footpath and the live lane:
 - 0.5m for barrier
 - 1m for safety fence or cone bars
- 7.ThisTMD must be used in conjunction with appropriate TTM for any work carried out on the shoulder or in the live lane

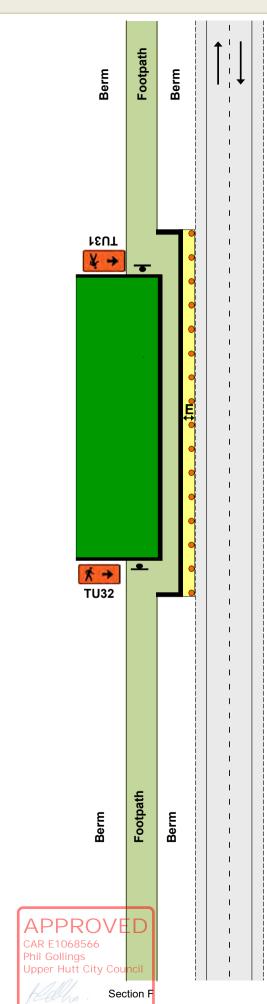


Footpath diverted onto carriageway Third preference

F2.3 Level 1

Notes

- 1.Minimum pedestrian footpath widths:
 - Residential/Rural/Suburban Centre - 1.2m
 - CBD 2m
- 2. Where the length of the temporary footpath exceeds 20m, these widths may have to be increased so footpath users do not have to wait to pass
- 3. Use safety fence to enclose the working space, or at attended worksites, cones connected with cone bars can be used to enclose the working space but only for a short period of time Note: Cone bars are not recommended where heavy equipment (eg a digger) is being used. A safety fence is preferred in these cases
- 4.Use barrier or safety fence to delineate the traffic side of the footpath, or at attended worksites cones connected with cone bars can be used to delineate the traffic side of the footpath for a short period of time (not for use on state highways)
- **5.**There must be a lateral safety zone between the traffic side of the footpath and the live lane:
 - 0.5m for barrier
 - 1m for safety fence or cone bars
- **6.**Use kerb ramps to assist mobility vehicles, pushchairs, etc
- **7.**At night-time, corners of safety fence may be illuminated with flashing amber warning lights
- 8.ThisTMD must be used in conjunction with appropriate TTM for any work carried out on the shoulder or in the live lane

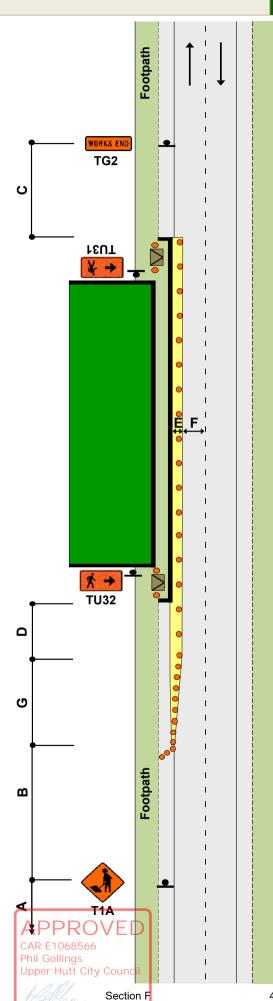

TMC APPROVAL REQUIRED


FOOTPATH

Footpath closed - permanent speed less than 65km/h Fourth preference

F2.4 Level 1


Notes

- 1.Use T2A and **PEDESTRIANS** supplementary plate to alert road users to the potential of footpath users crossing the carriageway
- 2.Use safety fence at each end of working space
- 3.Use kerb ramps
- 4.Use another TMD as well, where working space/safety zone encroaches on live lane
- 5. This TMD must be used in conjunction with appropriate TTM for any work carried out on the shoulder or in the live lane

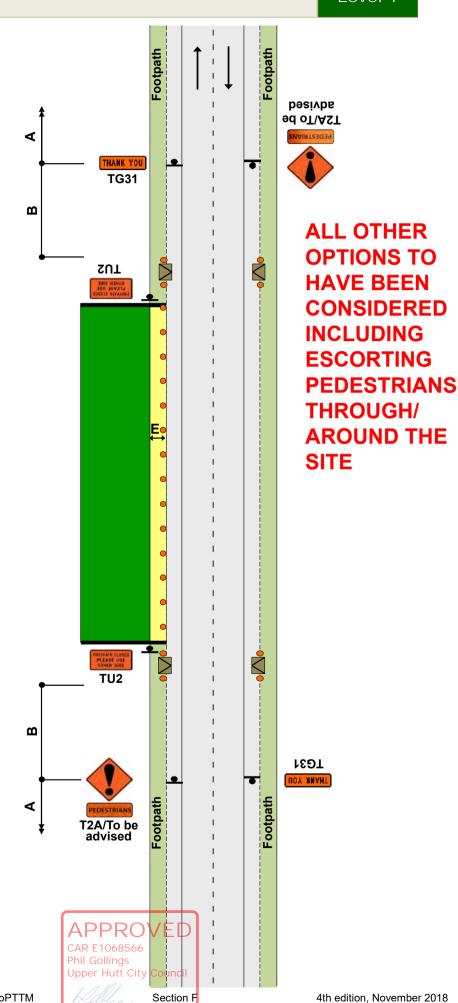



CC7 - Valve in shoulder or on berm

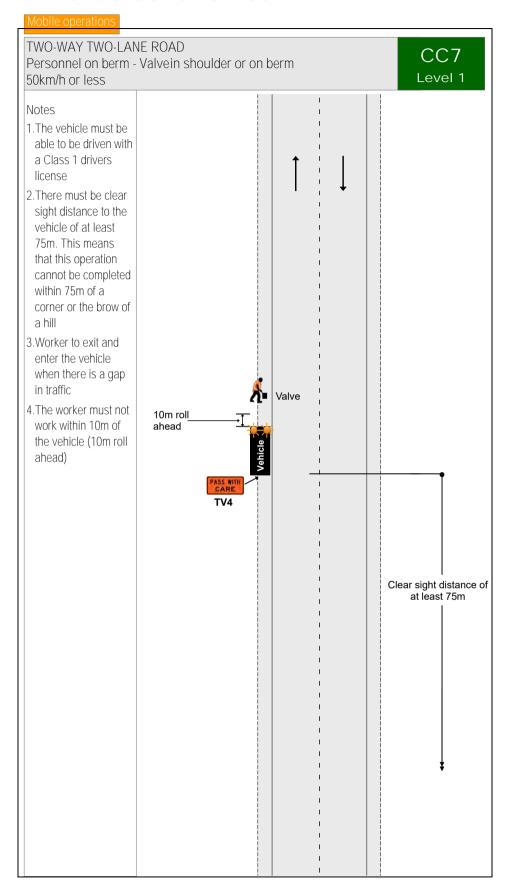


APPROVED
CAR E1068566

CAR E1068566 Phil Gollings

SHOULDER AND ROADSIDE ACTIVITIES Work on berm and/or footpath Permanent speed less than 65km/h

Notes


- 1. Where work is carried out on the berm or footpath and a work vehicle is parked in a legal parallel car park, provided the vehicle is only accessed from the off traffic side, advance warning T1A road works and TG2 WORKS END are optional
- 2.Traffic management must be provided where footpath users or cyclists are affected
- 3. This layout may only be used during daylight hours
- 4.Large plant and machinery must not be used in this situation, a more substantial closure is required

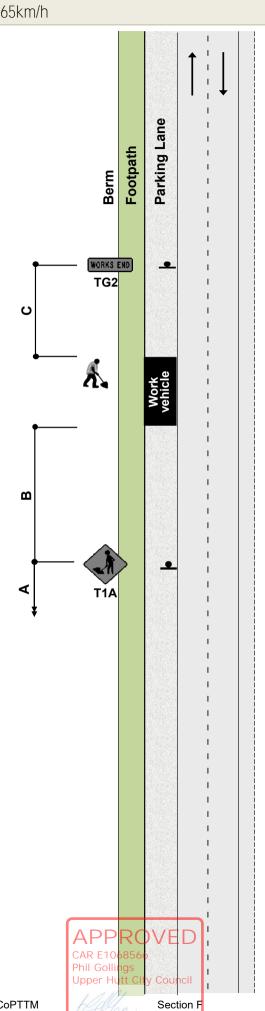

F2.6 Level 1

Notes

- 1. Where work is carried out in the legal parking lane (a place where a vehicle would normally park with a footpath and/or kerb and channel alongside), the following minimum standard of TTM must be provided:
 - a 10m taper in front of the work vehicle
 - cones alongside the work vehicle and the working space
 - a longitudinal safety zone
 - a 1m lateral safety zone along the working space
 - a T1A (or other appropriate advance warning sign) mounted on the back of the work vehicle
- 2.T1A road works and TG2 WORKS END signs are optional
- 3.The work vehicle must be no larger than a light truck and may have an amber flashing beacon
- 4.Traffic management must be provided where footpath users or cyclists are affected
- 5. This layout may only be used during daylight hours
- 6.Large plant and machinery must not be used in this situation, a more substantial closure is required

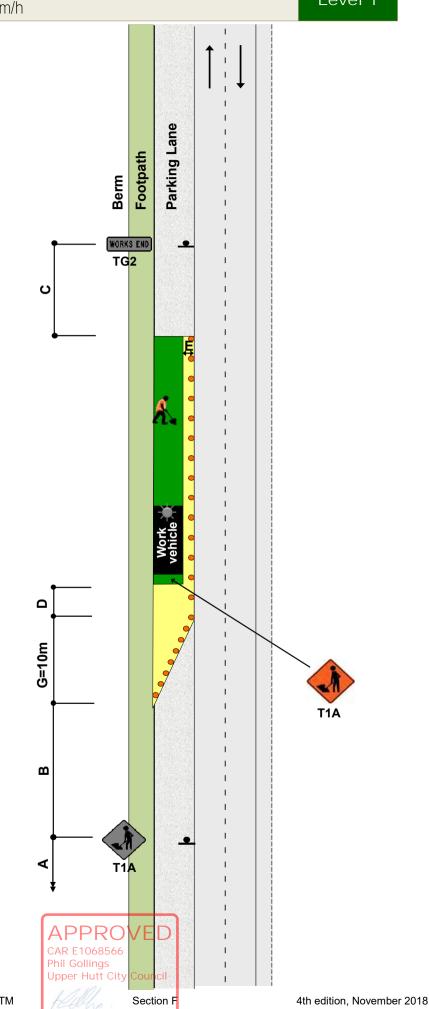

SHOULDER AND ROADSIDE ACTIVITIES Shoulder closure

F2.7 Level 1

Notes


- 1.A 10m taper is allowed where shoulder width is less than 2.5m
- 2.*For shoulders exceeding 2.5m width, apply the following calculation; calculation of taper length for lateral shift of less than 3.5m is:

$W \times G$

3.5

W = Width of shoulder


G = Taper length in metres from the level 1 layout distance table



Notes

- 1.*Calculation of taper length for lateral shift of less than 3.5m is: $W \times G$

 - 3.5
 - W = Width of lateral shift
 - G = Taper length in metres from the level 1 layout distance table
- 2.If traffic likely to cross the centreline, place cones on the centreline with RD6L signs at each end
- 3.Use TSLs if required by TSL decision matrix
- 4.If TSLs not required, the T1A and TG2 signs on the right hand side of the road are also not required
- 5.The T144 X0km/h AHEAD sign is optional

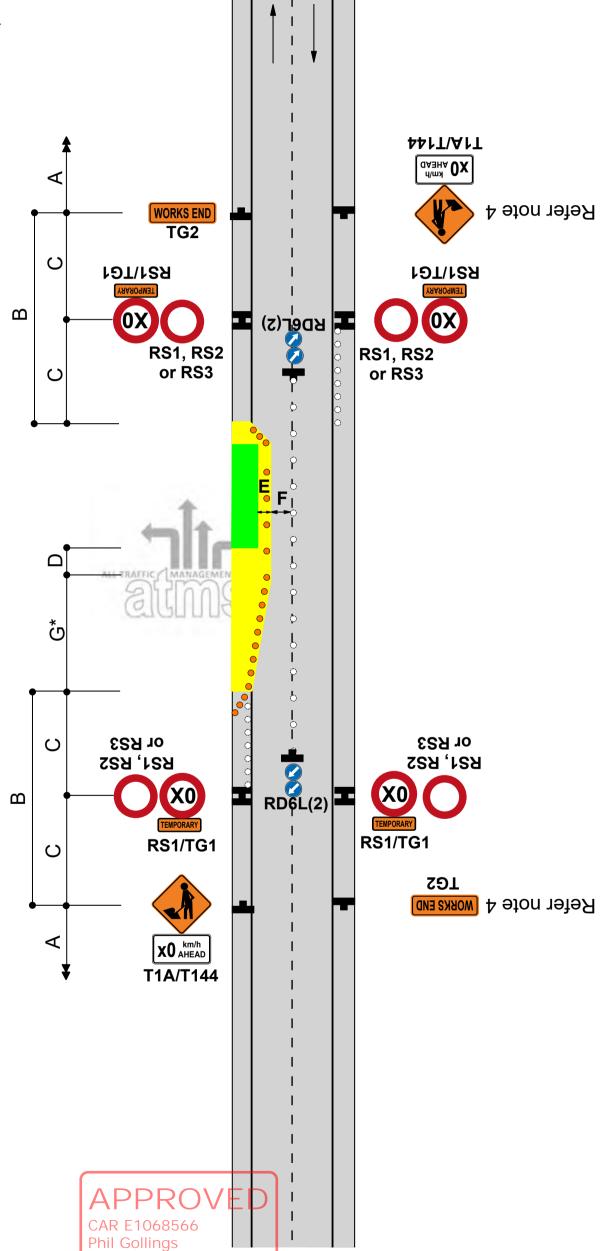

ices NZ and is not be used without written permission of ATMS NZ This design is the property of All Traffic Management Ser

4th edition, November 2018

Traffic control devices manual part 8 CoPTTMJpper Hutt City Counsection F

TWO-WAY TWO-LANE ROAD Traffic not crossing road centre Signs on median

F2.12 Level 1

Notes


- 1.Use this diagram if signs will not be visible on left-hand side of road, or if it is safer to place signs on median and this will not interfere with turning traffic movements
- 2. Where a median exists which is more than 2m wide, the signs may be positioned on the median. Signs must be placed back-to-back unless on a solid median
- 3. Where there is a solid median, signs are not required in the opposing direction
- 4.*Calculation of taper length for lateral shift of less than 3.5m is:

WxG

3.5

W = Width of lateral shift

- G = Taper length in metres from the level 1 layout distance table
- 5.Use TSLs if required by TSL decision matrix
- 6.The T144 X0km/h AHEAD sign is optional

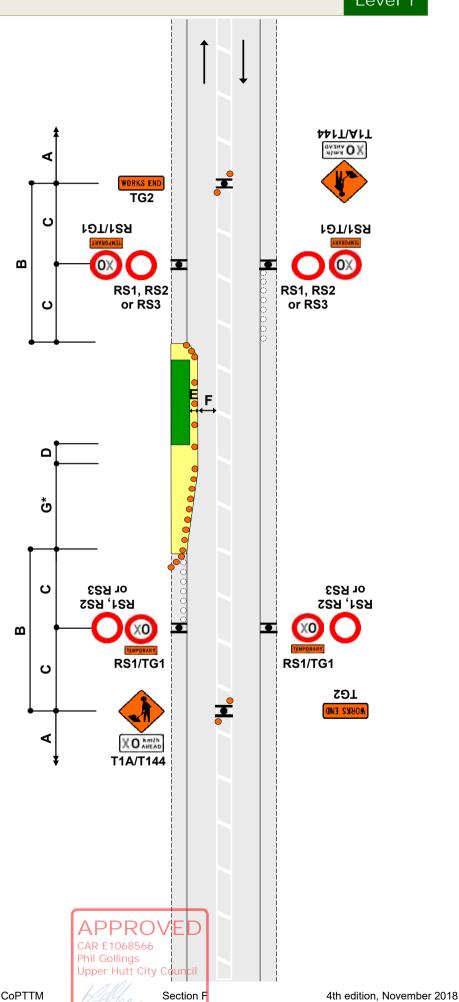

INSPECTION ACTIVITIES AND NON-INVASIVE WORKS On shoulder and on the live lane This TMD may also be applied on level LV roads

F4.10 Level 1

Notes

- Inspectors must move from live lanes to avoid traffic. They must not expect traffic to drive slowly or drive around them
- 2.On level LV and level 1 roads, a person completing an inspection or non-invasive works cannot be on a live lane for more than 5 minutes
- 3.Unless otherwise approved by the RCA, all inspections on the live lane of level 1 roads require a spotter. The RCA may provide a list of roads, times and/or activities suitable for inspection by a single inspector
- 4. There must be CSD to the inspector when on the live lane. If this cannot be achieved, a spotter must be placed in a position where CSD can be attained and verbal instructions be given to the inspector. If this is not possible, a static or mobile operation is required.
- 5.A spotter is not required for inspections and non-invasive works on level LV roads or working off the live lane of a level 1 road
- 6. Where an unaccompanied inspector is not able to maintain adequate attention (eg due to work tasks or poor visibility), a spotter will be required or another type of traffic management operation used
- 7. For inspection activities that are carried out by a TC on level LV and level 1 roads the STMS must be immediately contactable but does not have to be within 30 minutes travel time of the worksite
- 8.An unaccompanied inspector may walk across a level LV or level 1 road
- 9.A vehicle is not required on a level LV or level 1 road with a permanent speed of less than 65km/h if the inspector remains on a footpath
- 10.On roads with a permanent speed of less than 65km/h an amber flashing beacon is not required on the vehicle if the inspector or non-invasive works is on an unsealed shoulder (or further away from the carriageway including a footpath)

Forward visibility is greater than clear sight distance when inspector is on the live lane **Spotter required** when inspector on the live lane of a level 1 road (unless (s)П RCA has selected the road as suitable for 'single inspector' inspections) Rear visibility is greater than clear sight distance when inspector is on the live lane ROAD INSPECTION Rear visibility is greater TV3 than clear sight distance APPROVED CAR E1068566 Phil Gollings Upper Hutt City Council

Section F

25 November 2024

4th edition, November 2018


Mobile operations

INSPECTION ACTIVITIES AND NON-INVASIVE WORKS Inspection Activity - Centre Of Road This TMD may also be applied on level LV roads

ATMS07 Level 1

Notes

- Inspectors must move from live lanes to avoid traffic. They must not expect traffic to drive slowly or drive around them
- 2.On level LV and level 1 roads, a person completing an inspection or non-invasive works cannot be on a live lane for more than 5 minutes
- 3.Unless otherwise approved by the RCA, all inspections on the live lane of level 1 roads require a spotter. The RCA may provide a list of roads, times and/or activities suitable for inspection by a single inspector
- 4.There must be CSD to the inspector when on the live lane. If this cannot be achieved, a spotter must be placed in a position where CSD can be attained and verbal instructions be given to the inspector. If this is not possible, a static or mobile operation is required.
- 5. Where an unaccompanied inspector is not able to maintain adequate attention (eg due to work tasks or poor visibility), a spotter will be required or another type of traffic management operation used
- 6.For inspection activities that are carried out by a TC on level LV and level 1 roads the STMS must be immediately contactable but does not have to be within 30 minutes travel time of the worksite
- Inspectors MUST use 2 vehicles placed on either side of road shoulder. Inspector & spotter will use footpath to carry cones and cross when way is clear. Cones will be placed (min of 4 each direction) for protection. Spotter must not engage in work activities.

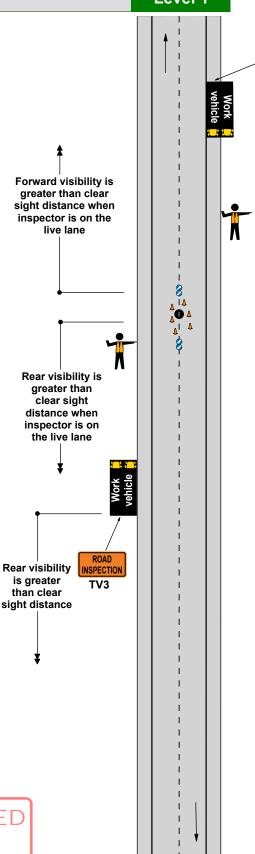

APPROVED


CAR E1068566 Phil Gollings Upper Hutt City Council

TWO-WAY TWO-LANE ROAD Traffic crossing road centre Two lane diversion

F2.13 Level 1

Notes

- 1.Cones are required on edge of the temporary lane opposite closure if road is not well defined
- 2.Return taper at end of closure may be shortened
- 3.*Calculation of taper length for lateral shift of less than 3.5m is: W x G 3.5 W = Width of lateral shift G = Taper length in metres from the level 1 layout distance table
- 4.To allow heavy vehicles to manoeuvre, cones in the channel must be offset by at least 10m where the direction changes. Refer C8.2.12
- 5.Use PN11 No Stopping signs, if necessary
- 6.Use TSLs if required by TSL decision matrix
- 7.The T144 X0km/h AHEAD sign is optional

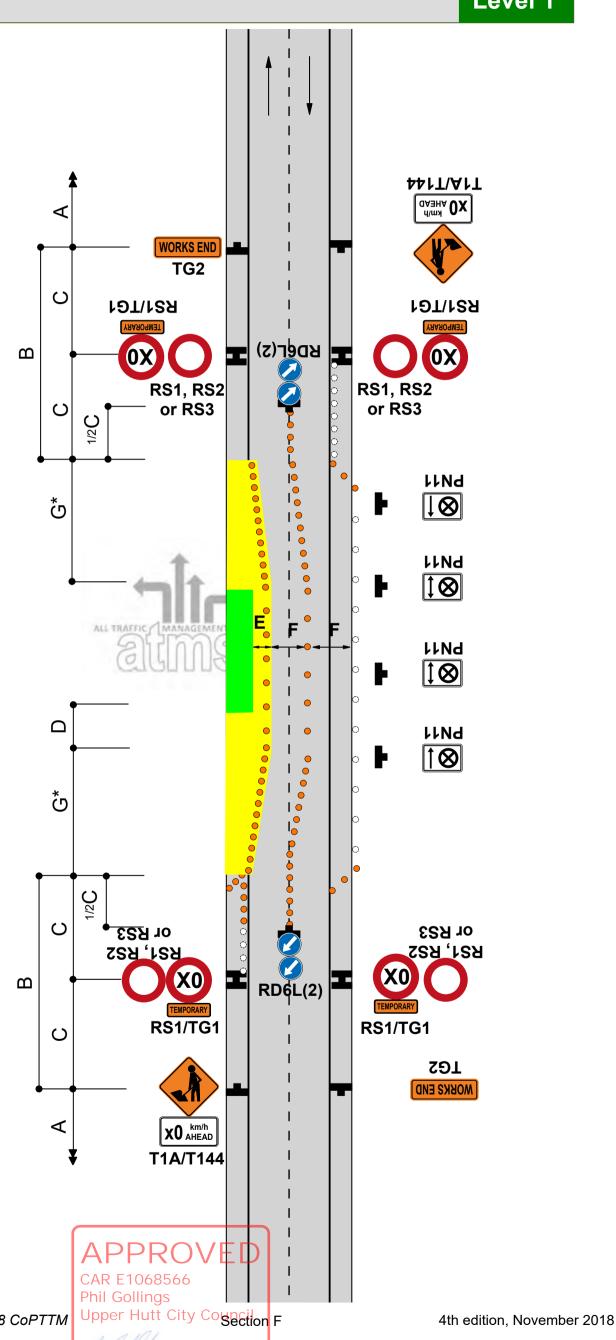

Traffic control devices manual part 8 CoPTTM

TWO-WAY TWO-LANE ROAD Single-lane alternating flow Portable e-STOP

ATMS02 Level 1

Notes THIS TMD IS NOT TO BE USED FOR ANY UNATTENDED PERIOD

- 1. Provide details of make and model of portable traffic signals in the TMP
- 2.Use PN11 no stopping signs, if necessary as per the approved TMP
- 3.Install temporary RP61/RP62 signs






- 4. Minimum 5 cones in cone threshold.
- 5. Extend or place extra advance warning signs towards on-coming traffic beyond any expected traffic queues

6.CONTINGENCY PLAN:

F2.14 to be implemented should issues arise with e-STOP/ adverse weather conditions or where stop go is unsuitable. ex; Short term stoppages is defined as "stopping traffic for a short period of time within a static site, at inconsistent intervals to assist with the entry/exit of vehicles or small tasks required to be undertaken in the live lane".

- 7. In circumstances where for safety reasons, the use of stop/go operations is deemed more appropriate, a site specific safe work method statement must be prepared.
- 8.The T144 30km/h AHEAD sign is optional on roads under 65km/h
- 9. e-STOP can only be used on an attended site. e-STOPs must be manned at all times.

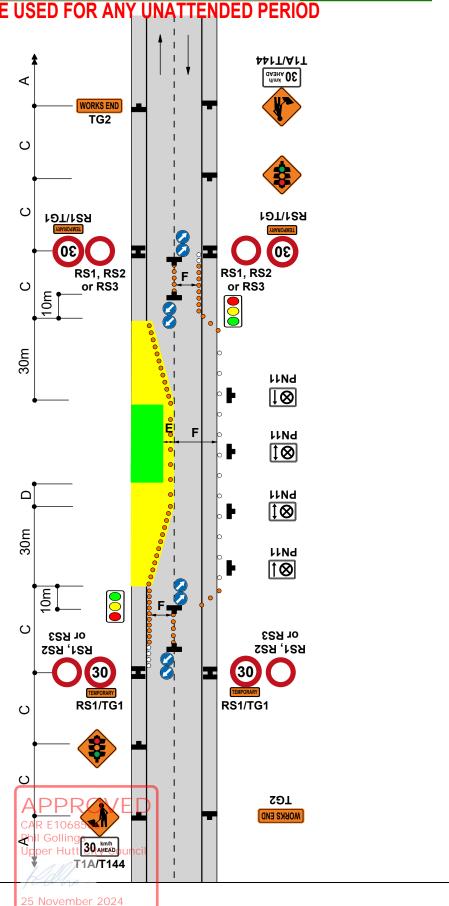



TWO-WAY TWO-LANE ROAD Single-lane alternating flow Manual traffic control (STOP/GO or STOP/SLOW)

Level 1

Notes

- 1.Extend or place extra advance warning signs towards on-coming traffic beyond any expected traffic queues
- 2.A 30m return taper at the end of the closure is mandatory
- 3. Cones are required on edge of the temporary lane opposite closure if road is not well defined
- 4.To allow heavy vehicles to manoeuvre, cones in the channel must be offset by at least 10m where the direction changes. Refer C8.2.12
- 5.Use PN11 no stopping signs, if necessary
- 6.MTC with RP4/RP41 STOP/GO or RP4/RP42 STOP/SLOW paddle on road shoulder located between 1st and 2nd cone in the cone threshold closest to the working space
- 7. Minimum 5 cones in cone threshold at:
 - 2.5m centres less than 65km/h
 - 5m centres more than 65km/h
- 8.Refer to C10.2.3 MTC essentials for further information
- 9. Delays cannot exceed the time approved by the RCA (normally 5 to 10 minutes)
- 10.The T144 30km/h AHEAD sign is optional

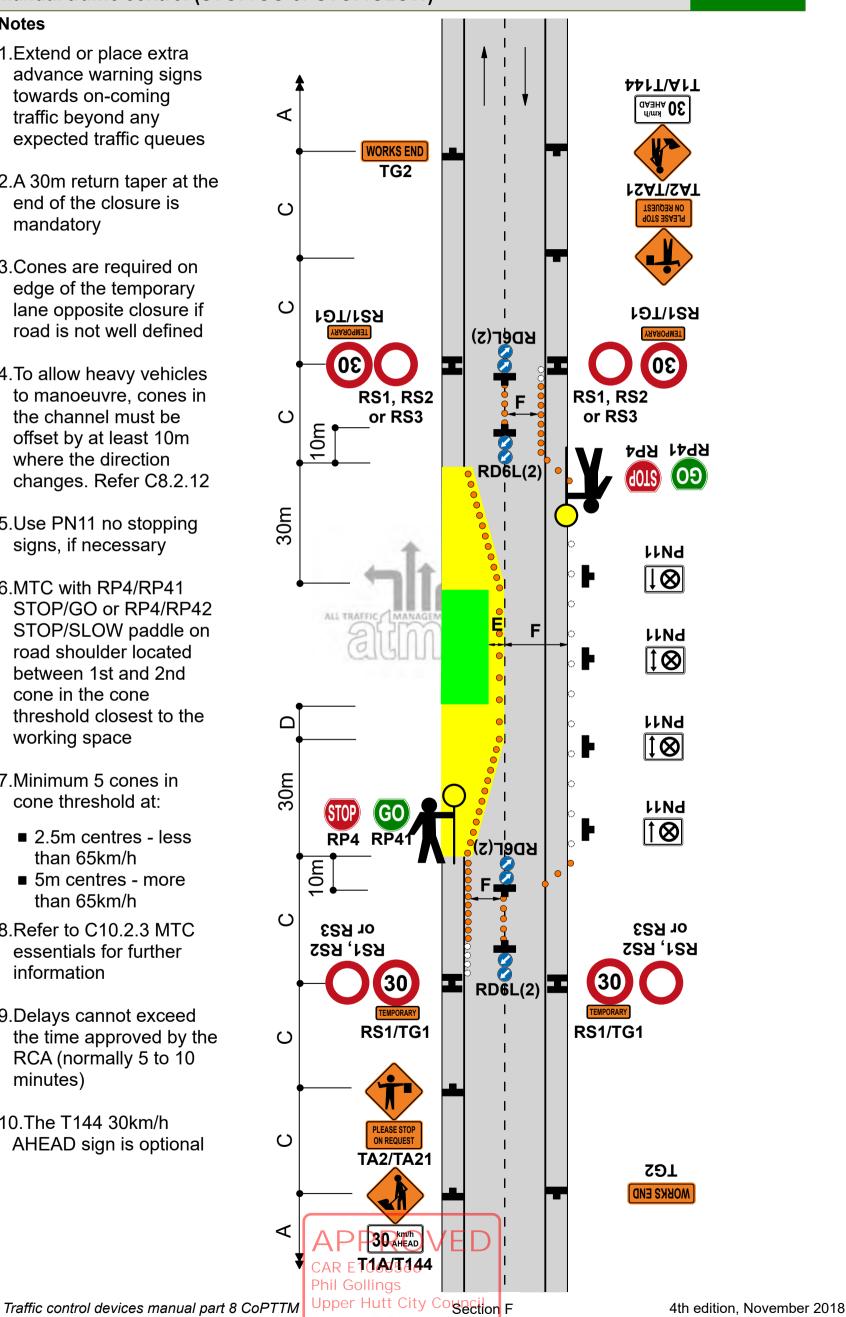

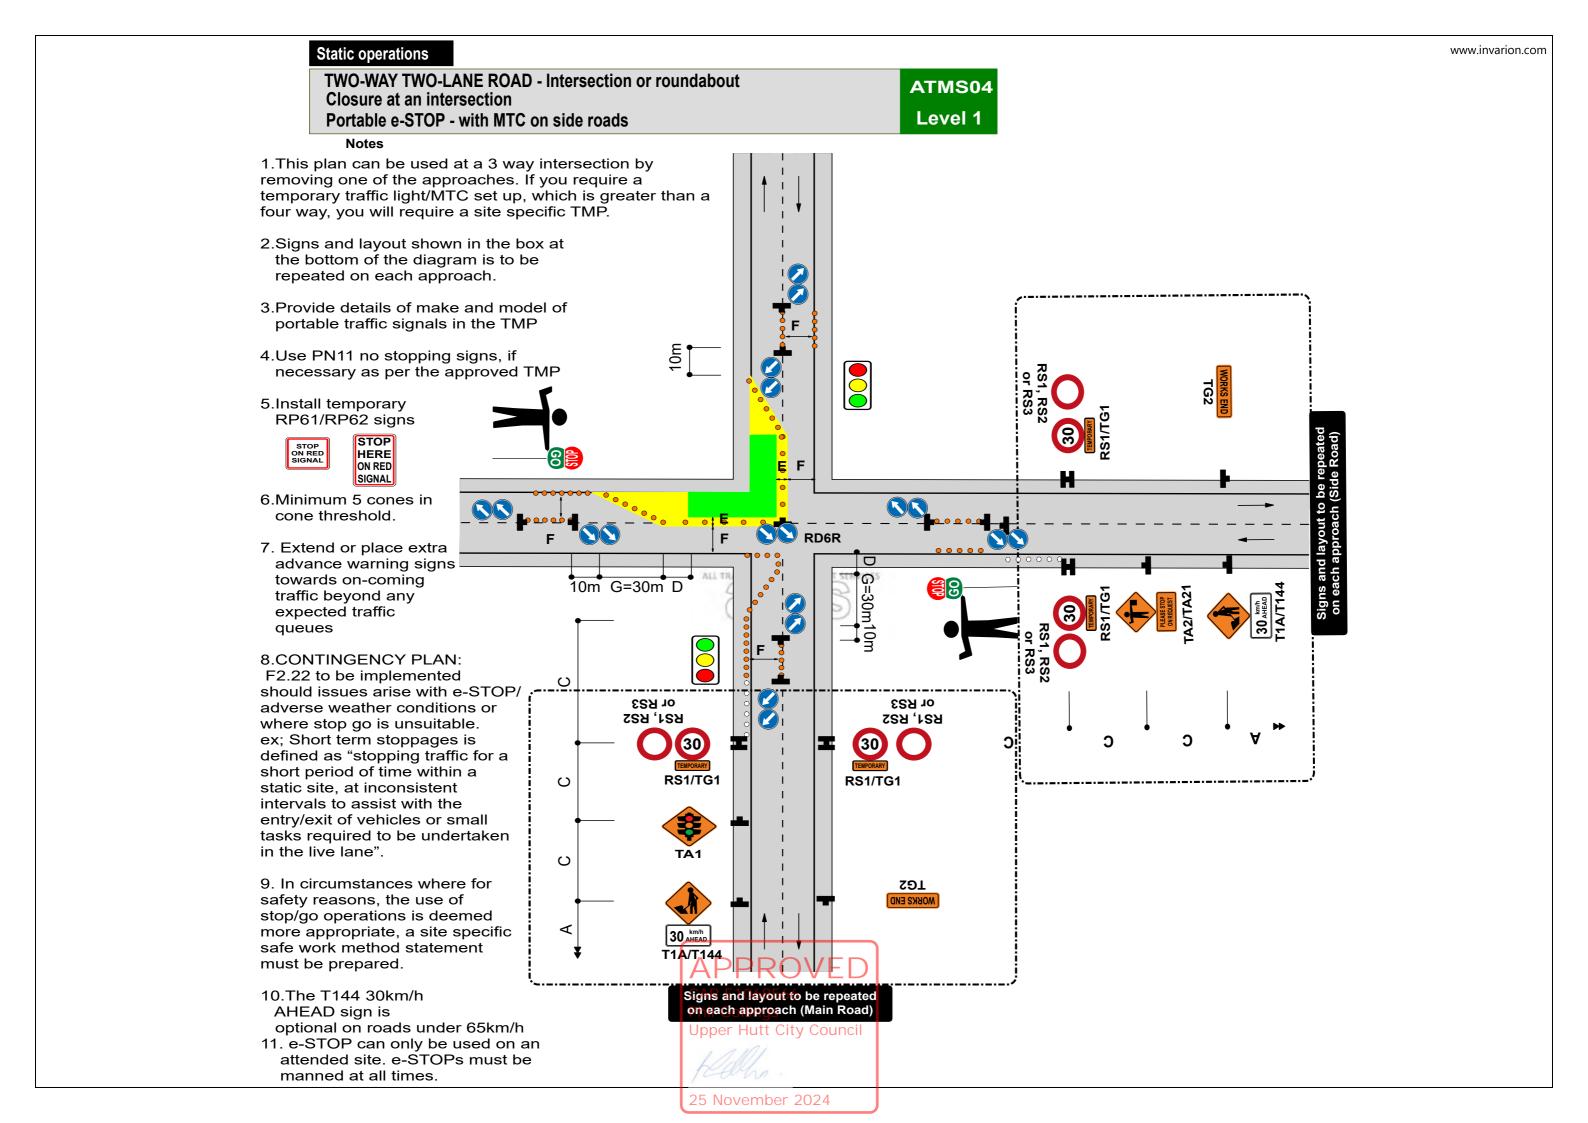


TWO-WAY TWO-LANE ROAD - Intersection or roundabout Closure at corner of an intersection Manual traffic control (Stop/Go or Stop/Slow)

F2.22 Level 1

Notes

- 1.This diagram may be used at a T intersection by removing any one of the roads
- 2.Signs and layout shown in the box at the bottom of the diagram is to be repeated on each approach
- 3.A 30m return taper at the end of the closure is mandatory
- 4.Use PN11 no stopping signs, if necessary
- 5.MTC with RP4/RP41 STOP/GO or RP4/RP42 STOP/SLOW paddle on road shoulder located between 1st and 2nd cone in the cone threshold closest to the working space
- 6.Minimum 5 cones in cone threshold at:
 - 2.5m centres less than 65km/h
 - 5m centres more than 65km/h
- 7.Refer to C10.2.3 MTC essentials for further information
- 8.On roads with a permanent speed limit of 100km/h, cones are required from the TSL to the taper if the speed is reduced by more than 30km/h
- 9.The T144 30km/h AHEAD sign is optional

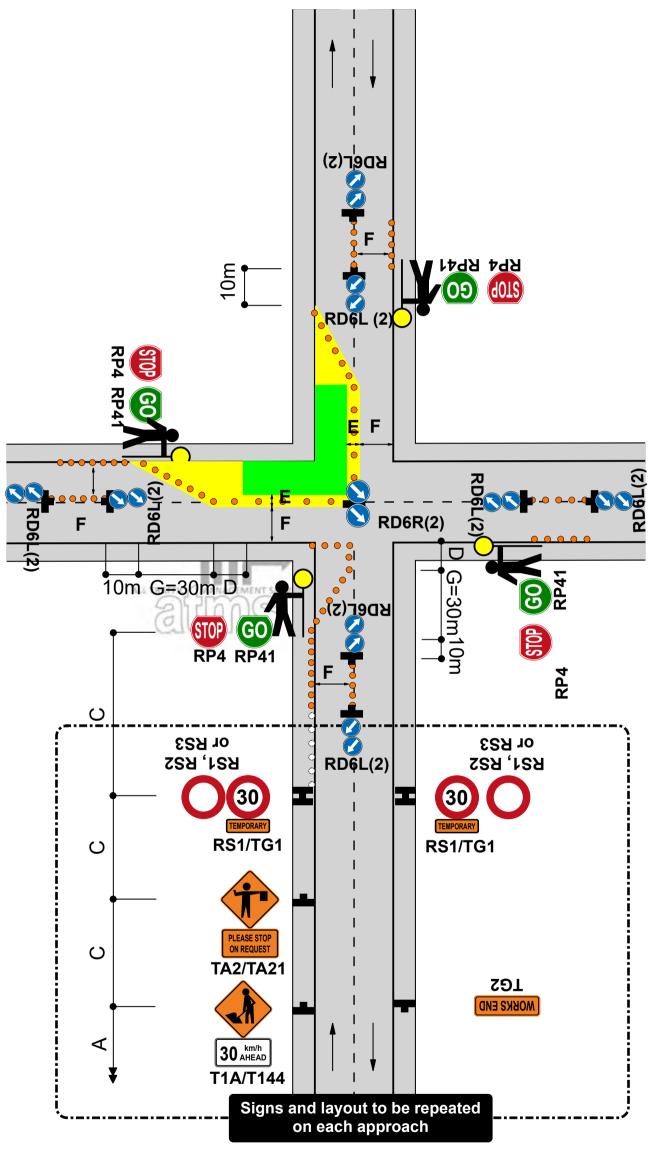

Traffic control devices manual part 8 CoPTTM


APPROVED

CAR E1068566
Phil Gollings
Upper Hutt City Cosection F

25 November 2024

4th edition, November 2018

eSTOPs at locations with limited road width or shoulder
The same risk assessment process should be undertaken
for placement of eSTOPs on these types of roads as if a
manual traffic controller was to be placed there.
Ideally approval should be sought for a full road closure.
Where this is not possible, placement of the eSTOP on the
live lane within a coned area as per the example below should

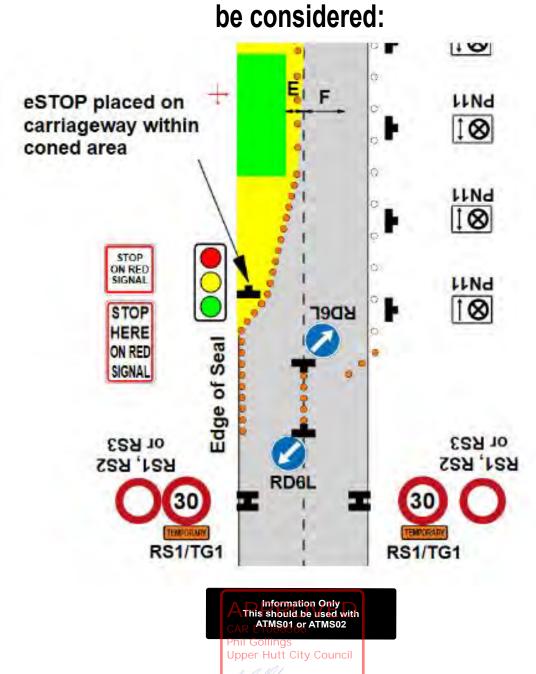


TWO-WAY TWO-LANE ROAD All traffic stopped temporarily Manual traffic control (STOP/GO or STOP/SLOW)

F2.15 Level 1

Notes

- 1.Closure period not to exceed the limit set or approved by the RCA
- 2.Extend advance warning signs towards on-coming traffic beyond any expected traffic queues
- 3.MTC with RP4/RP41 STOP/GO or RP4/RP42 STOP/SLOW paddle on road shoulder located between 1st and 2nd cone in the cone threshold closest to the working space
- 4. Minimum 5 cones in cone threshold at:
 - 2.5m centres less than 65km/h
 - 5m centres more than 65km/h
- 5.MTCs must show same message to oncoming traffic (eg STOP/STOP or GO/GO)
- 6.Refer to C10.2.3 MTC essentials for further information
- 7. When road users are passing the working space in alternating flow, all construction equipment must be stopped on same side of the road if there is no separation from the live lane
- 8. Where damage is likely to occur to passing traffic eg during sealing, traffic must be stopped in both directions
- 9.The T144 X0km/h AHEAD sign is optional

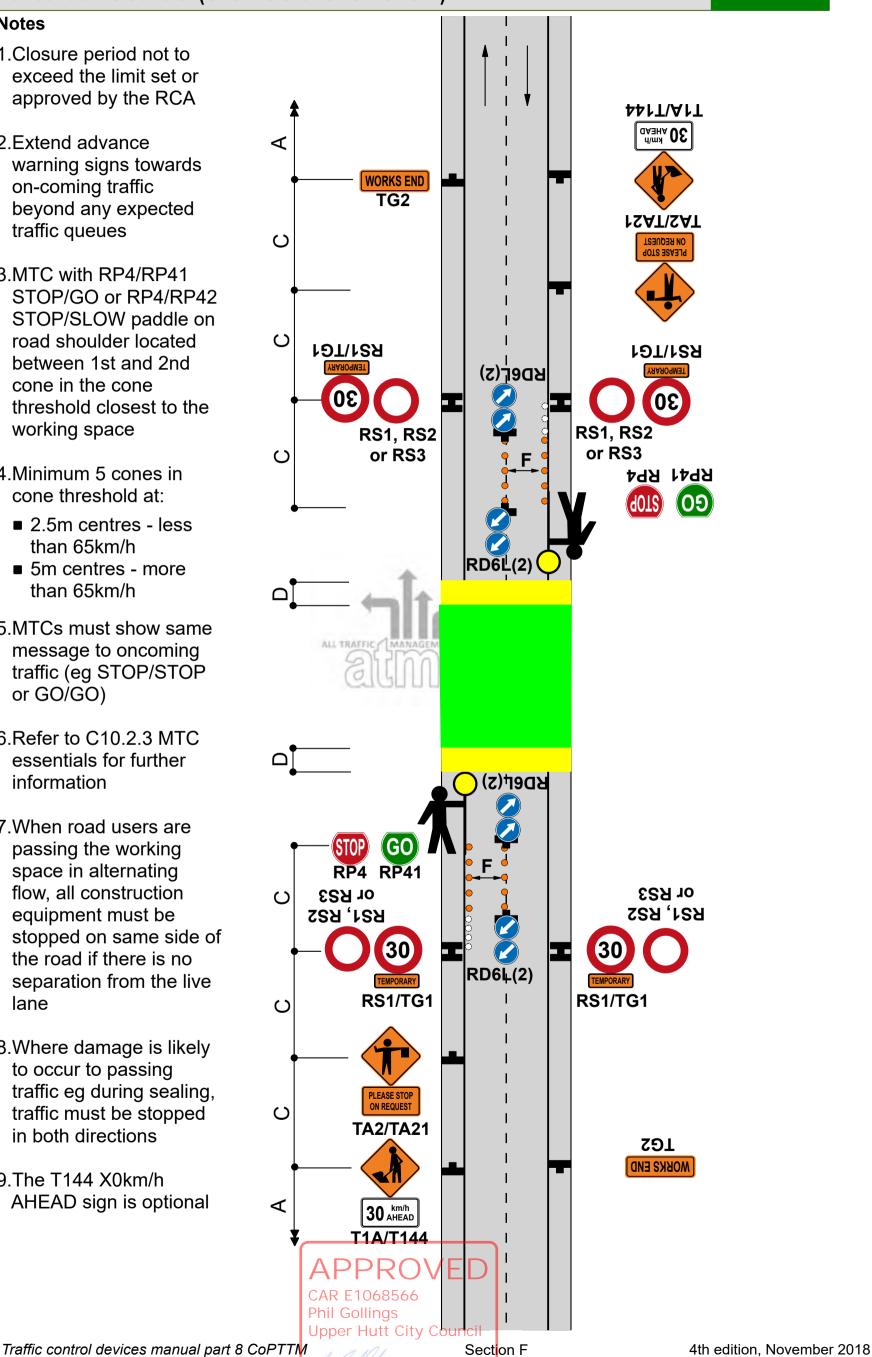


TMC APPROVAL REQUIRED FOR BOTH ATTENDED AND UNATTENDED SITES

TWO-WAY TWO-LANE ROAD Single-lane (traffic volume less than 1000vpd - 80vph) Give way control

F2.16 Level 1

Notes

- 1.The RP51/RP22 and RP52 controls must be placed in the following priority order:
 - downhill traffic must give way to uphill traffic
 - traffic that has to cross into the opposing lane gives way, however where visibility for this vehicle is marginal the contractor may require the other vehicle with better visibility to give way
- 2.Intervisibility is required as indicated on diagram. This means that a vehicle at one sign is able to see whether the way ahead is clear
- 3.A 30m return taper at the end of the closure is mandatory
- 4.Use PN11 No Stopping signs, if necessary
- 5.Cones are required on edge of the temporary lane opposite closure if road is not well defined
- 6.The T144 X0km/h
 AHEAD sign is optional

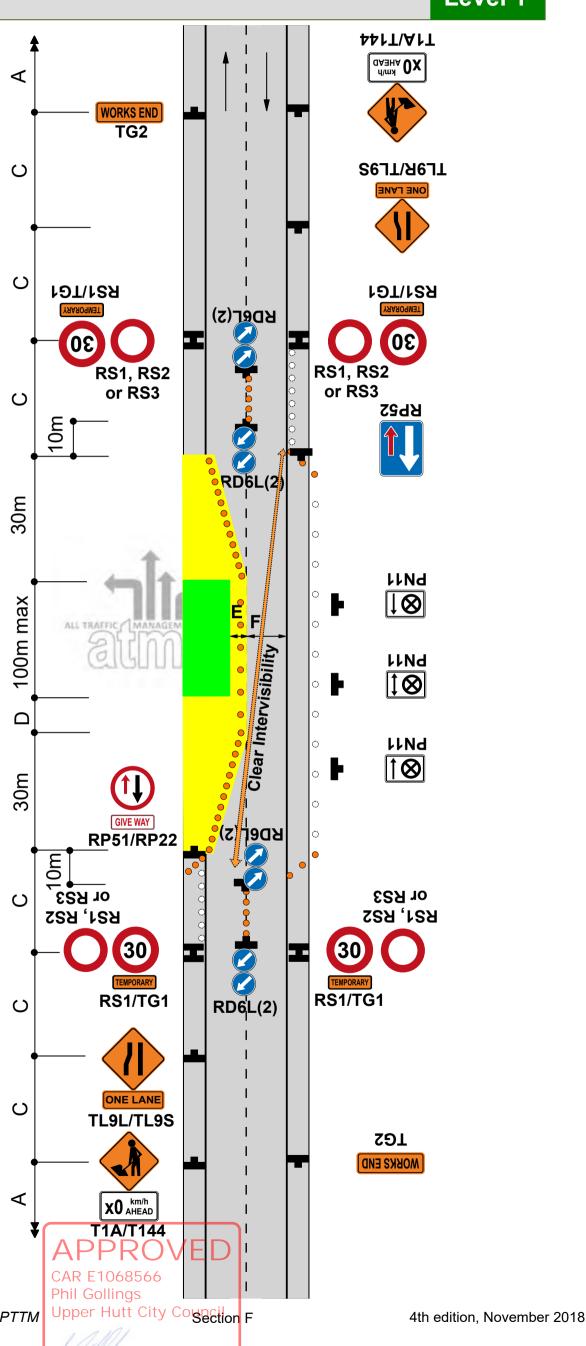

Traffic control devices manual part 8 CoPTTM

TMC APPROVAL REQUIRED FOR SENSORED TRAFFIC SIGNALS TO BE USED FOR ANY **UNATTENDED PERIOD**

TWO-WAY TWO-LANE ROAD Single-lane alternating flow Portable traffic signals


F2.17 Level 1

Notes

- 1. Provide details of make and model of portable traffic signals in the TMP
- 2.Install temporary limit lines (must be able to be removed upon completion) or use RP61/RP62 signs



- 3. Approved temporary speed humps may also be used. Consider use of MTC while speed humps are installed
- 4.A 30m return taper at the end of the closure is mandatory
- 5. Cones are required on edge of the temporary lane opposite closure if road is not well defined
- 6.Extend or place extra advance warning signs towards on-coming traffic beyond any expected traffic queues
- 7.Use PN11 No Stopping signs, if necessary
- 8.Minimum 5 cones in cone threshold at:
 - 2.5m centres less than 65km/h
 - 5m centres more than 65km/h
- 9.The T144 30km/h AHEAD sign is optional

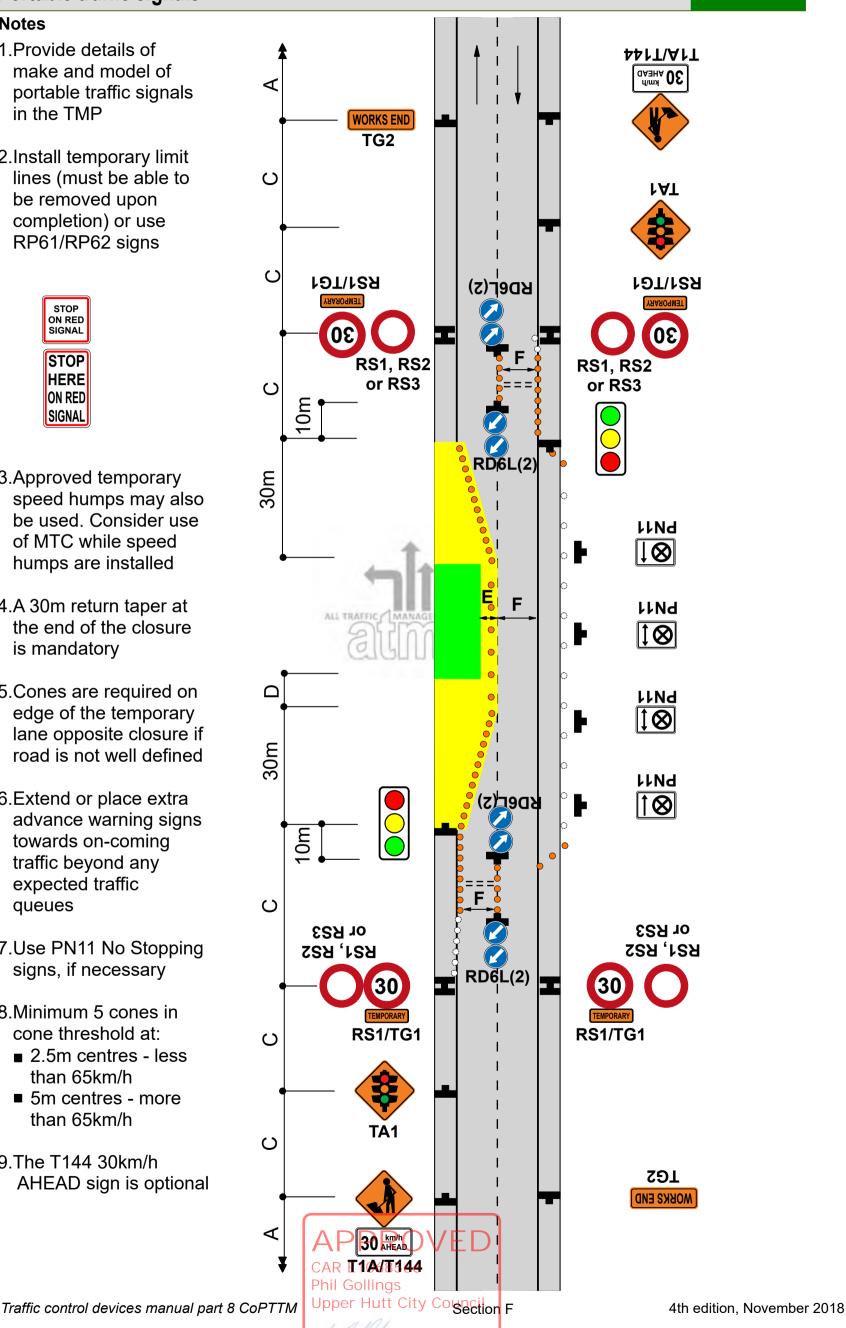

TWO-WAY TWO-LANE ROAD Work in centre of road

F2.18 Level 1

Notes


- 1.Cones are required on edge of the temporary lane opposite closure if road is not well defined
- 2.*Calculation of taper length for lateral shift of less than 3.5m is: $W \times G$

3.5

W = Width of lateral shift

G = Taper length in metres from the level 1 layout distance table

- 3.Use PN11 no stopping signs, if necessary
- 4.Use TSLs if required by TSL decision matrix
- 5.The T144 X0km/h AHEAD sign is optional

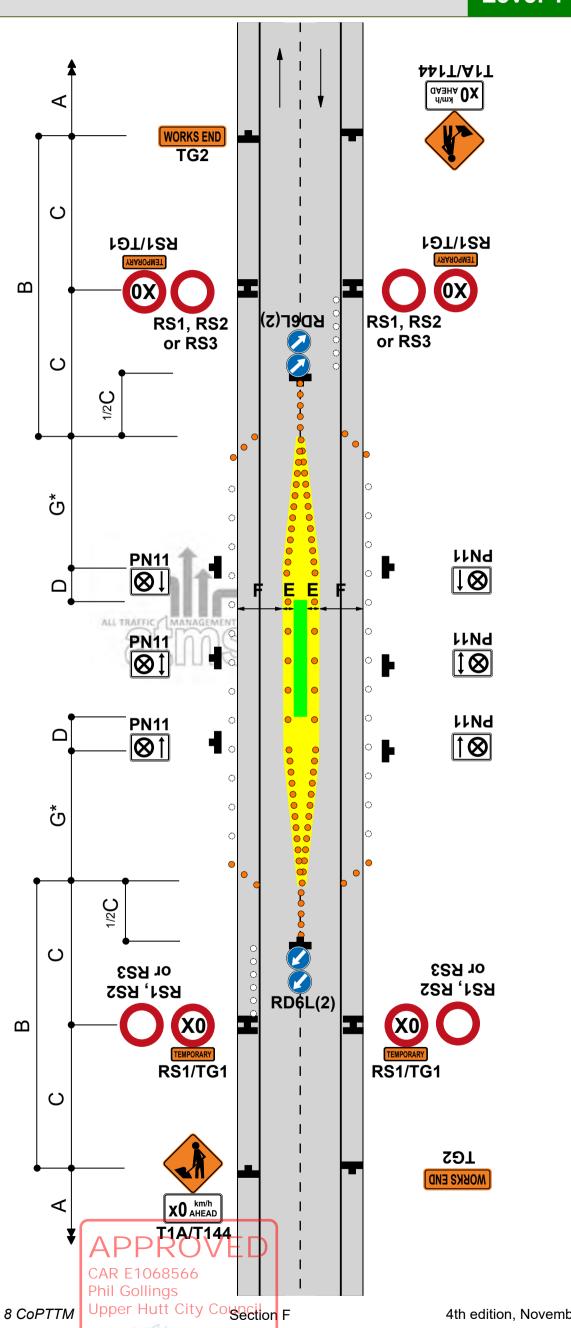


Traffic control devices manual part 8 CoPTTM

25 November 2024

4th edition, November 2018

TWO-WAY TWO-LANE ROAD - Intersection or roundabout Road works on side road after intersection - TSL on side road Traffic not crossing road centre

F2.19 Level 1

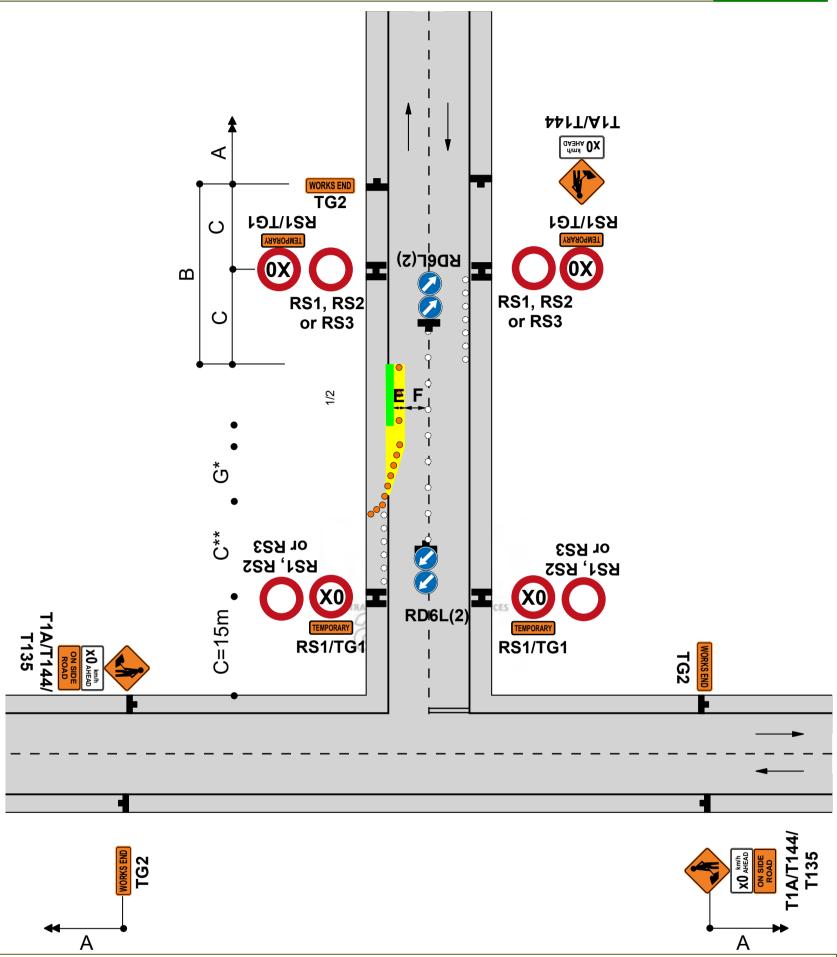

Notes

- 1. Sign spacing of TSL at the intersection can be reduced as per the table shown below
- 2. Where minimum dimensions cannot be achieved TMD F2.20 is to be used
- 3. Advance warning signs on main road must be at least the warning distance away from first cone in taper
- 4.*Calculation of taper length for lateral shift of less than 3.5m is:

W x G W = Width of lateral shift

- 3.5 G = Taper length in metres from the level 1 layout distance table
- 5.If traffic likely to cross the centreline, place cones on the centreline with RD6L signs at each end
- 6.Use TSLs as required by TSL decision matrix
- 7. The T144 30km/h AHEAD sign is optiona

			<u> </u>	
	Speed (PSL)	Intersection to TSL	TSL to taper	Total
	<50km/h	15m	15m	30m
FD	60km/h	15m	25m	40m
	>70km/h	15m	40m	55m
			<u> </u>	

Traffic control devices manual part 8 CoPTTM


Upper Hutt City Cousection F

4th edition, November 2018

CAR E1068566 Phil Gollings

TWO-WAY TWO-LANE ROAD - Intersection or roundabout Road works on side road after intersection - TSL on main road Traffic not crossing road centre

F2.20 Level 1

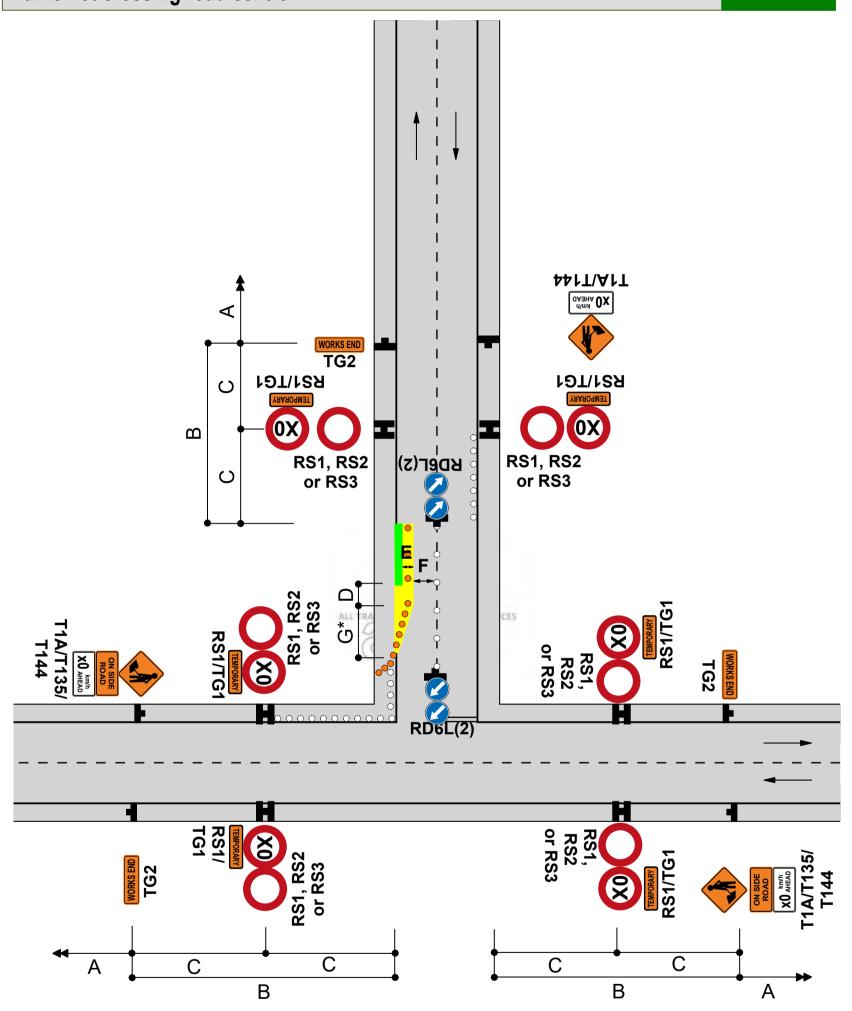

Notes

- 1.*Calculation of taper length for lateral shift of less than 3.5m is:
 - W x G W = Width of lateral shift
 - 3.5 G = Taper length in metres from the level 1 layout distance table
- 2.If traffic likely to cross the centreline, place cones on the centreline with RD6L signs at each end
- 3.Use TSLs as required by TSL decision matrix
- 4.The T144 X0km/h AHEAD sign is optional

APPROVED

CAR E1068566 Phil Gollings

Upper Hutt City Cousection F

4th edition, November 2018


Traffic control devices manual part 8 CoPTTM

ices NZ and is not be used without written permission of ATMS NZ This design is the property of All Traffic Management Ser

Static operations

TWO-WAY TWO-LANE ROAD - Intersection or roundabout Work in middle of intersection

F2.21 Level 1

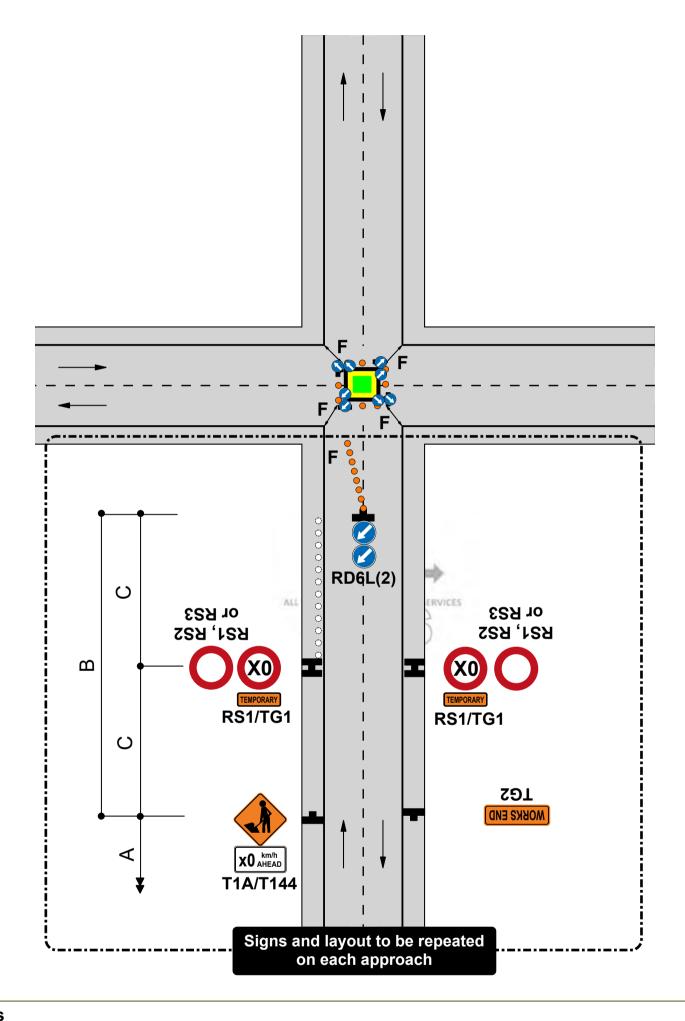

Notes

- 1. This diagram may be used at a T intersection by removing any one of the roads
- 2. Signs and layout shown in the box at the bottom of the diagram is to be repeated on each approach
- 3.RD6L signs are not required at an existing roundabout
- 4. Cone tapers are optional at existing roundabouts
- 5.Lane widths, F, may need to be increased to allow for turning movements of larger vehicles
- 6.Use TSLs if required by TSL decision matrix
- 7. The T144 X0km/h AHEAD sign is optional

CAR E1068566 hil Gollings

Traffic control devices manual part 8 CoPTTM

Upper Hutt City Cosection F


4th edition, November 2018

ONE-WAY TWO-LANE DIVIDED OR TWO-LANE ROAD Left-lane closure

F2.30 Level 1

Notes

- 1.Use TSLs if required by TSL decision matrix
- 2.On roads with a permanent speed limit of 100km/h, cones are required from the TSL to the taper if the speed is reduced by more than 30km/h
- 3.The T144 X0km/h AHEAD sign is optional

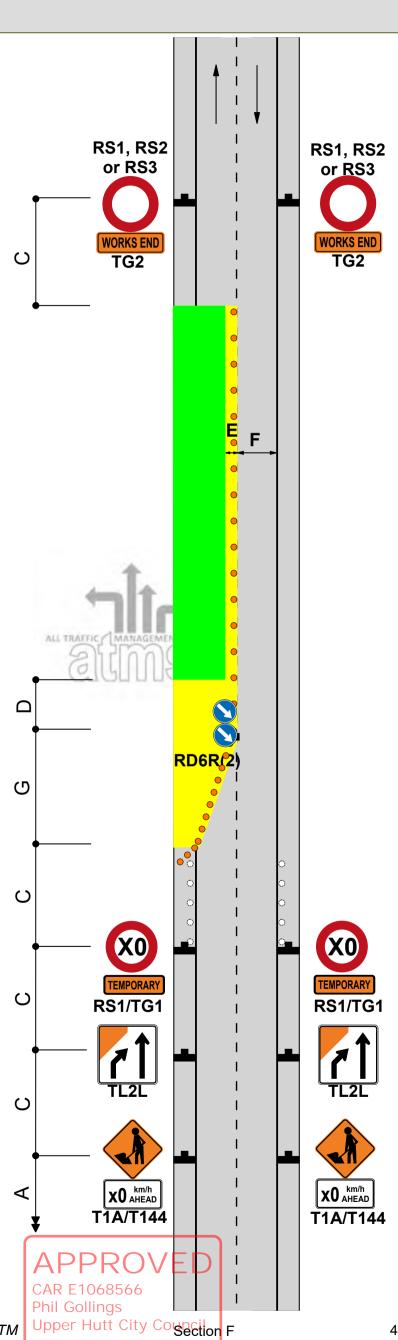

Traffic control devices manual part 8 CoPTTM


4th edition, November 2018

ONE-WAY TWO-LANE DIVIDED OR TWO-LANE ROAD Right-lane closure

F2.31 Level 1

Notes

- 1.Use TSLs if required by TSL decision matrix
- 2.On roads with a permanent speed limit of 100km/h, cones are required from the TSL to the taper if the speed is reduced by more than 30km/h
- 3.The T144 X0km/h AHEAD sign is optional

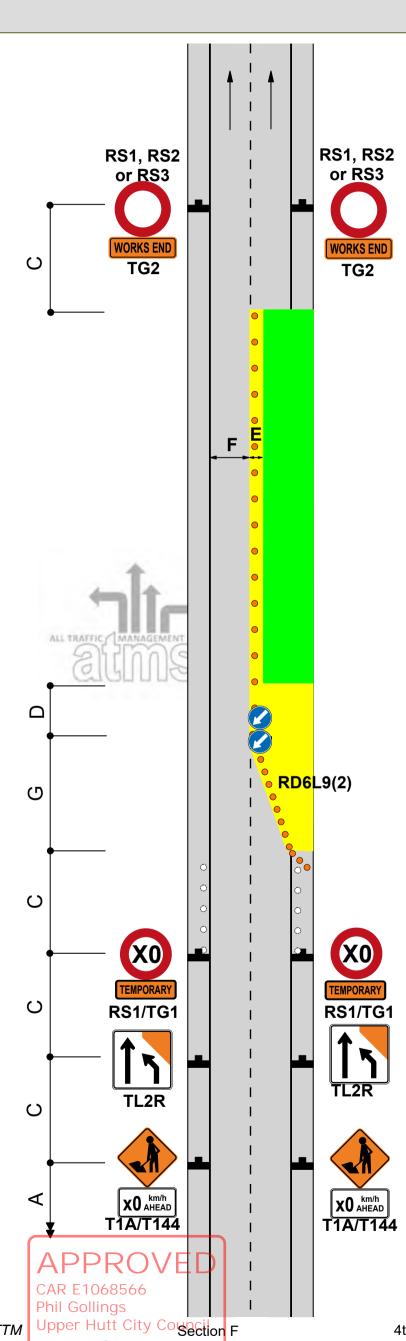


Traffic control devices manual part 8 CoPTTM

4th edition, November 2018




CC8 - Valve towards left of the lane

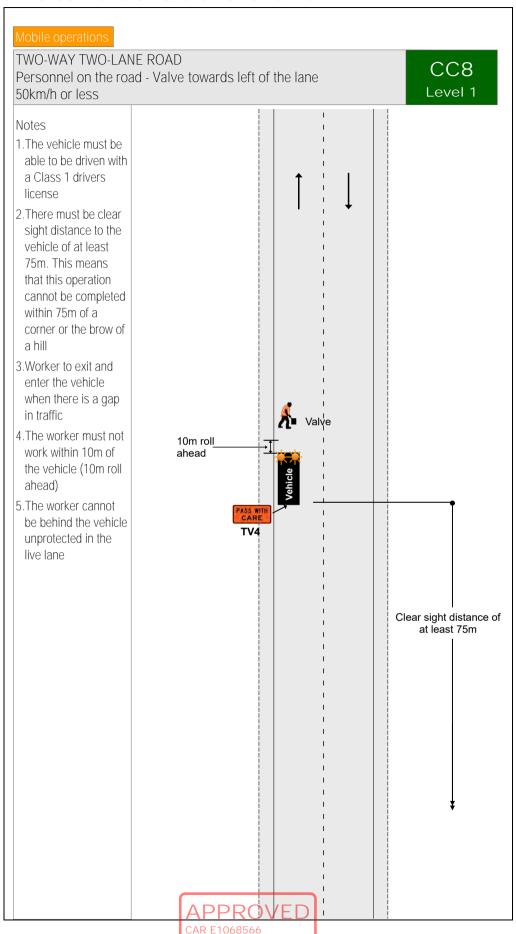




CC9 - Valve towards right of the lane

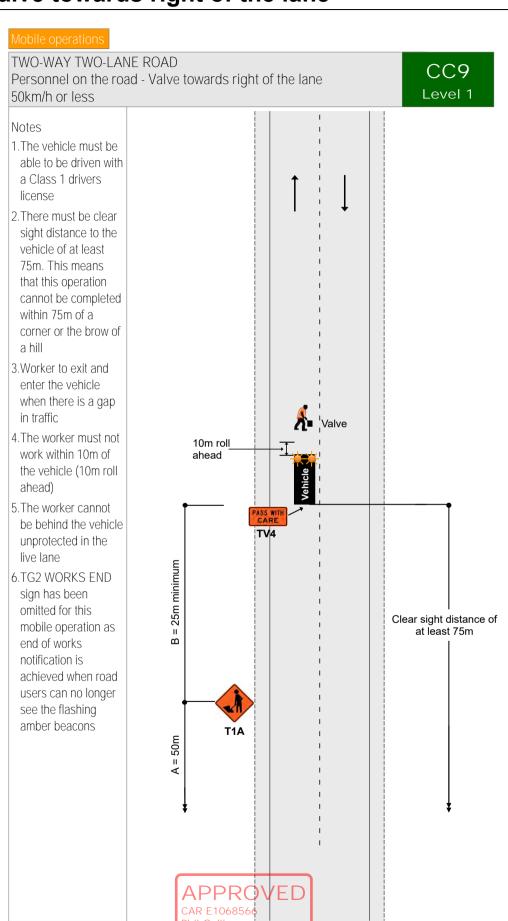




CC10 - Valve in centre of carriageway

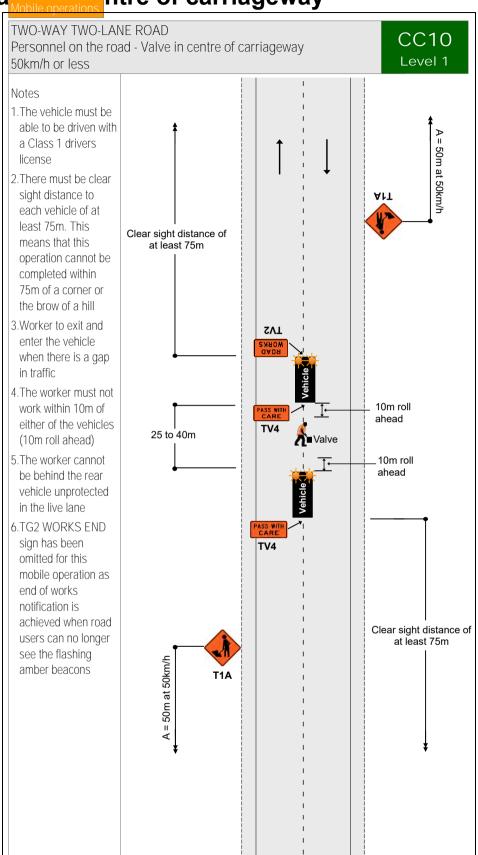






CC11 - Valve in centre of intersection

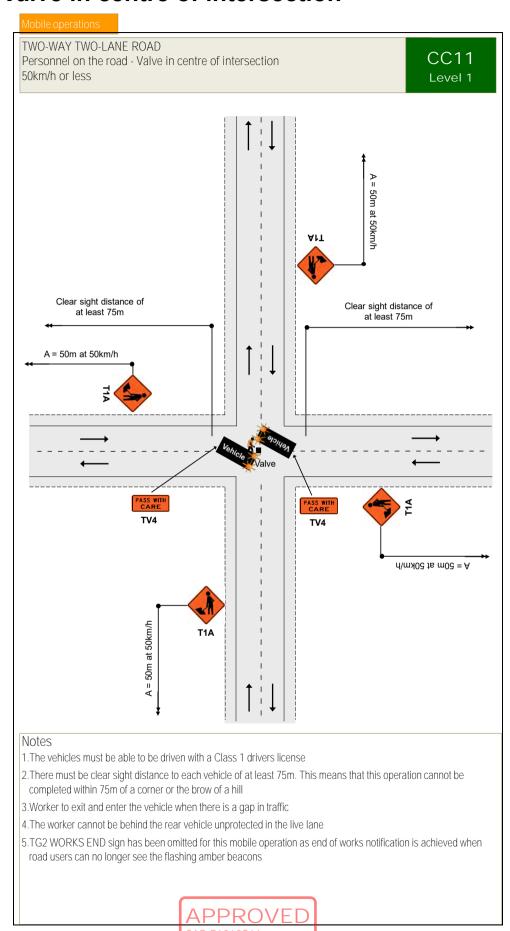




CC12 - Less than 75m CSD

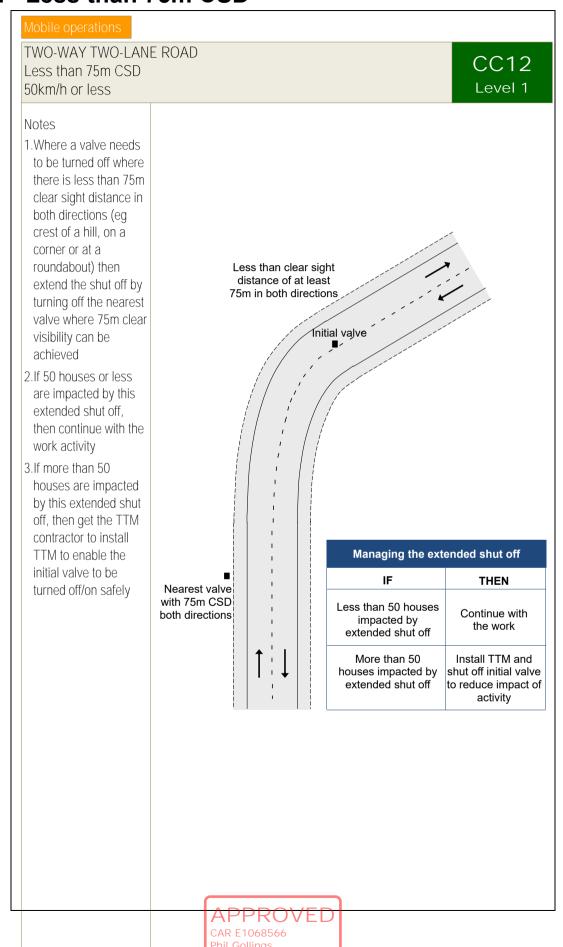

Traffic control devices manual part 8 CoPTTM

Section Epappendix Ay Traffic management plans

Edition 4, April 2020

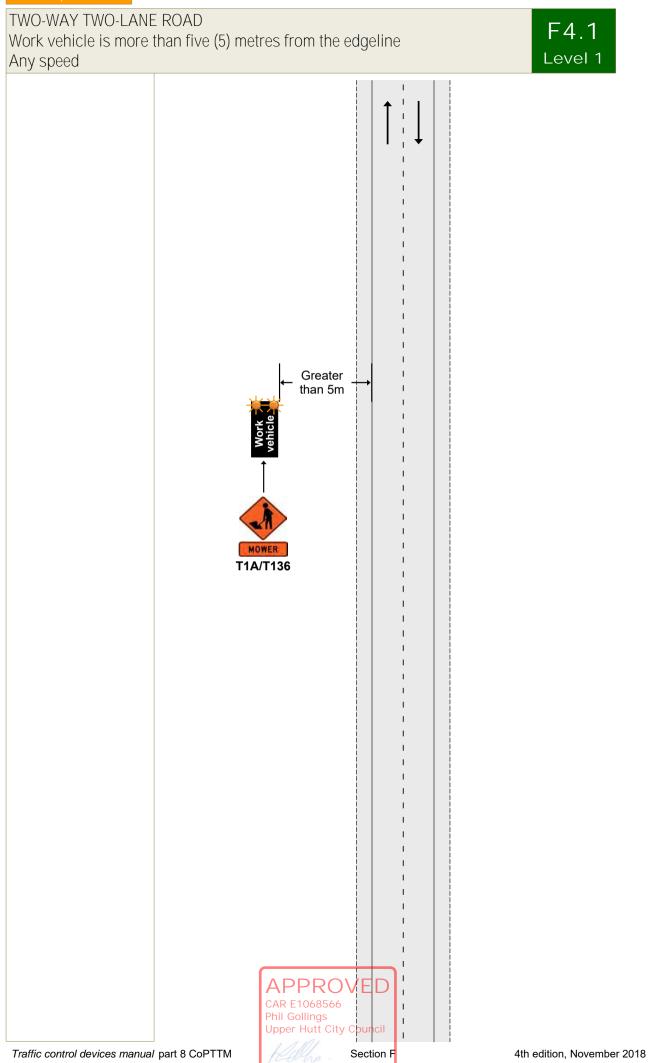


Mobile operations

TWO-WAY TWO-LANE ROAD Work vehicle is within five (5) metres of the edgeline CSD to work vehicle - not required under 65km/h, required over 65km/h

F4.2 Level 1

Notes

- 1.If permanent speed is under 65km/h, rear visibility to the work vehicle is not required
- 2.If permanent speed is over 65km/h, rear visibility to the work vehicle is required
- 3.A tail pilot vehicle equipped with T1A advance warning sign, appropriate supplementary plate and RD6R may replace the static signs if the permanent speed is under 65km/h (see TMD F4.3)

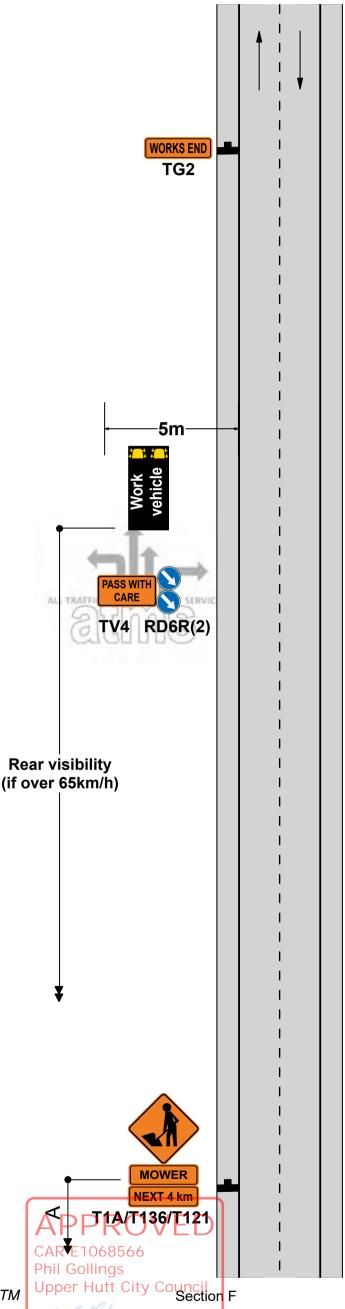

Traffic control devices manual part 8 CoPTTM

4th edition, November 2018


Mobile operations

TWO-WAY TWO-LANE ROAD Work vehicle is within five (5) metres of the edgeline Speed limit over 65km/h - the rear visibility is less than CSD

F4.3 Level 1

Notes

1.This TMD can replace TMD F4.2 when permanent speed is under 65km/h. In these situations, static signs are not required

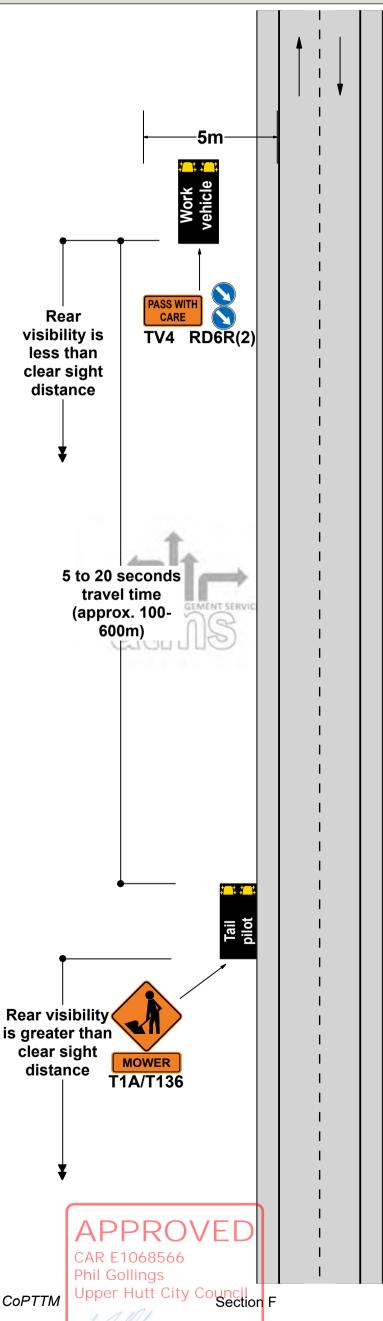

Traffic control devices manual part 8 CoPTTM

4th edition, November 2018


Mobile operations

TWO-WAY TWO-LANE ROAD Work vehicle is in a lane Permanent speed under 65km/h

F4.4 Level 1

Notes

- 1.Advance warning sign X may be replaced by tail pilot equipped with T1A advance warning sign and appropriate supplementary plate
- 2.In this case, signs marked with Y do not need to be erected
- 3.If using static advance warning signs and the operation is on the lane, then static advance warning signs must also be placed on any intersecting roads

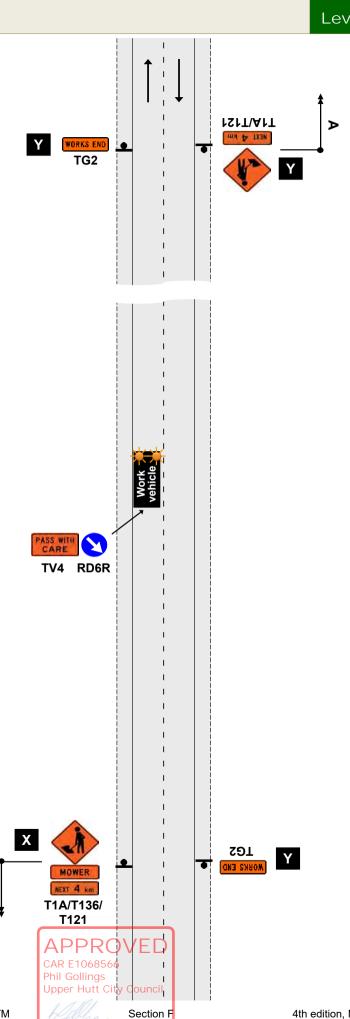

ATMS06

Level 1


Mobile operations


ONE-WAY TWO-LANE DIVIDED OR TWO-LANE ROAD Part or all of a lane occupied

Semi-static closure - work for up to 1 hour

Notes

- 1.Only use this TMD when activity can be completed within 1 hour (excluding set up and removal of worksite)
- 2.The T1A advance warning signs may be replaced by a tail pilot vehicle with a T1A sign, appropriate supplementary plate and a RD6R/L
- 3.If shadow vehicle is fitted with a TMA, the longitudinal safety zone (D) is not required
- 4.If using static advance warning signs and the operation is on the lane, then static advance warning signs must also be placed on any intersecting roads.
- 5. This site can be used on the opposite (left) lane also.

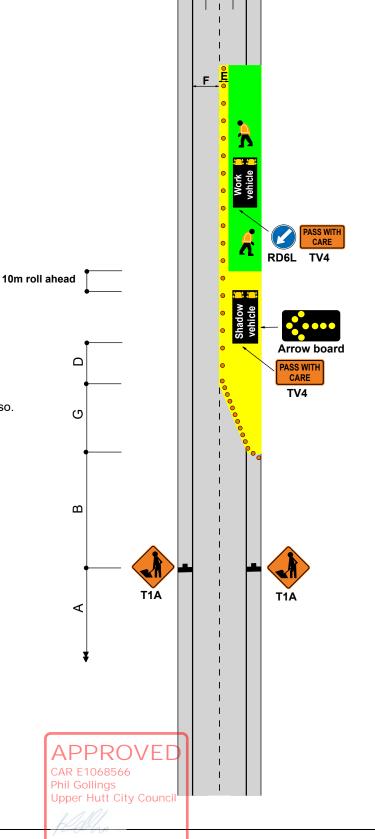

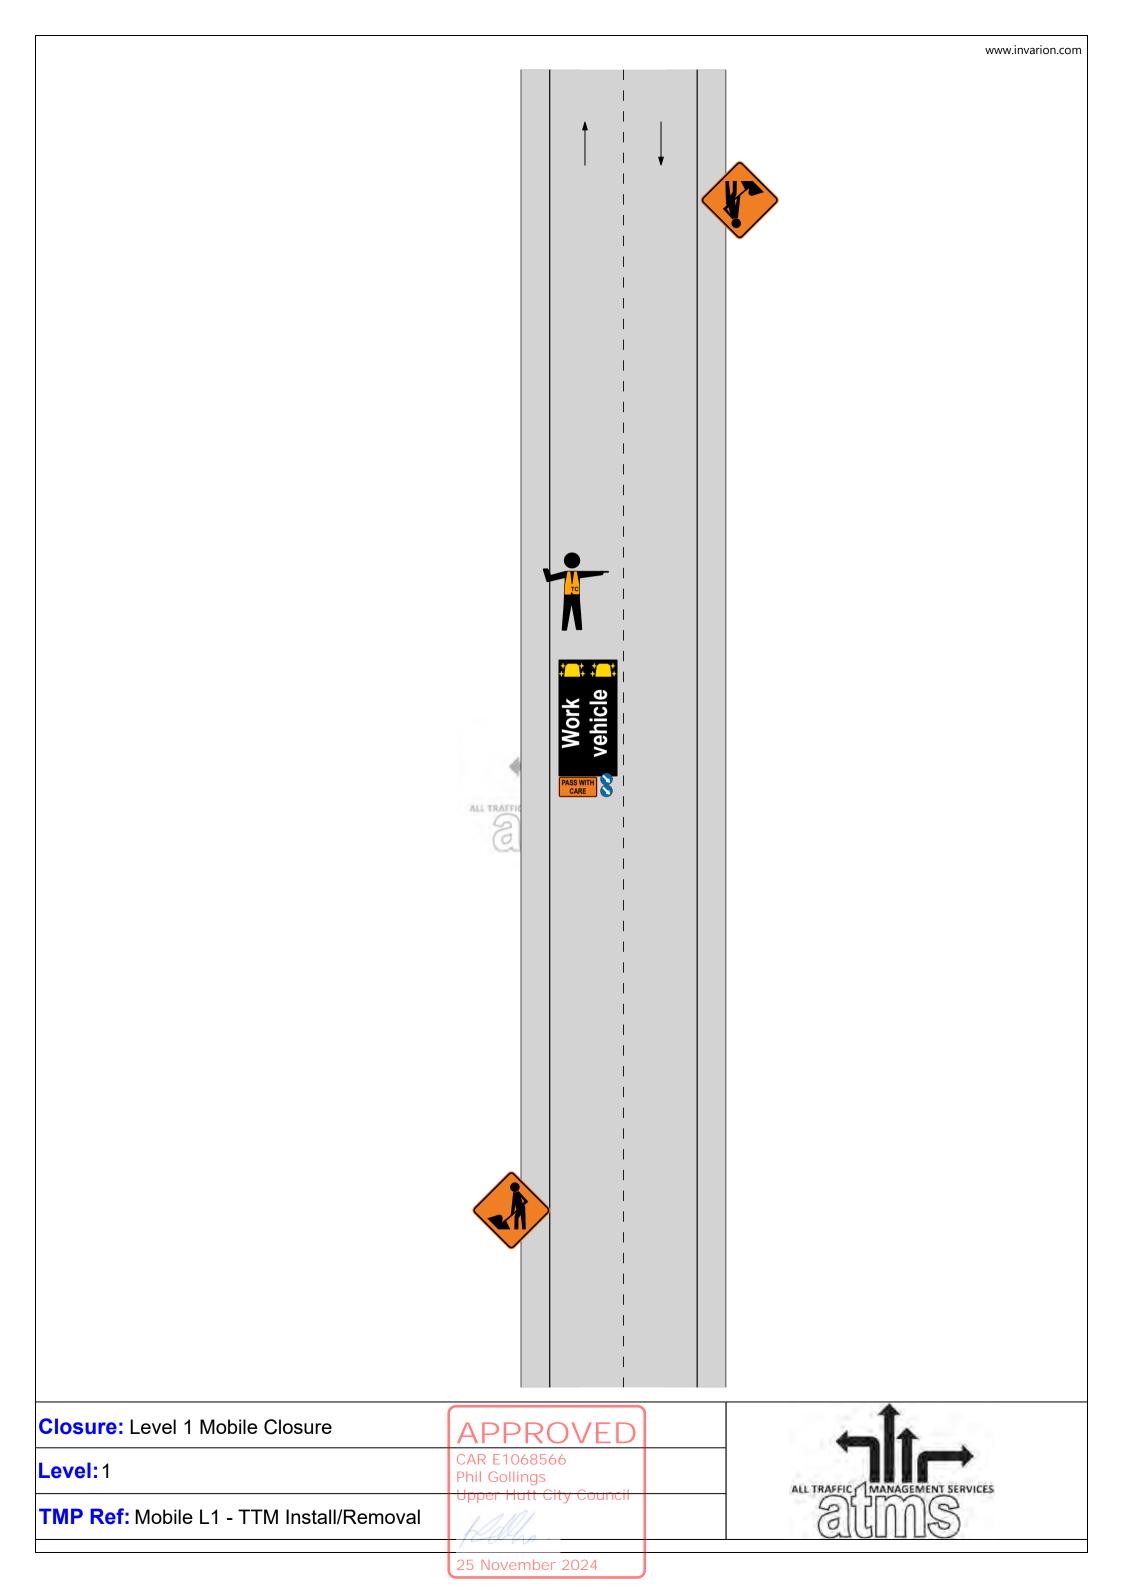

CYCLE LANE

Traffic not crossing road centre

Diverted cycle lane


Notes

- 1. Minimum cycle lane width must be:
 - 1m 50km/h or less
 - 1.5m 60km/h or more
- 2.A minimum cycle lane width of 1.5m is required if the temporary cycle lane is uphill
- 3.*Calculation of taper length for lateral shift of less than 3.5m is:

WxG

3.5

- W = Width of lateral shift
- G = Taper length in metres from the level 1 layout distance table
- 4.Use TSLs if required by TSL decision matrix
- 5.The T144 X0km/h AHEAD sign is optional

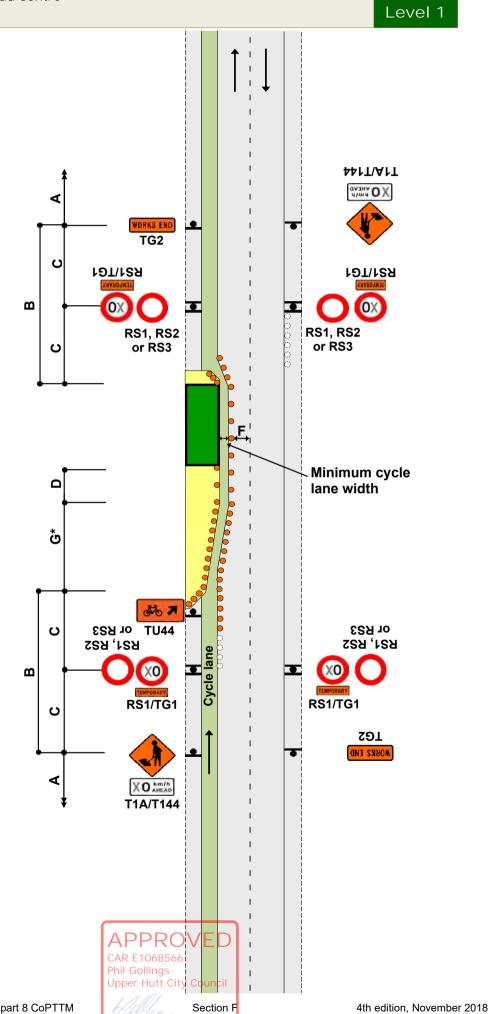

25 November 2024


F2.8

CYCLE LANE Traffic crossing road centre Diverted cycle lane - coned lane control

F2.9 Level 1

Notes

- 1.Minimum cycle lane width must be:
 - 1m 50km/h or less
 - 1.5m 60km/h or more
- 2.A minimum cycle lane width of 1.5m is required if the temporary cycle lane is uphill
- 3.*Calculation of taper length for lateral shift of less than 3.5m is: $W \times G$ 3.5 W = Width of lateral
 - shift
 - G = Taper length in metres from the level 1 layout distance table
- 4.To allow heavy vehicles to manoeuvre, cones in the channel must be offset by at least 10m where the direction changes. Refer C8.2.12
- 5.Use TSLs if required by TSL decision matrix
- 6.The T144 X0km/h AHEAD sign is optional

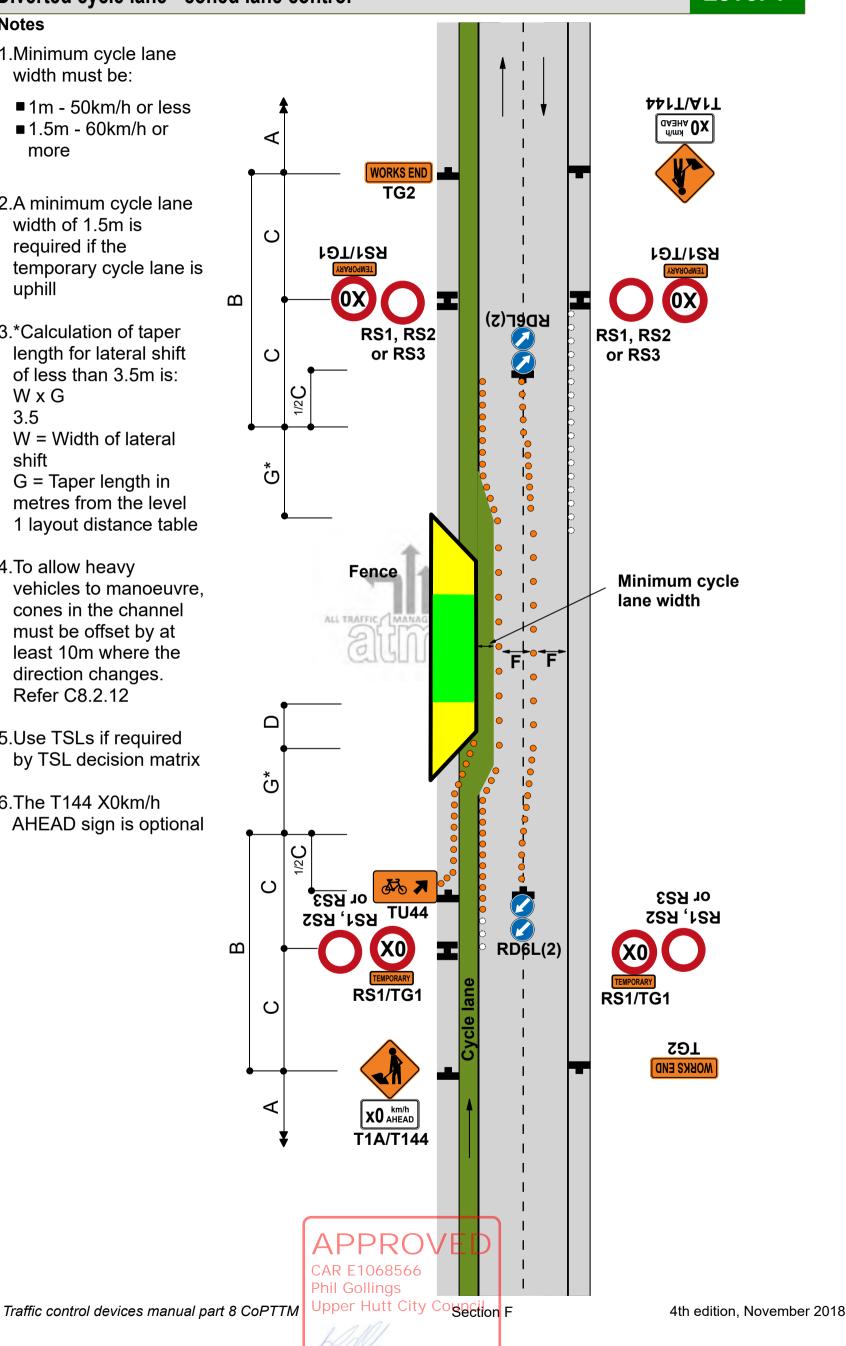

CYCLE LANE Cycle lane closed Poratable e-STOP

ATMS03 Level 1

Notes

- Merge of cycle lane
 with live lane must be
 delineated with cones at
 1.0m centres for at least 10m
- 2.The T144 30km/h
 AHEAD sign is optional on roads
 under 65km/h
- 3. Signs and layout shown in the box at the bottom of the diagram is to be repeated on each approach that requires cycle lane signage. ATMS01 or ATMS02 to be used on all non cycle lane approaches.
- 3. Provide details of make and model of portable traffic signals in the TMP
- 4.Use PN11 no stopping signs, if necessary as per the approved TMP
- 5.Install temporary RP61/RP62 signs. STOP NRED STOP HERE
- 7. Extend or place extra advance warning signs towards on-coming traffic beyond any expected traffic queues.

8.CONTINGENCY PLAN:


F2.14 or F2.22 to be implemented should issues arise with e-STOP/adverse weather conditions or where stop go is unsuitable. ex; Short term stoppages is defined as "stopping traffic for a short period of time within a static site, at inconsistent intervals to assist with the entry/exit of vehicles or small tasks required to be undertaken in the live lane".

 In circumstances where for safety reasons, the use of stop/go operations is deemed more appropriate, a site specific safe work method statement must be prepared.

10.e-STOP can only be used on an attended site. e-STOPs must be Amanned at all times.

CAR E1068566 Phil Gollings Upper Hutt City Counc Signs and layout to be repeated on each cycle lane approach follow ATMS01 & ATMS02 for non cycle lane approaches.

Level 1

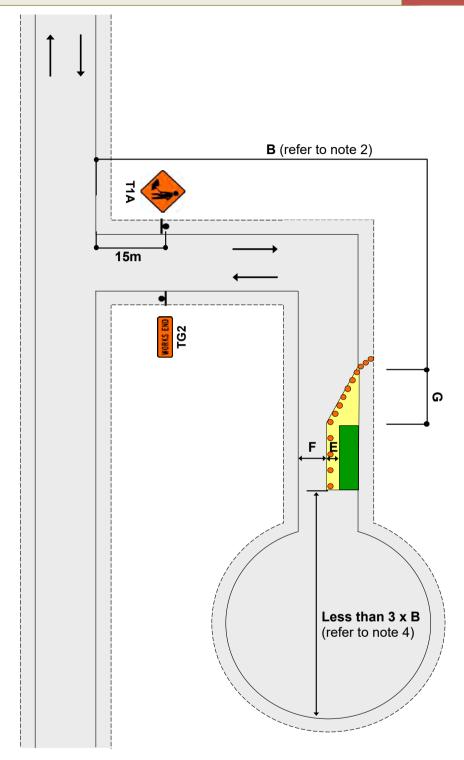


Notes

- 1. T1A sign to be placed at least 15m from the intersection
- 2. Where less than B, T1A/T135 and TG2 signs required on main road
- 3. Working space to be less than 100m
- 4. Signage is not required past the worksite where there is less than 3 x B from the end of the working space to the end of the road


TWO-WAY TWO-LANE ROAD - Intersection or roundabout Major obstruction close to intersection Allows shorter sign spacings and MTC operation

J2.19a

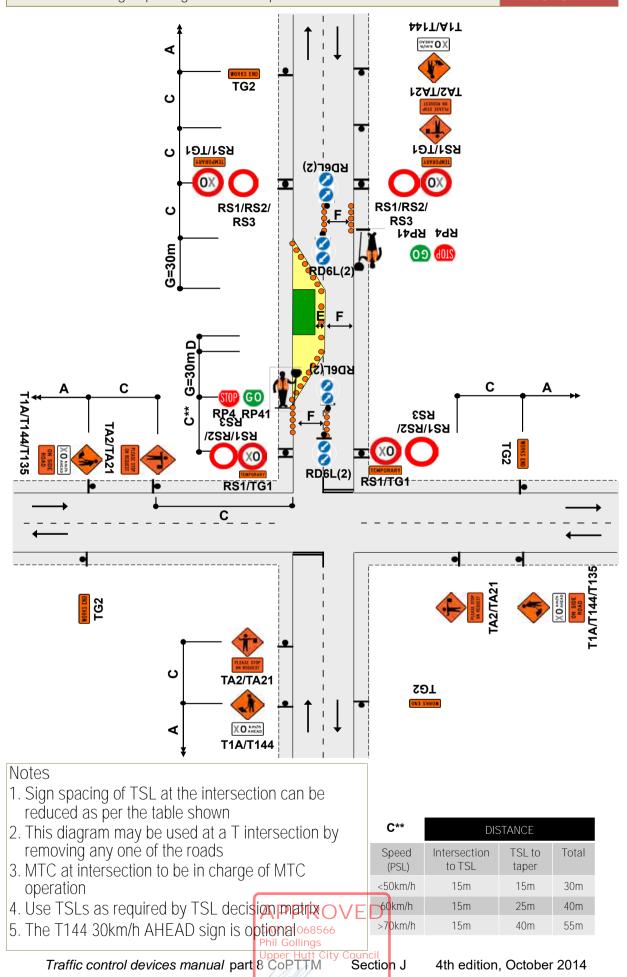

TWO-WAY TWO-LANE ROAD - Intersection or roundabout After intersection - Traffic not crossing road centre

J2.20a

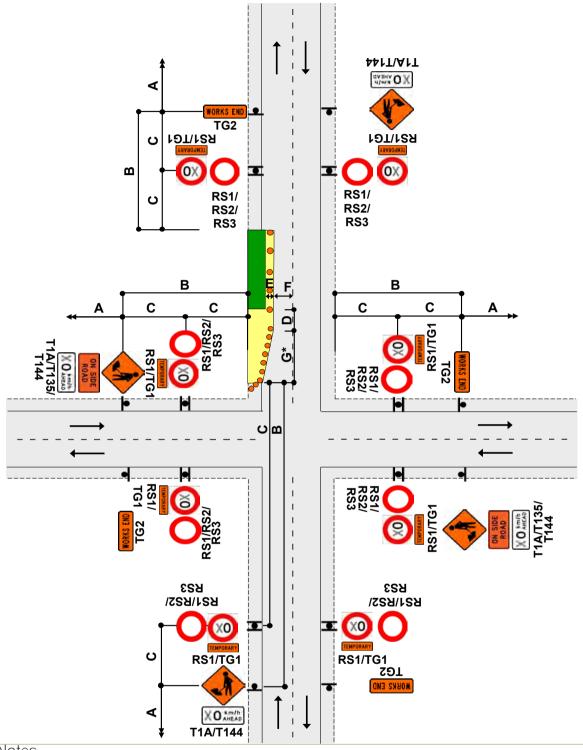

Notes

- 1. This diagram may be used at a T intersection by removing any one of the roads,
- 2. Taper length may be reduced by adding a RD6R sign
- 3. *Calculation of taper length for lateral shift of less than 3.5m is:

W x G 3.5

W = Width of Shoulder G = Taper length in metres from the level 1 layout distance table

25 November 2024

- 4. Use TSLs if required by TSL dedision matrix VED
- 5. The T144 X0km/h AHEAD sign is optional 8566

Traffic control devices manual part 8 CoPTTM


PTTM Section J

4th edition, October 2014

RD6R

TWO-WAY TWO-LANE ROAD - Intersection or roundabout After intersection - Traffic crossing road centre

J2.20b Level 1

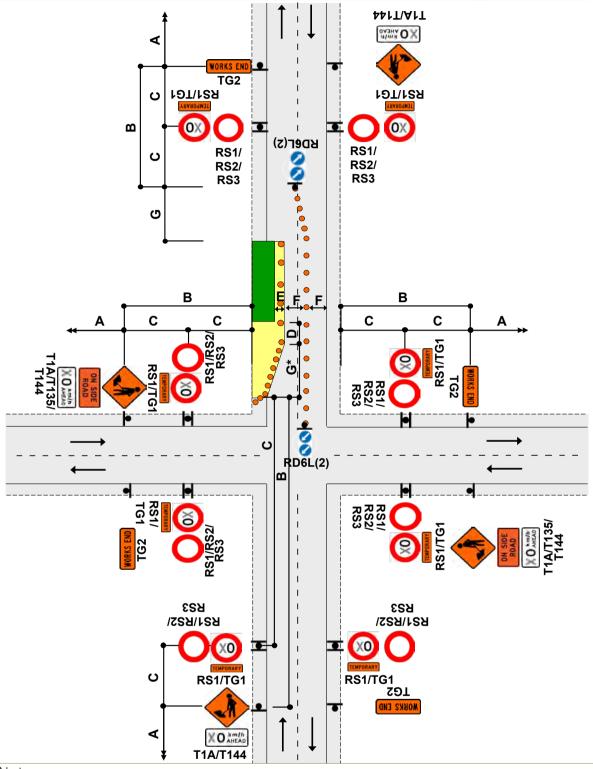

Notes

- 1. This diagram may be used at a T intersection by removing any one of the roads
- 2. Taper length may be reduced by adding a RD6R sign
- 3. *Calculation of taper length for lateral shift of less than 3.5m is:

$W \times G$ 3.5

4. Use TSLs if required by TSL decision Amatrix ROVED


- W = Width of Shoulder G = Taper length in metres from the level 1 layout distance table
- 5. The T144 X0km/h AHEAD sign is optional in the contract of t

Traffic control devices manual part 8 CoPTTM Section J 25 November 2024

RD6R

TWO-WAY TWO-LANE ROAD - Intersection or roundabout Before intersection - Traffic not crossing road centre

J2.20c

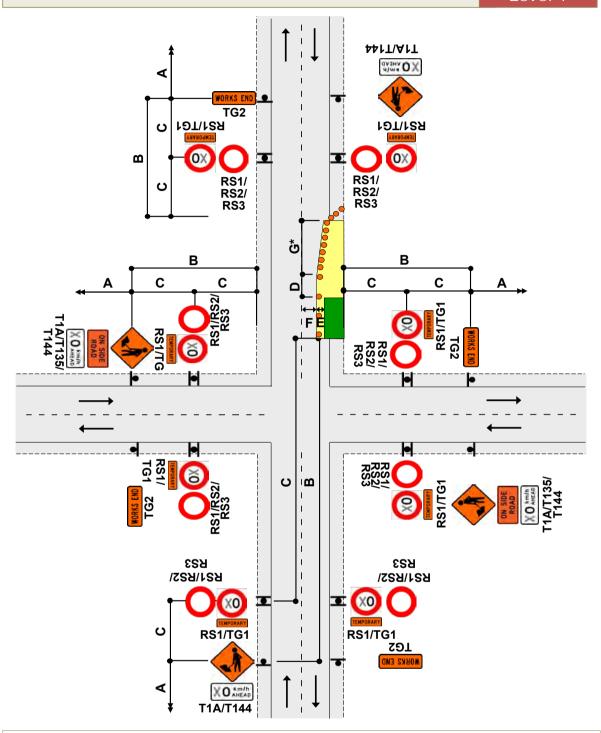


Notes

- 1. This diagram may be used at a T intersection by removing any one of the roads
- 2. Taper length may be reduced by adding a RD6R sign
- 3. *Calculation of taper length for lateral shift of less than 3.5m is:




 $W = Width \ of \ Shoulder \quad G = Taper \ length \ in \ metres \ from \ the \ level \ 1 \ layout \ distance \ table$

- 4. Use TSLs if required by TSL decision matrix
- 5. The T144 X0km/h AHEAD sign is optional—



RD6R

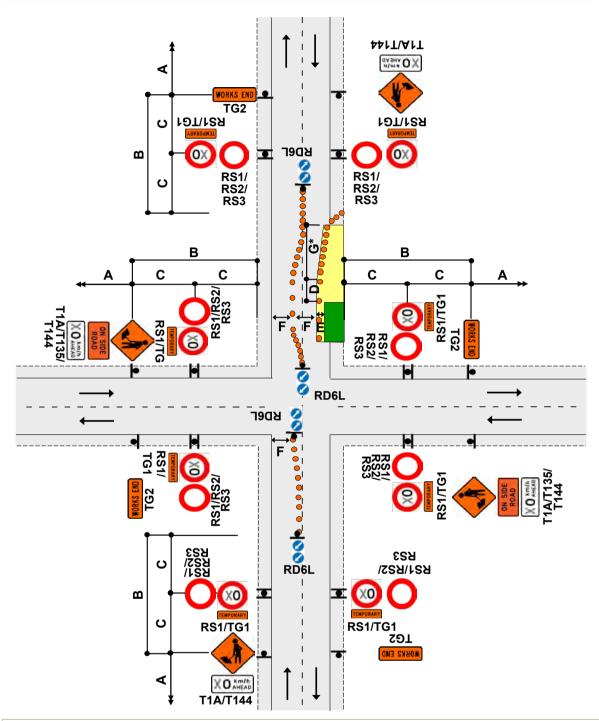

Notes


- 1. This diagram may be used at a T intersection by removing any one of the roads
- 2. *Calculation of taper length for lateral shift of less than 3.5m is:

$W \times G$

3.5

W = Width of lane G = Taper length in metres from the level 1 layout distance table

- 3. Install shifting taper to move road users into the new alignment
- 4. Use TSLs if required by TSL decision matrix
- 5. The T144 X0km/h AHEAD sign is optional 1068566

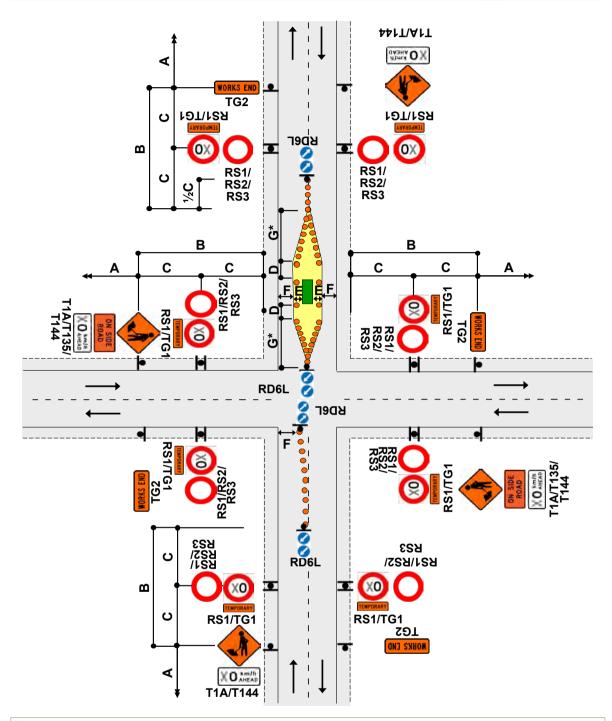

Notes

- 1. This diagram may be used at a T intersection by removing any one of the roads
- 2. *Calculation of taper length for lateral shift of less than 3.5m is:

W x G

3.5

W = Width of lane G = Taper length in metres from the level 1 layout distance table

- 3. Install shifting taper to move road users into the new alignment
- 4. Use TSLs if required by TSL decision matrix
- 5. The T144 X0km/h AHEAD sign is optional
